



SCHEDULE HELP TOPICS

PLANNING, SCHEDULING & RISK

INEIGHT 

Information in this document is subject to change without notice. Companies, names and data used in examples are fictitious.

Copyright ©2025 by InEight. All rights reserved. No part of this document may be reproduced or transmitted in any form or by any means, electronic or mechanical, for any purpose, without the express permission of InEight.

Microsoft Windows, Internet Explorer and Microsoft Excel are registered trademarks of Microsoft Corporation.

Although InEight Schedule has undergone extensive testing, InEight makes no warranty or representation, either express or implied, with respect to this software or documentation, its quality, performance, merchantability, or fitness for purpose. As a result, this software and documentation are licensed “as is”, and you, the licensee are assuming the entire risk as to its quality and performance. In no event will InEight be liable for direct, indirect, special, incidental or consequential damages arising out of the use or inability to use the software or documentation.

Release 25.1
Last Updated: 14 February 2025

CONTENTS

LESSON 1 – SCHEDULE OVERVIEW	11
Overview of the Schedule And Risk Process	11
Plan View	12
Markup View	14
Schedule Review View	15
Cost Risk View	16
Short Interval Planning View	17
Risk Register View	17
LESSON 2 – USER ACCESS	21
Schedule Navigation	21
Main Menu	21
Open Schedule from Main Menu	21
User Setup and Roles	23
Schedule Roles	23
Schedule Creator	23
Project Member	24
Administrator	24
Knowledge Library Administrator	24
User Creation	25
Create a New User	25
Schedule Contributor Setup	28
Schedule Contributors	28
Contributor Role Types	28
Markup	29
Short Interval Planner	29
Scheduler	29
Selecting Project Contributors	29

LESSON 3 – USER INTERFACE	31
Project List View	31
Schedule folders	33
Schedule type	35
Locked Columns	37
Show/Hide Logic, WBS	40
Annotations	40
Schedule Critique Overview	43
Toggle Schedule Critique Annotations On / Off:	43
Missing Predecessor or Successor	44
Builder Menus	45
Column set builder menu	45
Query builder menu	46
Sort builder menu	47
Group by builder menu	48
View builder menu	50
Hide No Results	51
LESSON 3 – KNOWLEDGE LIBRARY	52
Knowledge Base	52
Resources in the Knowledge Base	52
CPM Schedule	53
Activity Productivity Rates	54
Knowledge Tags	55
Calendars	56
Register	57
Categories	60
Machine learning	63
Set Up Resources	64
Import/Export	67
Site Administration	69
General Settings	70
Users	70
LESSON 4 – PROJECT CREATION	71
Import a Schedule	71
Importing a schedule	71
Export a Schedule	73
Exporting a schedule	73

Create a Schedule from Scratch	74
Details	74
Context	76
Outline	76
Schedule Configuration Settings	79
Schedule Configuration	80
General	81
Contributors	81
Knowledge Tags	82
Calendars	82
Resources	83
SIP Resources	85
Project Suite	86
Print View	86
Page Setup options	87
Gantt Setup options	92
Save to PDF	97
LESSON 5 – PACKAGES AND ACTIVITIES	101
Activity Productivity Rates	101
Set the productivity factor	101
Using the Productivity Rate Calculator	103
Using the Knowledge Base Suggested Rates	106
Calculate Productivity Rates	108
Create Activities	109
Knowledge subnets	109
Building a schedule	110
Activities from Scratch	111
Build Activities from Scratch	112
WBS summary activity type	113
Change Activity Type	114
Change Activity Type	114
Bulk Activities from Scratch	116
Create Activities in Bulk	117
Assign Knowledge Tags	118
Assigning Knowledge Tags in the Iris	118
Assigning Logic	120
Using the Gantt Chart to Assign Logic	120
Planning Mode	122
Create a new planning package	122

Bulk creation of planning packages	125
Advanced Work Packaging	127
Unlink a Project Suite project	130
Schedule Configuration	130
LESSON 6 – RESOURCE MANAGEMENT	131
Project Resources	131
Import resources from Knowledge Base Resource register into Project	
Resources Register	132
Resource Assignments	134
Assign Resources at the Activity Level	134
Fill Down	138
Fill Down from the summary level	138
Resource Histogram	143
Generate a Resource Histogram	144
Filtering by Resource	149
Histogram Comparison Mode	149
Export Assignments	153
Project Specific Resources: Project Configuration Setup	154
Create a project-specific resource via the Resource Assignment window	155
Create a Project Specific Resource via the Resource Assignment	
Window	156
Resource histogram view	156
Enable the Resource Histogram View	157
Add statuses to the Resource histogram	159
S-curve	161
Enable the S-curve	161
Actual status enabled with S-curve	163
Over-allocation	164
Enable the Over-allocation	165
Stacked histogram	165
Enable the Stacked Histogram	166
Changing the stacked histogram colors	168
Edit Stacked Histogram Colors	168
Burn Rate	169
Enable the Burn rate	169
Excel Export	171
Export from Histogram	172
Import into the Schedule	173

LESSON 7 – SCHEDULING	175
Scheduling Overview	175
Scheduling	175
Setting Schedule Progress Attributes	175
Critical Path - Driving Indicator	180
Progressing	181
Percent Complete	183
Adding % Complete columns to the Gantt Chart	188
Snapshot And Schedule Settings	189
Set Snapshot	189
Set the Snapshot	190
Scheduling	191
Data Date	193
Schedule Mode (Planning vs. Scheduling Mode)	194
Auto CPM	195
Auto Progress	195
Baseline/Snapshot	195
Active baseline	198
Create a snapshot	199
Create a snapshot	199
Overwrite a snapshot	200
Overwrite a snapshot	201
Analysis View template	201
Analysis View template	201
View snapshots in the Gantt Chart	203
View snapshots	204
Variance Columns	204
Promote to Schedule	205
Promote to Schedule	206
Project list view	206
Integrations	208
LESSON 8 – SCHEDULE MARKUP PROCESS	209
Markup Process Overview	209
Assigning Markup	209
Initiating the Review Cycle	210
Marking up the Schedule	211
Reviewing Markup	211
Initiating the Review Cycle	212
Opening the View Cycle	212

Register Threshold	214
Team Member Markup	215
Export Options	215
Start/Stop a Review Cycle	216
Generate a Review Cycle	216
Marking Up the Schedule	218
Uncertainty	218
Scorecard Values	220
Marking Up the Schedule via the scorecard	221
LESSON 9 – SCHEDULE REVIEW PROCESS - RISK OVERVIEW	225
Review And Risk Process Overview	225
Import/Export	231
Add Register Event	231
Filter	232
Matrix Definition	232
P-Value Overview	233
Markup Feedback and Consensus	234
Inference Engine (AI)	235
Human Intelligence (HI)	235
Risk Intelligence (RI)	236
Custom	237
Multiple User Feedback	237
Distribution Options	239
Uncertainty Status	240
Risk Histogram	241
Tornado Analysis	242
Cost Item Mode	243
Root node in Cost Risk	244
Risk Mode	245
LESSON 9 – COST RISK	246
Cost Risk Overview	246
Import Cost Risk Items	248
Step by Step – Import Cost Risk Items	250
Estimate Cost Risk Export	253
Control Cost Risk Export	253
LESSON 10 – SHORT INTERVAL PLANNING	257
SIP Overview	257

Process Overview	257
Planning Steps/Tasks	257
Milestones	258
Resources	258
SIP General Navigation	259
Short Interval Planning View	259
Toolbar - Icons, Functions, Settings	260
LESSON 11 – REGISTER ITEMS	267
	267
Organizational Register Items	267
Events Register	267
Register Types	268
Import and Export	270
Add Register Event	271
Filter	272
Matrix Definition	272
Project Register Events	273
Event Types	273
Events Library	274
Create an Event	274
Risk Range Scoring	276
Assign Register Items	277
Assign a Register Item	277
11.1 INEIGHT SCHEDULE WORKFLOWS	279
InEight Schedule - Focused Workflow	279
Scheduling & Short Interval Planning Workflow	281
Scheduling Business Process Workflow	281
11.2 SCHEDULE FREQUENTLY ASKED QUESTIONS	282

This page intentionally left blank.

LESSON 1 – SCHEDULE OVERVIEW


OVERVIEW OF THE SCHEDULE AND RISK PROCESS

InEight Schedule is a (CPM) Critical Path Method planning and risk management tool. It provides multiple tools to support planning and risk management throughout the lifecycle of a project.

Schedule contains six primary schedule views: Plan, Markup, Schedule Review, Cost Risk, Short Interval Planning, and Risk Register. These views correspond to different processes of the Scheduling ecosystem:


Project View	Description
Plan	Create, detail, and plan out the CPM schedule.
Markup	Assess, critique, and provide feedback on the planned CPM schedule.
Schedule Review	Consolidate markups, conduct risk analysis, and update the CPM Schedule based on review.
Cost Risk	Consolidate markups, conduct risk analysis, and update cost based on review.
Short Interval Planning	Conduct short interval planning, detailing daily work for crews and short term plan to get the CPM Activities done.
Risk Register	Risk Matrix tracking all project events surfaced throughout the planning, markup, review, and execution phases of the Project Schedule.

To access each view, open a schedule and go to the menu bar at the top left of the screen.

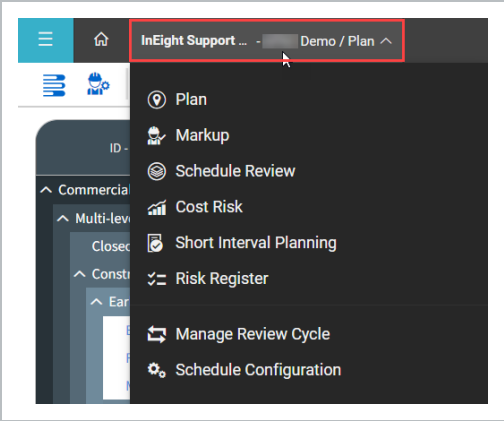

PLAN VIEW

When you open a schedule, you land on the project’s Plan view. In this view, you can see the schedule details (such as activities, work package groupings, dates, duration, and float) where you can create, detail and plan out the CPM schedule.

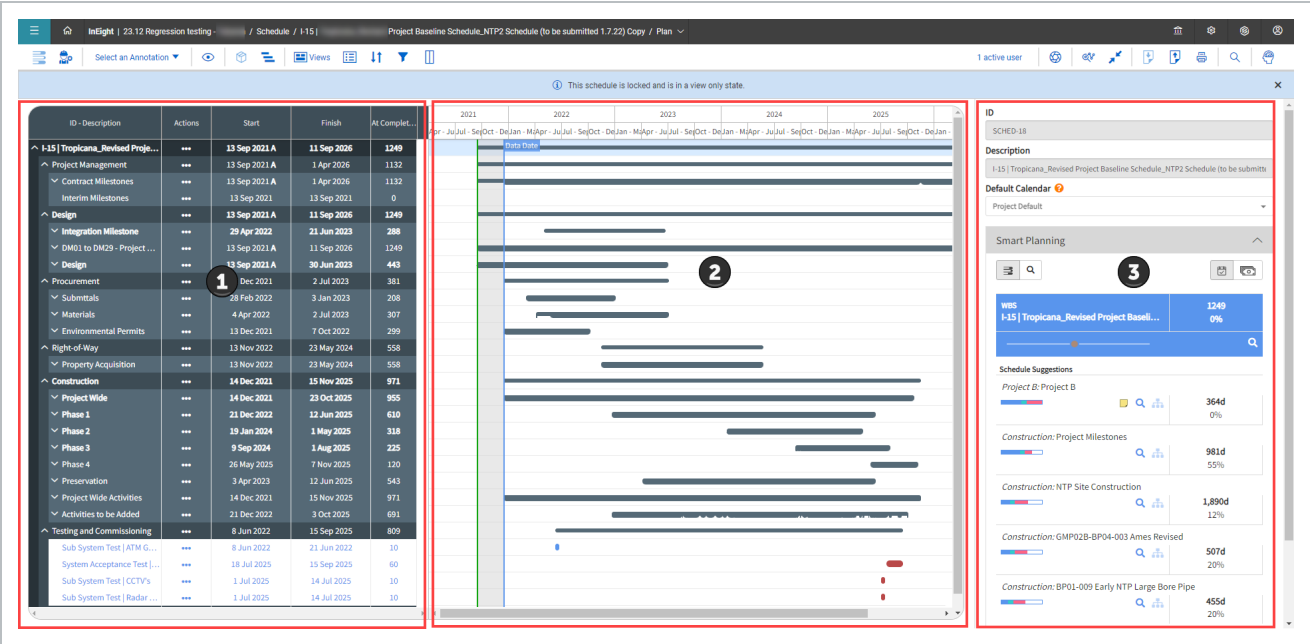

- 1 Contains customizable Gantt chart columns providing a summary view of schedule details including, but not limited to, activity/work package description, dates, durations, float, and cost.
- 2 This Gantt chart provides a visual layout of scheduled activities, work packages, and


milestones over time. The Gantt chart also has integrated functionality allowing users to adjust dates, schedule logic, and schedule critiques.


- 3
- The Iris contains the fine details of the schedule. Activities, work packages, and milestones that can be detailed out with specific constraints, tags, resources, reviewers, short interval planners, and events. Additionally, the Iris also houses the Smart Planning AI functionality which references and pulls in Knowledge Base information into project work packages and activities.


NOTE


You can [import](#) or [export](#) a schedule in Plan view.

Gantt chart legend


Vertical Bar Type	Description
Project start 	The planned or actual project start dates

Data date 	The point in time when the status of the schedule is recorded
---	---


Project finish 	The planned or actual project finish dates
---	--

Horizontal Bar Type	Description
Dark grey 	WBS

Light grey 	Completed activity
---	--------------------

Black outline, white center 	Planning package
--	------------------


Orange 	Baseline activity
---	-------------------

Green 	LOE
--	-----

Horizontal Bar Type	Description
Blue	Non-critical activity
Red	Critical activity

MARKUP VIEW

The Markup view is where project contributors assigned to activities and work packages can provide feedback on the current planned schedule. You can also assess, critique, and provide feedback on the planned CPM schedule.

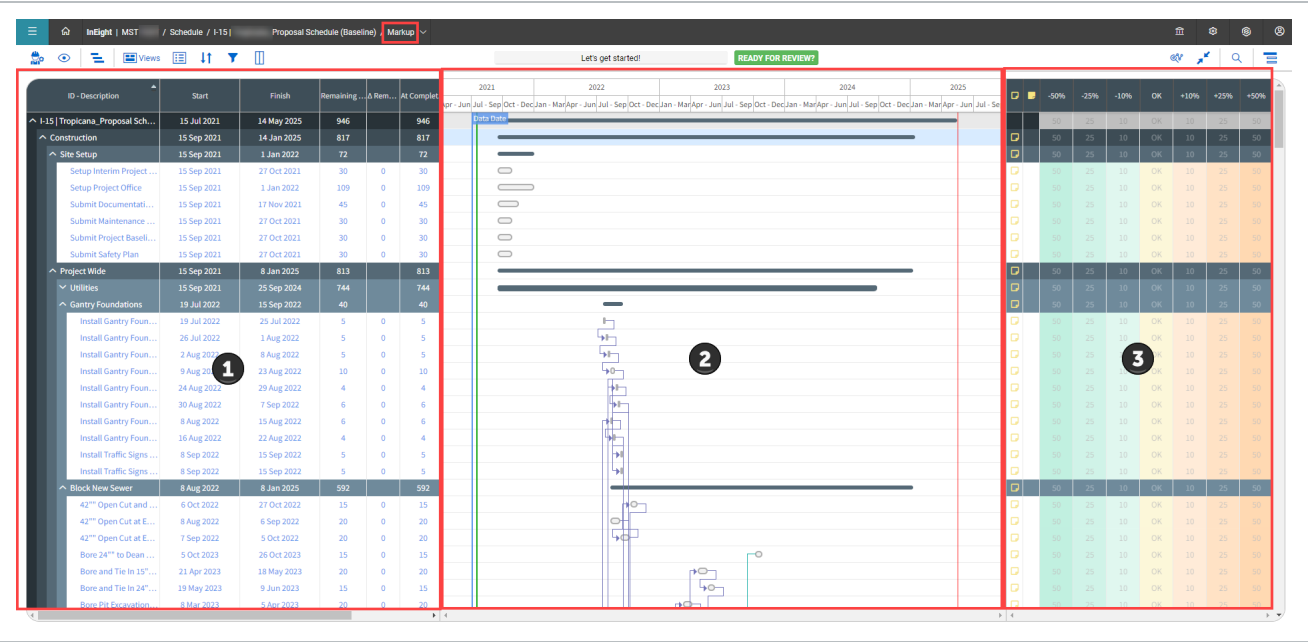


- 1 Gantt chart columns contain activity metadata: ID-description, dates, remaining duration, total duration, delta [change in] remaining duration, delta [change in] end date, and completed [markup status].
- 2 This Gantt chart provides a visual layout of how the schedule would be affected by the markups provided.
- 3 This section contains the markup score card. The score card is a quick way for project contributors to increase, decrease, or confirm the dates and durations for the schedule items assigned. Additionally, project events (such as risks, opportunities, and ideas) can be provided as feedback by contributors.

SCHEDULE REVIEW VIEW

Project View	Description
Schedule Review	Consolidate markups, conduct risk analysis, and update the CPM Schedule based on review

After the project contributors have finished providing their markups, the Review view is where all the feedback is consolidated. Schedulers can take the information and can begin to conduct risk analysis on the schedule, adjust durations, and associate risk events.

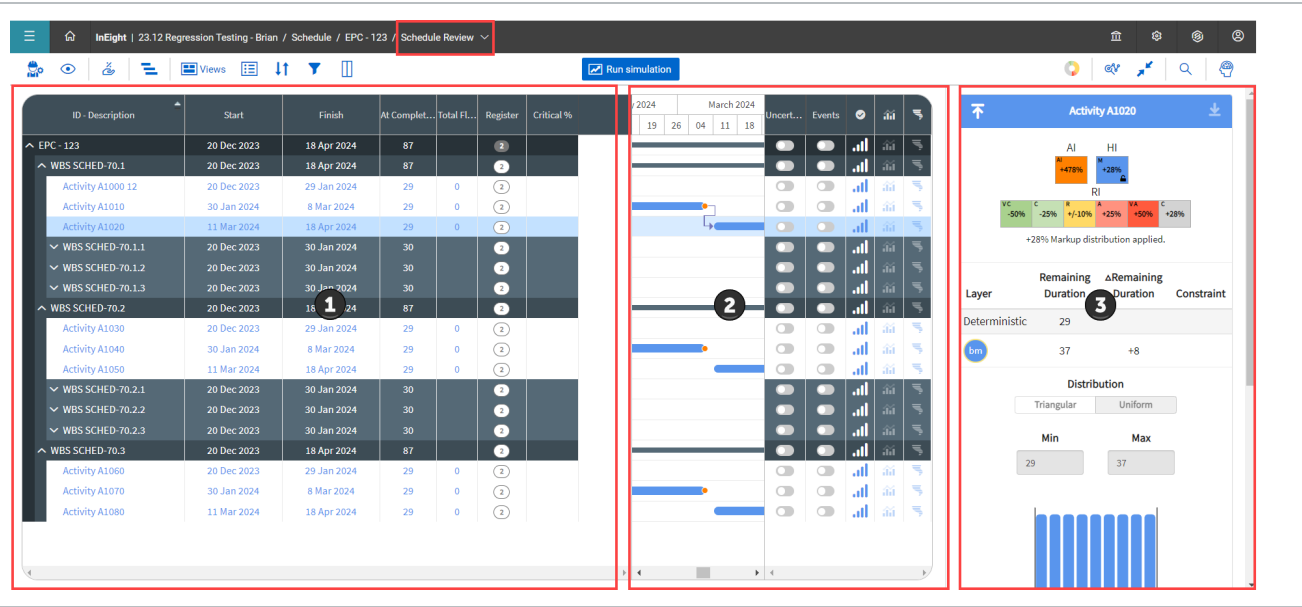

- 1 Gantt chart columns show the original start and finish dates but can have the uncertainty and events from the markups switched on and off to show the changes and impacts to the schedule.
- 2 This Gantt chart provides a visual layout using bars that adjust dependent upon the uncertainty and risk applied. In the right-most columns of the Gantt chart are the icons to access the risk histogram and tornado charts.
- 3 The Iris in this view shows details regarding the markups provided, giving a quick glance at the distribution data from multiple contributor markups. Additionally, the Inference Engine, Human Intelligence, and Risk Intelligence data are housed here to aid in the review process.

With the feedback provided, users can adjust the schedule to reflect the appropriate markups and/or conduct risk analysis with the uncertainty and various events provided.

COST RISK VIEW

Project View	Description
Cost Risk	Consolidate markups, conduct risk analysis, and update cost based on review

The Cost Risk view is where all the feedback is gathered and consolidated for cost items. When you bring in your cost structure, you can begin to conduct risk analysis on the budget using uncertainty and risk events.

The screenshot shows the InEight Cost Risk View interface. The top navigation bar includes 'InEight | 23.12 Regression testing', 'Schedule /', 'MPP Import /', and 'Cost Risk'. Below the navigation bar is a toolbar with icons for Views, Run simulation, and other functions. The main content area is divided into three sections:


- Table Section (Left):** A table with columns: ID, Description, Actions, Exclude, by Cost %, Max Cost, and Max Cost %. The table lists various activities and milestones, such as 'Start Milestone A1700', 'Activity A1670', 'Activity A1730', 'Finish Milestone A1720', 'Activity A1670', 'Activity A1750', 'Start Milestone A1700', 'Activity A1670', 'Activity A1740', 'Activity A1730', 'Activity A1740', 'Finish Milestone A1720', 'Activity A1680', 'Activity A1680', 'Activity A1690', and 'Activity A1690'. The 'by Cost %' column shows 100% for all items. The 'Max Cost' column shows \$0 for all items. The 'Max Cost %' column shows 100% for all items. Callout 1 points to the 'by Cost %' column.
- Uncertainty and Events Section (Middle):** A table with columns: Uncertainty, Events, Register, and a set of icons. Callout 2 points to the 'Events' column.
- WBS Sum Act Panel (Right):** A panel titled 'WBS Sum Act' with input fields for Min (\$), Likely (\$), and Max (\$). Below these fields is a histogram showing a distribution. Callout 3 points to the histogram.

- Columns for Cost Item information that shows actual, remaining, and totals of items prior to simulations with the option to display risk adjusted amounts based on user selection.
- Provides toggles to turn on or off uncertainty or events and view events assigned to cost items. Users can also view the risk histogram and tornado chart post simulation runs.
- The details are shown regarding markups provided, giving a quick glance at the distribution data. With the feedback provided, users can conduct risk analysis with the uncertainty and various events provided.

SHORT INTERVAL PLANNING VIEW

Project View	Description
Short Interval Planning	Conduct short interval planning, detailing daily work for crews and short term plan to get the CPM Activities done

In the Short Interval Planning view, schedulers and field execution planners can plan out their day to day work. CPM activities brought in from the Planning view can be broken down into steps and tracked for progress. Crews can be established with specific production rates and goals.

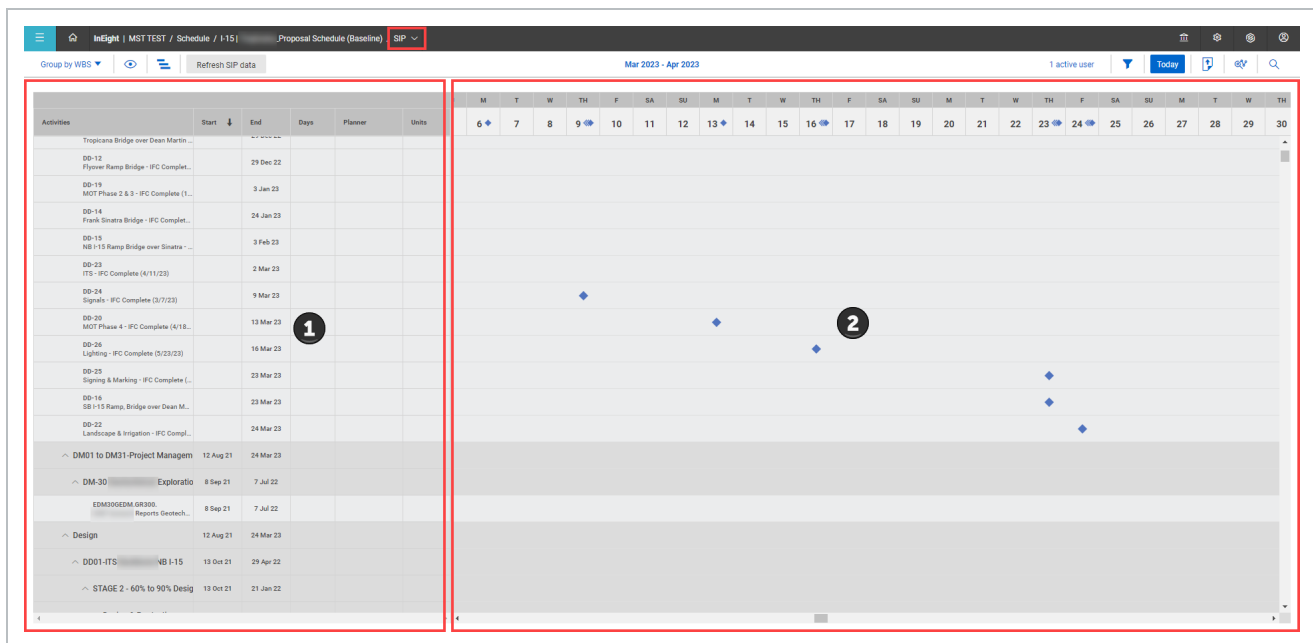


- 1 Contains all work packages, activities, and steps listed with dates and durations.
- 2 This visual represents how steps and crew activity are spread out over the coming weeks. Additionally, the original CPM dates have duration bars shown so users can visually see when steps to complete an activity vary from the baseline CPM schedule dates.

RISK REGISTER VIEW

Project View	Description
Risk Register	Risk matrix tracking all project events surfaced throughout the planning, markup, review, and execution phases of the project schedule

The Risk Register is where the schedule’s risk events, matrix settings, uncertainty values are stored and set.




- The Project Register Events tab summarizes all events on the project. Events can be selected and deselected and edited in this register.

The screenshot displays the 'PROJECT REGISTER EVENTS' tab. It features a table with the following columns: Active, Event Id, Title, Type, Description, %, Dur, \$, Score, Risk Own..., Mitigation, Status, Markup, Schedule, Cost, Publish, and an icon column. Two rows are visible:

Active	Event Id	Title	Type	Description	%	Dur	\$	Score	Risk Own...	Mitigation	Status	Markup	Schedule	Cost	Publish	Icon
<input checked="" type="checkbox"/>	R1	Rapid river water	Threat	crane on a barge!	Extremely Low	Very Low (≤ 40d)	Very Low (≤ \$50K)	1	Garl...	Bring the crane	Mitigated		1			
<input checked="" type="checkbox"/>	O1	Rent equipment for 50% off	Opportunity	overbought!	Ultra Low (5%)	Ultra Low (≤ 7d)	Ultra Low (≤ \$...)	1	Garl...		Unmitigated					

The Microsoft Excel import tool lets you import new or updated register events and their activity associations.

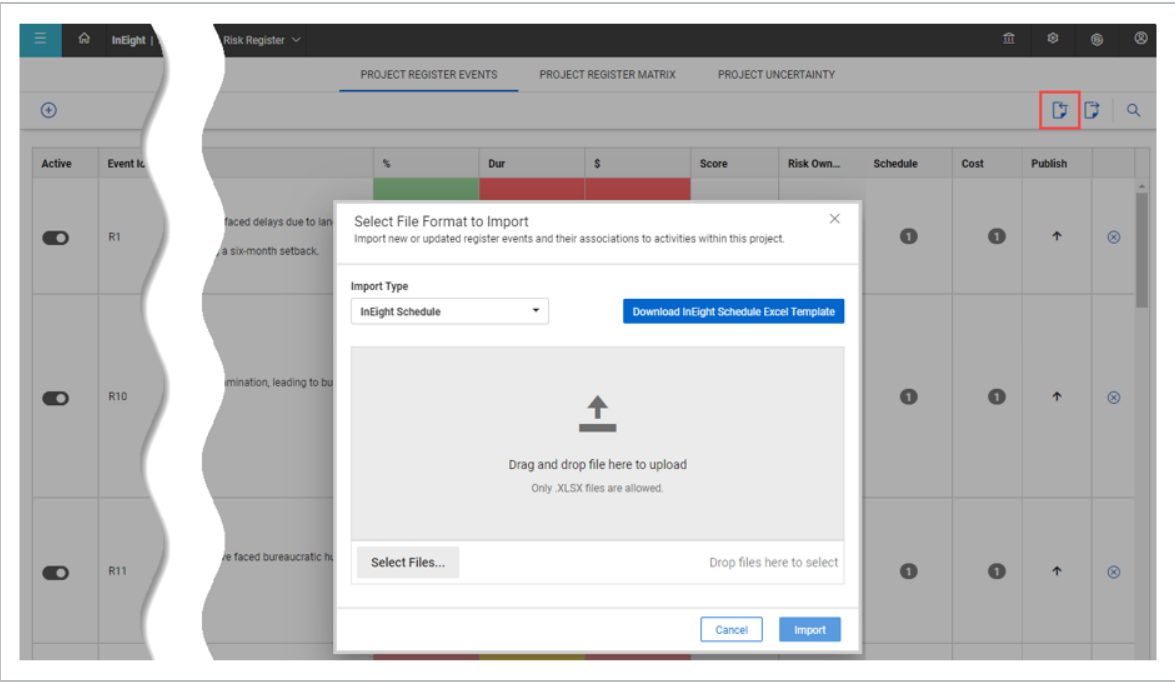

- The Project Register Matrix tab shows the attributes available for up to nine events created in the project. These are the default values available when entering data for an event.

There is also an opportunity color column which shows a blue scale to help differentiate various opportunities. The Opportunity Color scheme shows throughout the application where opportunities are presented.

PROJECT REGISTER EVENTS PROJECT REGISTER MATRIX PROJECT UNCERTAINTY					
Number of ranges 9					
Description	Probability	Schedule Impact	Cost Impact	Threat Color	Opportunity Color
Ultra Low	5	7	1000		
Extremely Low	15	20	25000		
Very Low	25	40	50000		
Low	35	50	75000		
Medium	50	60	100000		
High	65	100	1000000		
Very High	75	120	5000000		
Extremely High	85	160	7500000		
Ultra High	95	180	10000000		

For example, in the Project Register Events page, the Opportunity in the second row shows three different color ranges that are associated with the Opportunity Description in the Project Register Matrix.

PROJECT REGISTER EVENTS PROJECT REGISTER MATRIX PROJECT UNCERTAINTY								
Active	Event Id	Title	Type	Description	%	Dur	\$	Score
<input checked="" type="checkbox"/>	R1	MST Threat	Threat		Very Low (25%)	Very High (<= 1...	Medium (<= \$1...	21
<input checked="" type="checkbox"/>	O1	MST Opportunity	Opportunity		High (65%)	Very Low (<= 4...	Medium (<= \$1...	36

The Opportunity ranges one through nine (Ultra High to Ultra Low) and the blue color scale is also visible in the Mitigation page for opportunities.

Description%

Dur

\$

Score

Risk Own...

Mitigation

O1 - MST Opportunity

Probability:

High (65%)

Duration Impact:

Very Low (<= 40d)

Cost Impact:

Medium (<= \$100K)

Unmitigated:

30

+ Add new value

ID	Mitigation	%	Dur	\$	S..	Cost	Owner	Start	End
M1	MST MIT2	High (65%)	Very Low (<= ...	Medium (<= \$10...	30				

- The Project Uncertainty tab shows the attributes which the Markup & Review Cycle Score Card apply. These are the default values the scorecard will use when markups are being conducted.

PROJECT REGISTER EVENTS

PROJECT REGISTER MATRIX

PROJECT UNCERTAINTY

Description	Min	Most Likely	Max	Color
Very Conservative	50%	100%	100%	
Conservative	75%	100%	105%	
Realistic	90%	100%	110%	
Aggressive	95%	100%	125%	
Very Aggressive	100%	100%	150%	

LESSON 2 – USER ACCESS

SCHEDULE NAVIGATION


MAIN MENU

The Main menu navigation dynamically changes based on the selection of a project or an organization, your level of permissions, and the application you choose. One of the Main menu's functions is to let you connect and share data between all Eight applications involved in managing a project. This allows project management workflows to pass between job site, field office, and front office seamlessly in a consistent and standardized user interface. More information on the Main menu can be found [here](#).


Schedule can be accessed from All projects & organizations in the Main menu, which opens to the Schedule Project List page. If a schedule is linked to a project, from the project home page the Main menu click **Schedule** to open to the project workspace.

OPEN SCHEDULE FROM MAIN MENU


1. Click the Main menu icon.




2. Select **All projects & organizations** from the Main menu.

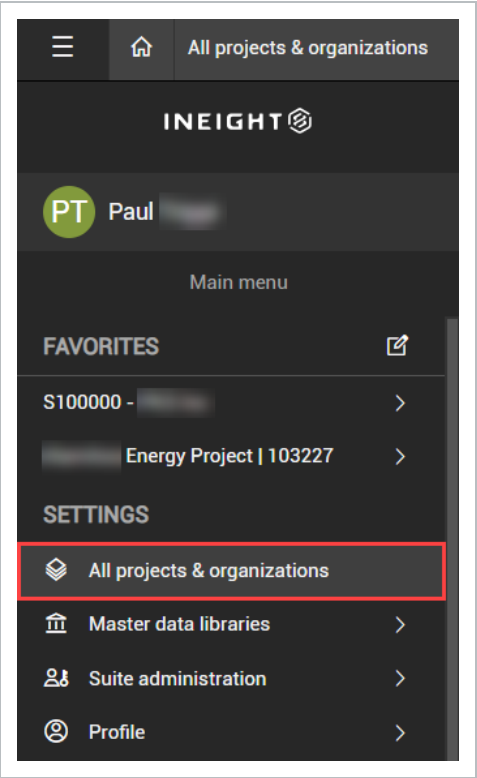

3. Click on either a **project** or an **organization**.



4. Select Schedule

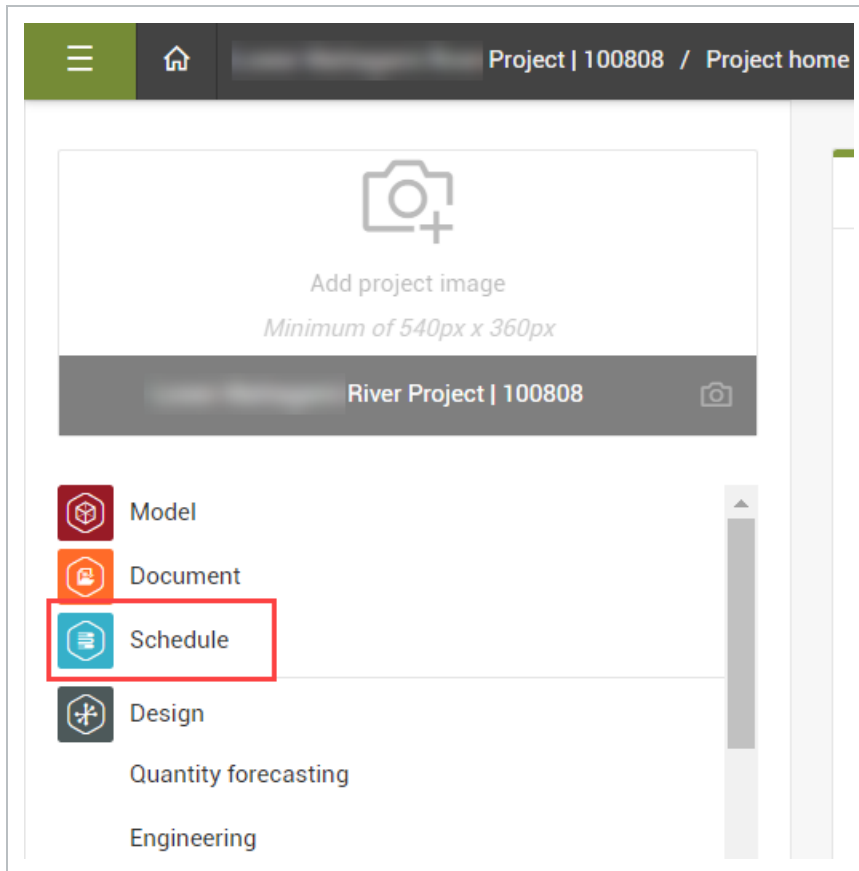

USER SETUP AND ROLES

SCHEDULE ROLES

SCHEDULE CREATOR

The Schedule Creator role is typically a planner or scheduler at an organization. The user can create schedules and has full rights to those schedules.

Schedule creators can:

- Create / delete their own schedules
- Use Knowledge Library and Smart Planning to inherit schedules and subnets
- Use Productivity Rates
- Assign contributors to schedules for markup

- Manage markup process
- Manage Review and consolidation process
- Contribute to other schedules when assigned as a schedule contributor

PROJECT MEMBER

The Project Member role can be wide range of organizational roles. The organization roles can be Supervisors, Foremen, SME's, External Subs, Customers, anyone that a project would like to contribute to the project. The Project Member role serves as a contributor to projects assigned to them by the administrator or project creator.

ADMINISTRATOR

The Administrator role in Schedule can also be considered the Super User. This role has full rights to everything in the customer instance of Schedule. The typical person in a company that would have these permissions is a senior planner who is a super user or a Planning/Scheduling leadership role.

In addition to the permissions described for the Schedule Creator and Contributor Role the Administrator can do the following:

- Manage the Knowledge Library (Schedules, Productivity Rates, Knowledge Tags, Risks)
- Create, delete, and modify any schedule
- Access to the system settings to add users to the instance

KNOWLEDGE LIBRARY ADMINISTRATOR

The Knowledge Library Administrator role is primarily responsible for creating and updating Knowledge Library tags, schedules, deliverable rates, and Register Items.


NOTE

When a user in the InEight cloud platform has their permissions updated or a new role added with administrator permissions (Level 2 or Level 3), then the Administrator permissions are automatically assigned to the corresponding Schedule user.


USER CREATION

CREATE A NEW USER


- 1. Click **Suite Administration**.



- 2. Select **User Management**.



3. Click the **Add Users**.



4. In the Details tab, enter the user contact information.

Add users

1

DETAILS

2

ROLES

* First name

Brian

* Last name

Smith

* Email address

bsmith@concreteinc.com

* Start date

02/02/2024

* End date

06/28/2025

Vendor

AA1 - Lewis Concrete

Hint: type vendor name or ID

Contact

Office number

480-555-6644

Mobile number

480-662-6654

Country / Region

United States Of America

Address 1

568 East Poinsettia Drive

Address 2

City

Scottsdale

State

Arizona


Postal / Zip code

85259

Cancel

Next

5. In the Roles tab, select the **Role** and **Organization**.



Add users

1 DETAILS 2 ROLES

Roles (1) [Add role](#)

* Role
Administrator

* Organization/Project
Desalination | 102035-DNU

Back Cancel Save

6. Select **Save**.


RELEVANT LINKS

InEight Platform - Roles and Permissions Quick Guide

SCHEDULE CONTRIBUTOR SETUP

SCHEDULE CONTRIBUTORS

Schedule Contributors are users assigned to the schedule. The contributors and their roles on a schedule are managed from the Schedule Configuration register.

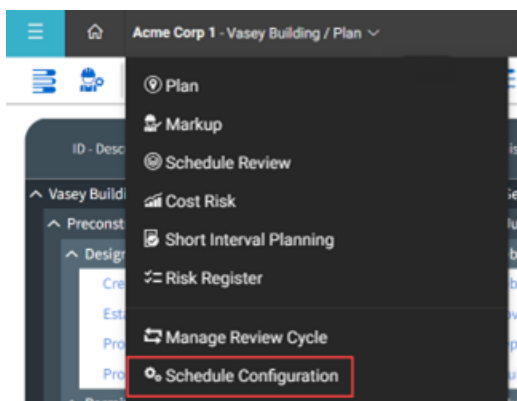

CONTRIBUTOR ROLE TYPES

Project Contributor role types pertain to the user and are specific to each project. Users can be assigned different contributor roles for each project.

MARKUP

The Markup role grants access to markup and review cycles on a schedule. Selecting this on will allow this user to be assigned to activities for markup.

SHORT INTERVAL PLANNER


This role grants access to the Short Interval Planning (SIP) section of InEight Schedule. Users in this role can be assigned to activities for field execution planning. For details on how to use the SIP Functionality, see chapter 6.

SCHEDULER

The Scheduler role has all access and privileges of the Markup and Field Execution Planner roles. Additionally, schedulers can adjust items in the Planning view, such as details in the Iris, logic in the Gantt chart, and resources.


SELECTING PROJECT CONTRIBUTORS

1. In Schedule Configuration, go to the **Contributors** tab.

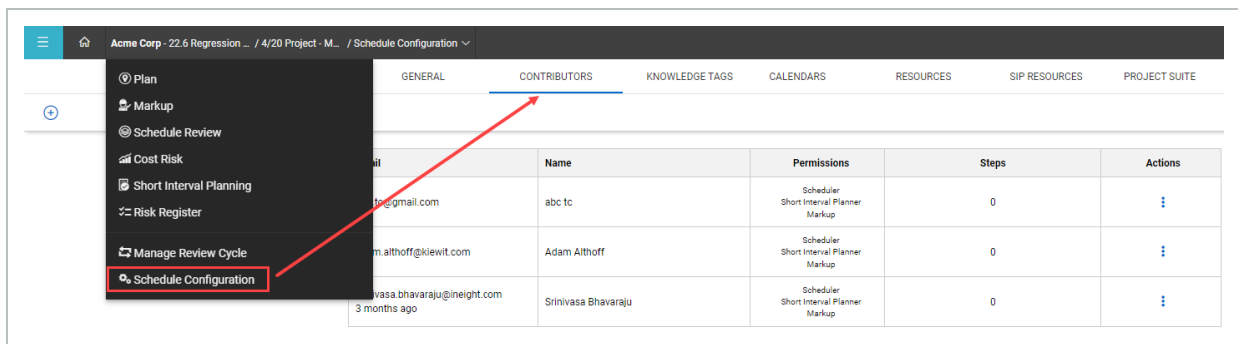


- All Project Contributors are listed in the register

2. To add a new user, click **Add User**.




- The Add User Window opens

- Schedule and Non-Schedule options are at the top of the window. Select **Schedule** to list all users currently registered in Schedule.
- Click on the user(s) to be added as project contributors.

**NOTE**

Switching to Non-Schedule changes the window to a registration form which lets guest user to be added to the project. White toggle means it's turned *Off* and when it's dark, it's turned *On*.




- Once selected, select **On** each role the new user should have.
- Click **Add**.

LESSON 3 – USER INTERFACE

PROJECT LIST VIEW

The Schedule home page is where you can see a list of projects and schedules, which includes a Gantt chart that illustrates project work and time periods. When a new project is created in InEight Platform, a workspace in Schedule is automatically added and linked to the project, which shows in the Project List view.

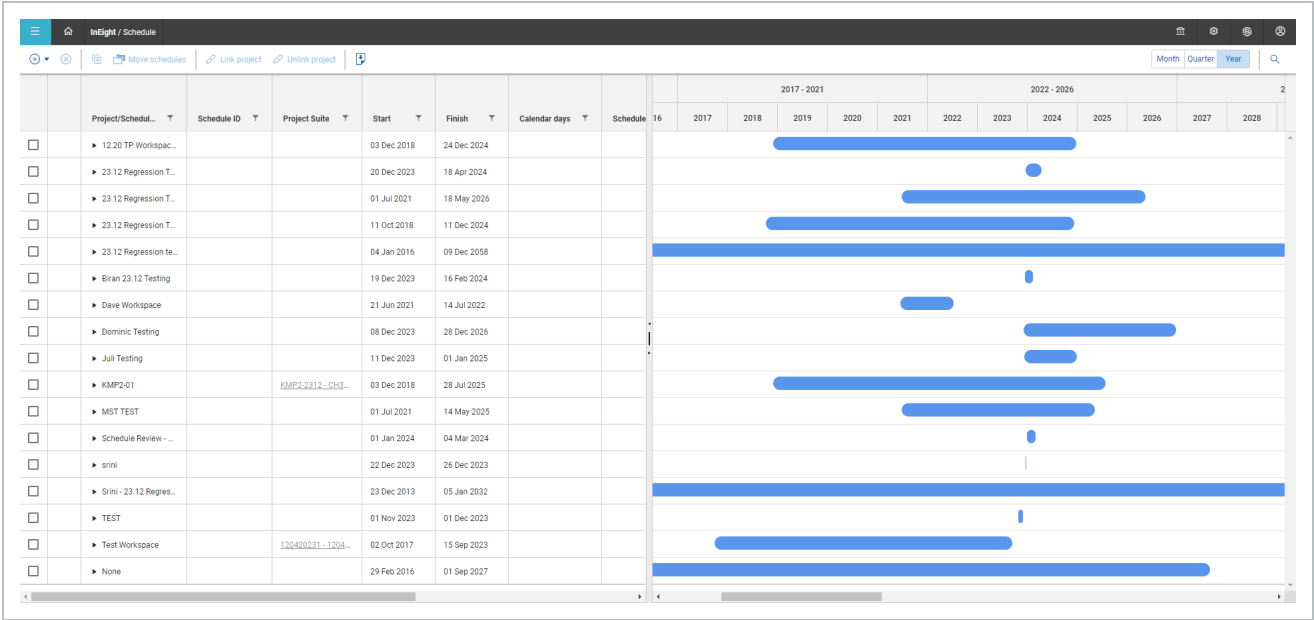


You can select multiple schedules on the Schedule home workspaces page, and then choose from the options to delete, copy or move. A locked schedule cannot be moved or deleted.

		Name	Schedule ID	Project
<input type="checkbox"/>		▶ 104256		104256
<input type="checkbox"/>		▶ 104256-D		104456
<input type="checkbox"/>		▶ 104257		104257
<input type="checkbox"/>		▼ 104690 JOC		104690
<input checked="" type="checkbox"/>		2024-C Staffing	SCHED-85	
<input checked="" type="checkbox"/>		Master Task Order Schedule	SCHED-43	

You can change the name of workspaces, folders, and IDs on the page by double-clicking the entry in the field.


		Name	Schedule ID	Project Suite	Start	Finish
<input type="checkbox"/>		-DNU-		<u>-DNU- -DNU-</u>		
<input type="checkbox"/>		<input type="text" value="Dev Solar"/>		<u>104726 -</u>	23 Dec 2013	19 Feb 2014
<input type="checkbox"/>		<u>12-9</u>	SCHED-486		09 Dec 2024	09 Dec 2024
<input type="checkbox"/>		<u>KB_Schedule_1</u>	SCHED-483		02 Dec 2024	31 Jan 2025

A Gantt chart is built in to the Schedule home page. The schedule Gantt chart illustrates horizontal lines representing work over a period in relation to the time planned for the work.

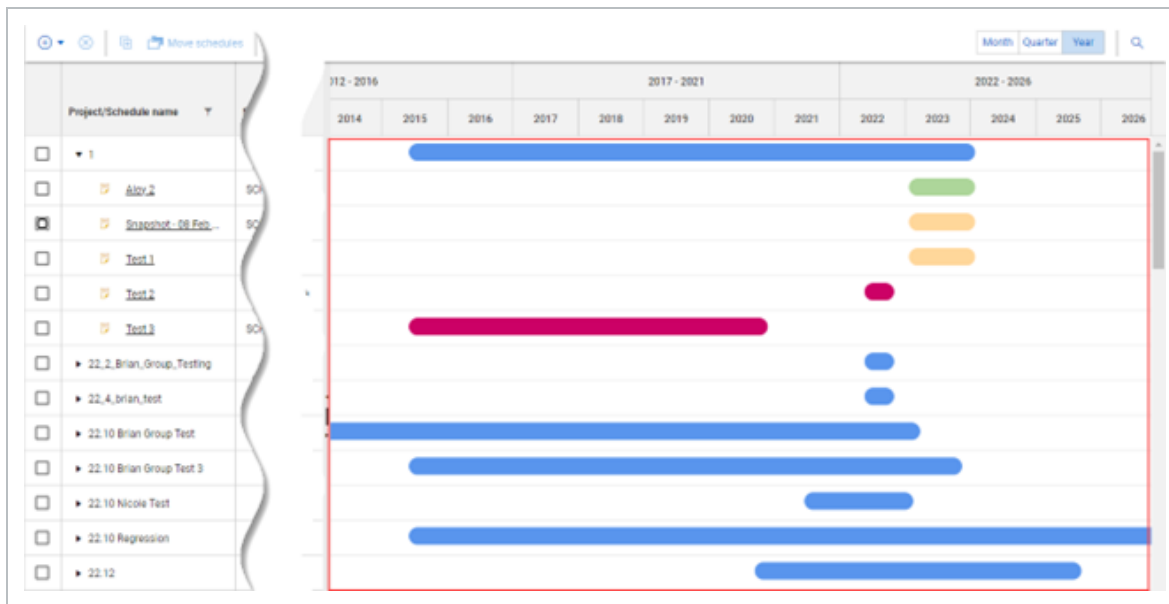

SCHEDULE FOLDERS


You can create and manage multiple project folders inside of a workspace to better organize your schedules. Schedule project folders act as storage containers that help you group like schedules into manageable repositories.




You can create up to three levels of folders to organize your schedules into, conditional upon how you want to build out the hierarchy of your folder structures.

		Name ▾	Schedule ID ▾	Project Suite ▾	Start ▾	Finish ▾
<input type="checkbox"/>		▼ Water Treatment Workspace			01 May 2024	30 Apr 2025
<input type="checkbox"/>		▼ Water Treatment Facility Folder			01 May 2024	30 Apr 2025
<input type="checkbox"/>		▼ West Coast Sub Folder			01 May 2024	30 Apr 2025
<input type="checkbox"/>		Central Coast Water Treatment...	SCHED-96		01 May 2024	30 Apr 2025

When you import schedules, there is a new Folder drop-down to select which folder to place the schedule into.

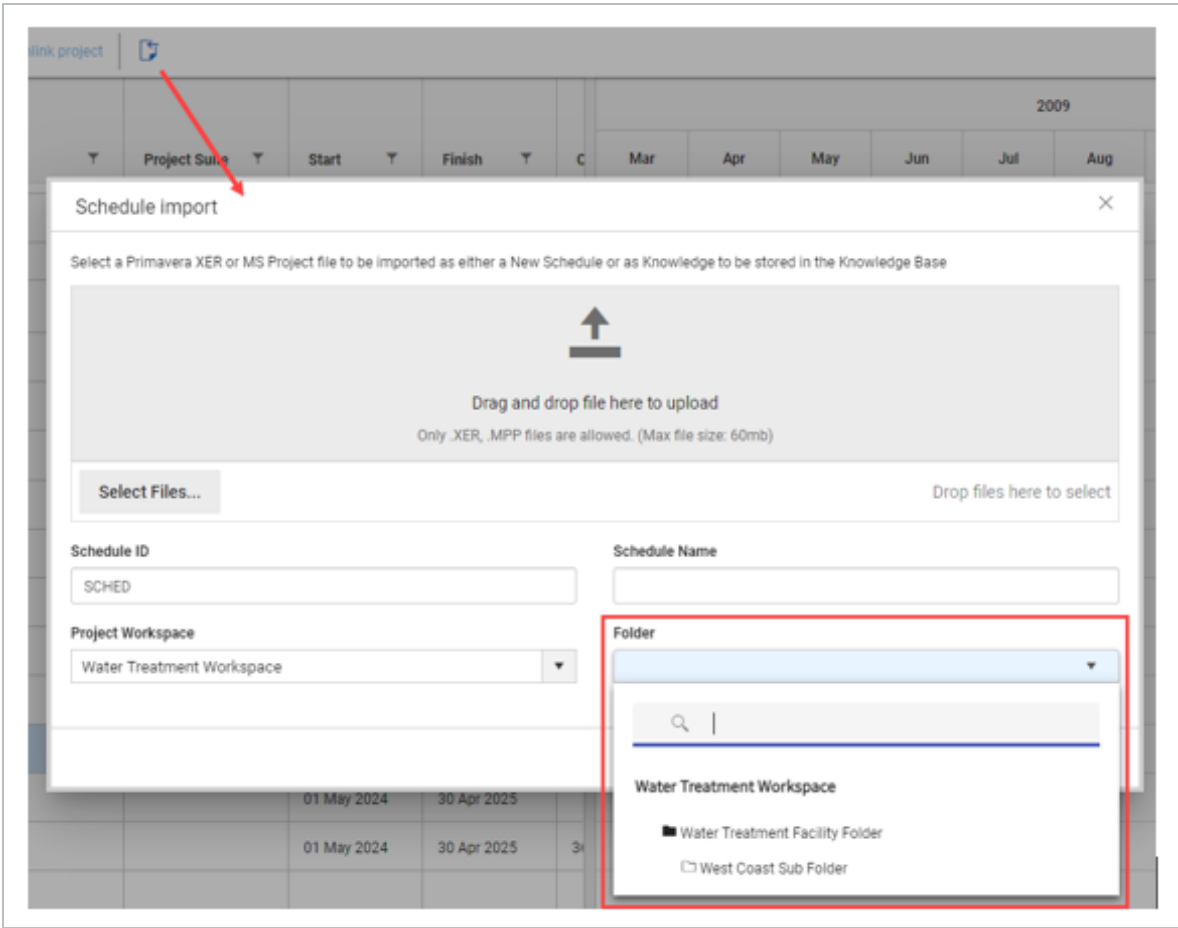




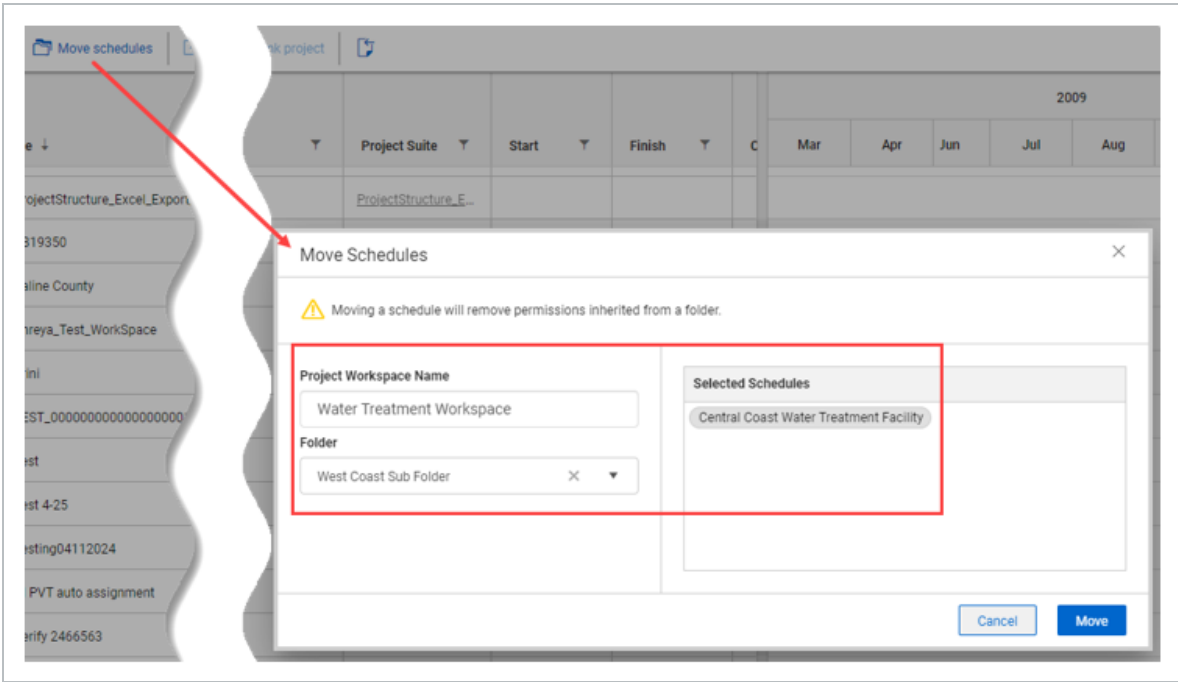






You can move schedules into specified folders.



SCHEDULE TYPE


The schedule type shows a corresponding color scheme in the Gantt chart.

Schedule type ▼	
None ▼	
Active Estimate ▼	
Inactive Estimate ▼	
Active Baseline ▼	
Inactive Baseline ▼	
Re-Baseline ▼	
Active Update ▼	
Inactive Update ▼	
Planned ▼	
What If ▼	

Schedule Type	Definition
None	No schedule type selected.
Active Estimate	Represents the latest project agreed schedule based on the construction estimate.
Inactive Estimate	Represents the previous iterations of schedules based on the construction estimate.
Active Baseline	Represents the latest submitted/client approved construction baseline.
Inactive Baseline	Represents previous iterations of submitted/client approved construction baselines
Re-Baseline	Represents a copy of a schedule that has been re-baselined prior to submittal/client approval.
Active Update	Represents the current iteration of a schedule that is actively being


Schedule Type	Definition
	executed.
Inactive Update	Represents previous iterations of a schedule being executed.
Planned	Represents variations of schedules at conceptual phases of a project.
What If	Represents variations of schedules designed to test how different scenarios impact the overall time line. Used for schedule comparison.

You can change the Schedule type values to change the colors of the horizontal lines in the Gantt chart.

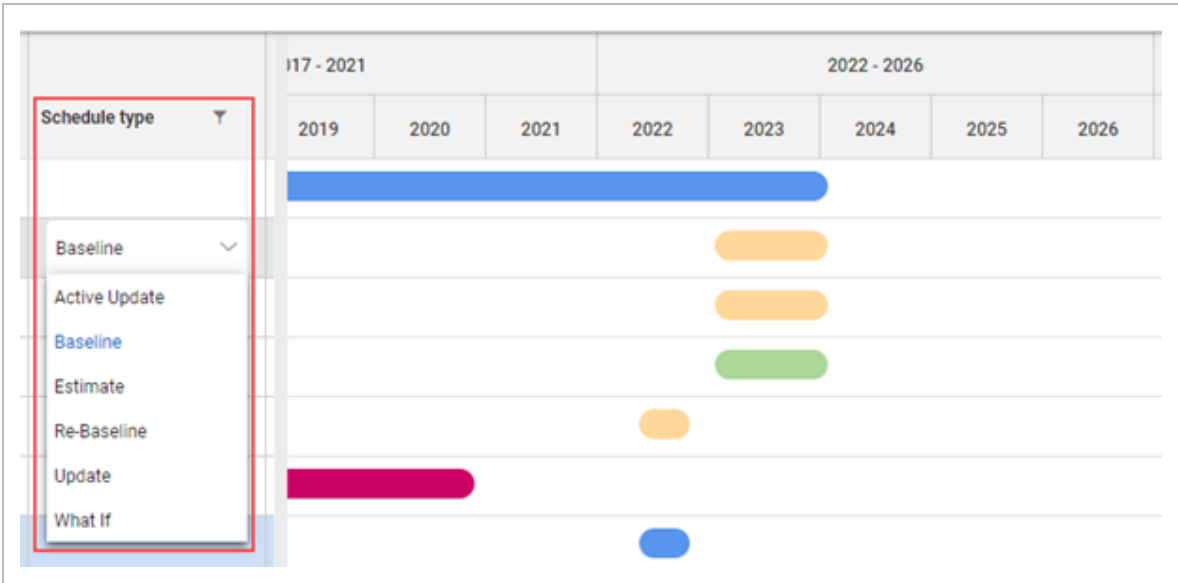

LOCKED COLUMNS

The active baseline schedule type now automatically locks the schedule and converts it into a read-only state, which includes the Gantt grid, all Iris fields, and the Import icon. The locked read only state is applied to all views and impacts any functionality that involves the changing of data.

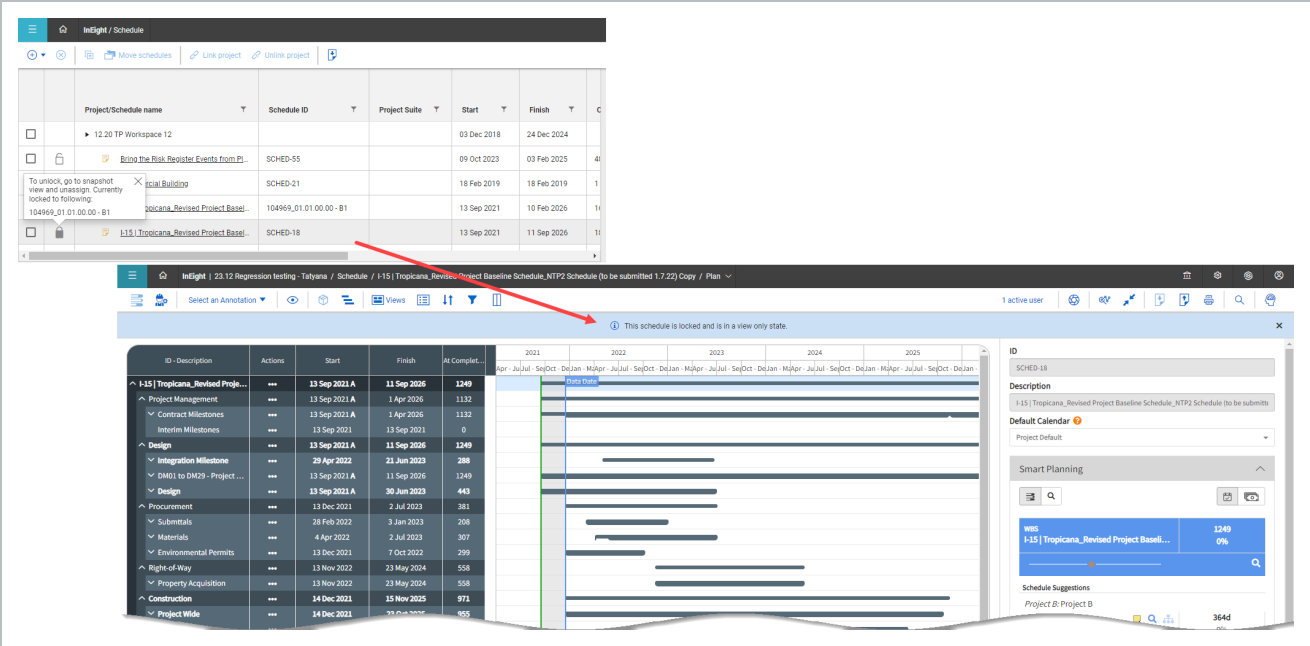

Active baselines are contractual schedule agreements between contractors and owners with infrequent changes. Some scenarios require active baselines to never change, which requires the active baseline to become locked.

The Risk register and Manage Review Cycle views are also in a locked and view only state, but data can still be exported from the Risk register.

Acme Corp | 22.10 Regression / Schedule / 10/12 Group test / Risk Register

This schedule is locked and is in a view only state.

PROJECT REGISTER EVENTSPROJECT REGISTER MATRIXPROJECT UNCERTAINTY

Active	Event Id	Title	Type	Description	%	Dur	\$	Score	Risk ...
<input type="checkbox"/>	R4	New Event	Threat						
<input type="checkbox"/>	07	Srini - ProjectOpe	Opportunity	Srini - ProjectIssue des	Low (25%)	Very High (< 180..	Very High (< \$10..	10	
<input type="checkbox"/>	629 Oppor	629 Oppor	Opportunity		Low (25%)	Low (< 30d)	Low (< \$10K)	4	
<input type="checkbox"/>	06	Srini Opp	Opportunity	Srini Opp	Low (25%)	Very Low (< 11d)	Low (< \$10K)	4	

Acme Corp | 22.10 Regression / Schedule / 10/12 Group test / Manage Review Cycle

This schedule is locked and is in a view only state.

End Review Cycle

End Review Cycle to review Markup from team members

Message

Explain to your team members the purpose of the review cycle as well as what to focus on. This message will appear in popup

Register Threshold

Difference in Schedule Duration and Team Member Markup that requires a Register entry

Team Member Markup

Assignee	Team Contribution	Last Accessed	Rea	Just	Clear Markup
Tatyana Pustovit	25% (12d) 15% (7d)	3/8/23			
Srinivasa Bhavaraju		12/21/22			
Overall	15% 7%				

Uncertainty

Export project uncertainty ranges generated from team member markup to a risk analysis tools - Oracle PRA (Pertmaster)

The Markup and Schedule Review views are disabled when the project is in a read-only state.

Acme Corp | 22.10 Regression / Schedule / 10/12 Group test / Plan

Select an Annotation

Plan

Markup

Schedule Review

Cost Risk

Short Interval Planning

Risk Register

ID - Description


ABC Building Project Baseline

ABC Building


Summary & Milestones

SHOW/HIDE LOGIC, WBS

In the Plan view from the first level drop-down menu within a project, click the **ID** icon to show or hide WBS Codes.

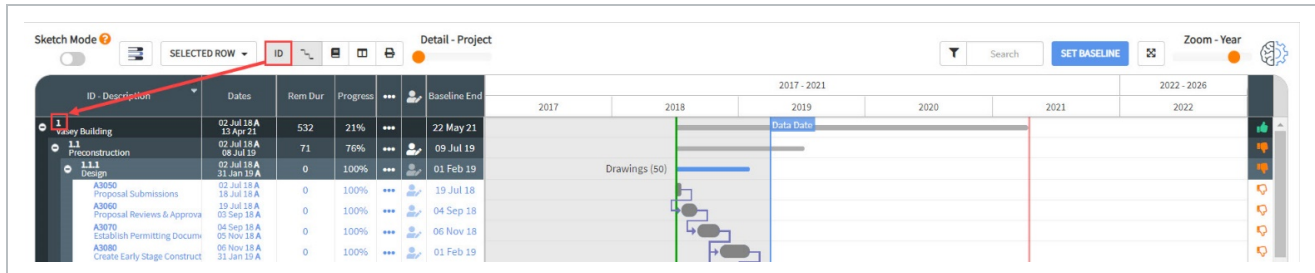


Click on the **Logic** icon to show or hide logic relationships.

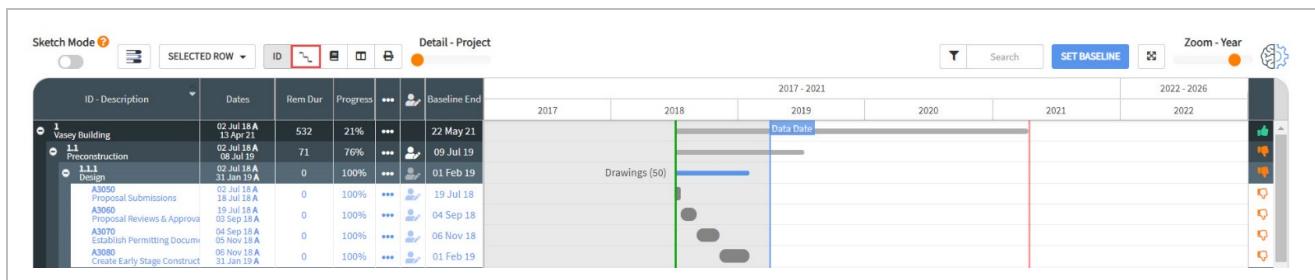


ANNOTATIONS


In the Plan view from the first level drop-down menu in a project, click the **Annotations** drop-down menu.

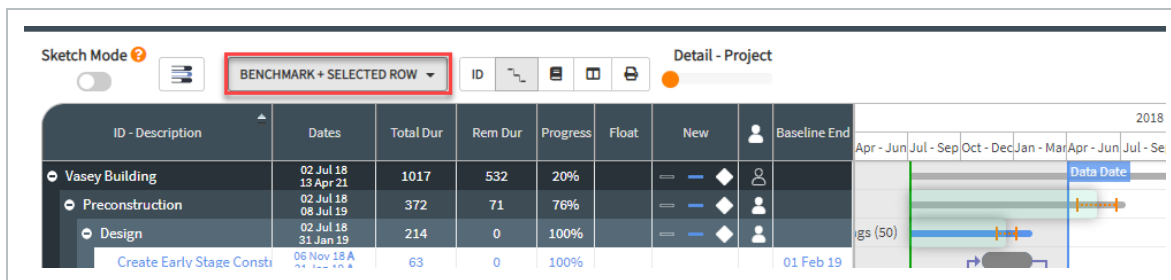


From here, Annotations can be changed by clicking the various options, which will update the information displayed on the Gantt Chart.

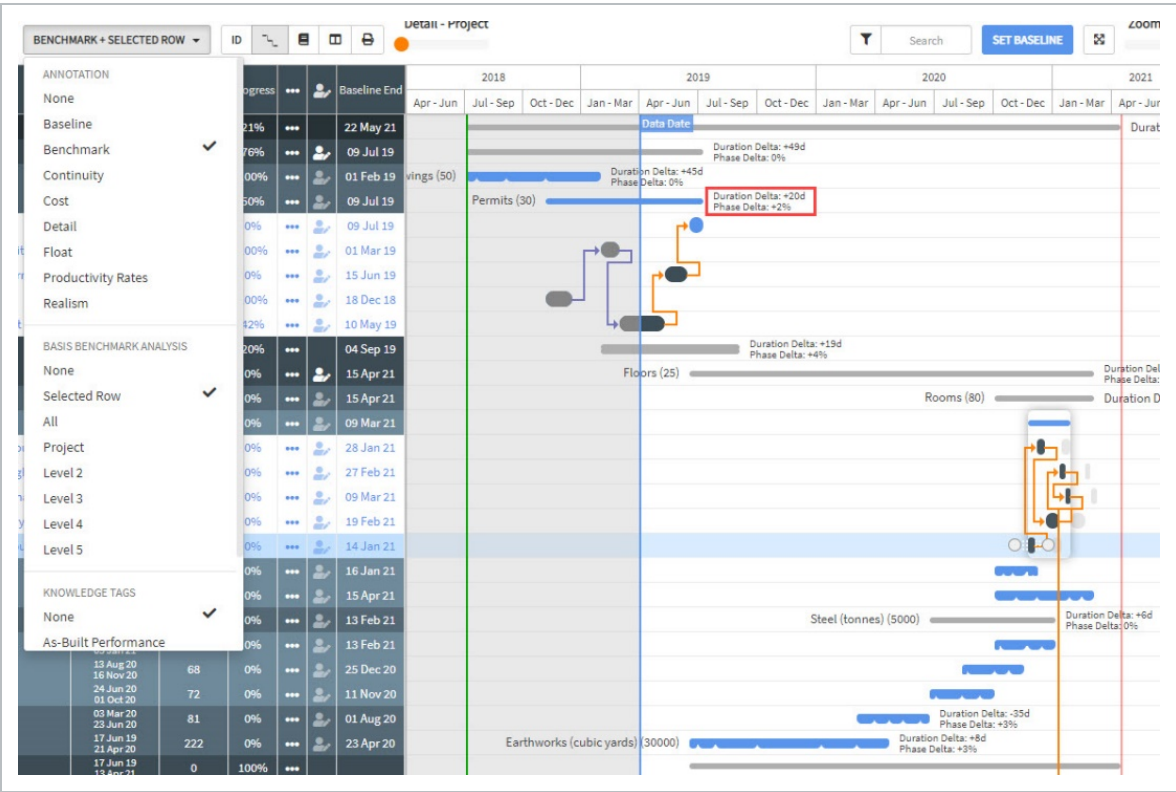

The Benchmark Analysis options can also be used to change what level or WBS elements the phase windows appear.

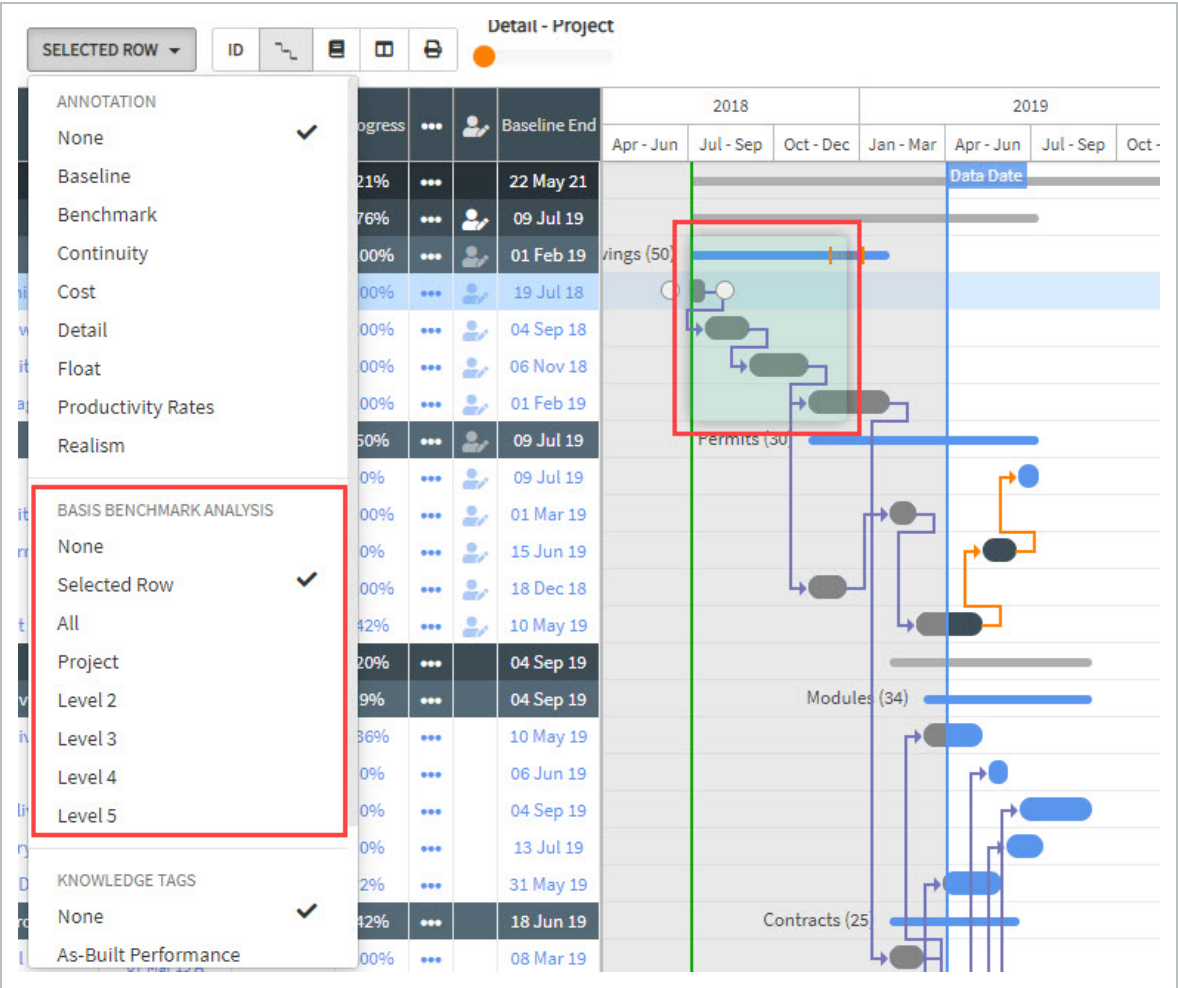

The phase window indicates the time period that the benchmark falls within in the Knowledge Library project, conformed to the current project using the current project's start date and knowledge tags normalizers. For items that have the phase window showing, there is also a set of brackets indicating a range that the complete date of a summary WBS element is expected to fall within.

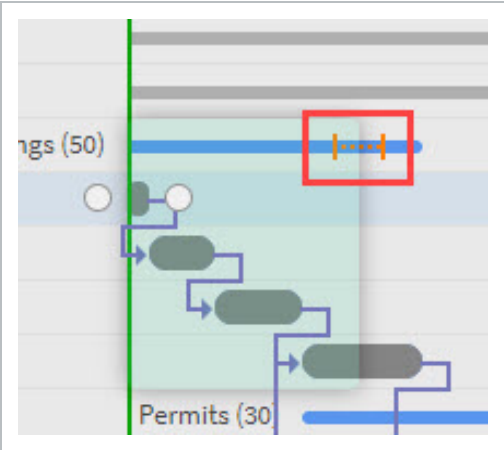


This is based on the % of tolerance defined in the project settings, the start date of the summary WBS in the current project, and the duration of the benchmark from the Knowledge Library.

SCHEDULE CRITIQUE OVERVIEW


The **Schedule Critique** annotations and filters are available in the Plan view in Schedule. These functions aid schedulers in quickly identifying and isolating potential concerns with the current schedule logic.

TOGGLE SCHEDULE CRITIQUE ANNOTATIONS ON / OFF:







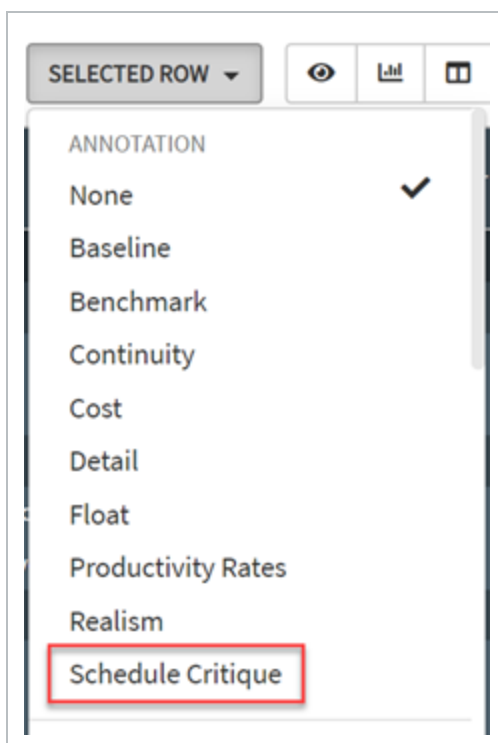

1. Start from the Plan view of a project and select the 1st level drop-down menu.



2. Under the Annotation section select **Schedule Critique**.



3. Once selected, the following icons will populate in the Gantt chart, representing potential logic and schedule concerns. These icons are detailed in the table below:

Icon	Description	Definition
	Missing Predecessor	The activity does not have any predecessor logic links and is not at the start of the project.
	Missing Successor	The activity does not have any successor logic links and is not at the end of the project.
	Lead or Lag	Predecessor and / or successor logic links contain lag.
	Insufficient Detail	The activity spans more than 10 % of the overall project duration.
	Incoming Bottleneck	The activity has 3 or more predecessor logic links.
	Logic Complexity	The activity has 3 or more predecessor logic links and 3 or more successor logic links.
	Hard Constraint	The activity uses a Must Start On / Must Finish On constraint.
	Negative Float	Total float is less than zero.

NOTE

The color of each icon represents the criticality of a critique. Blue icons are typically not desired as they often impede the flow of a schedule. Orange icons are considered with more caution, as these have a higher potential for schedule delay. Red icons identify activities of serious concern.


MISSING PREDECESSOR OR SUCCESSOR

A **Missing Predecessor** or **Missing Successor** indicator appears when an activity does not have a predecessor or successor activity associated. Adding a predecessor or successor activity resolves this critique.

BUILDER MENUS


You can run advanced grouping, sorting, and query filters on multiple columns in several Schedule views, save as personal views and reuse in your assigned projects.

All menu builders can be saved and reused and are highlighted when there are existing saved views. Menu builder icons show when there are existing saved views. The enhanced search functions are available for all group by and sort builders.




COLUMN SET BUILDER MENU

The Column set builder menu lets you add and remove columns in the Plan, Markup, and Schedule Review views.

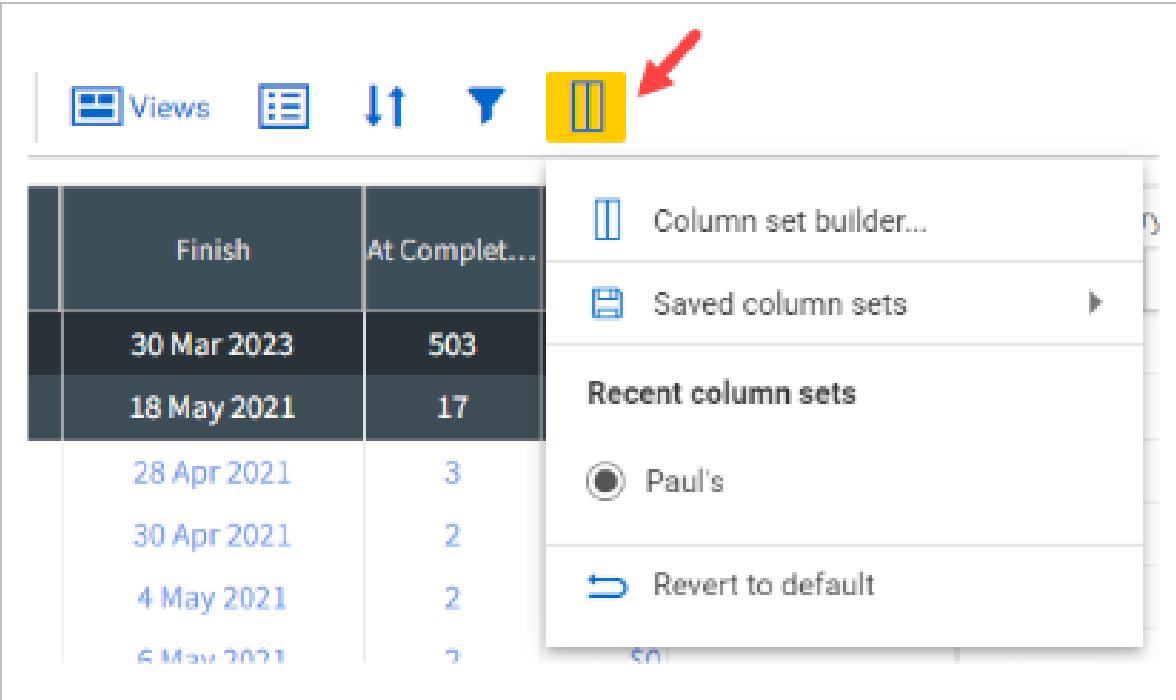


You can choose available columns in the Column set builder to create customized column page layouts.

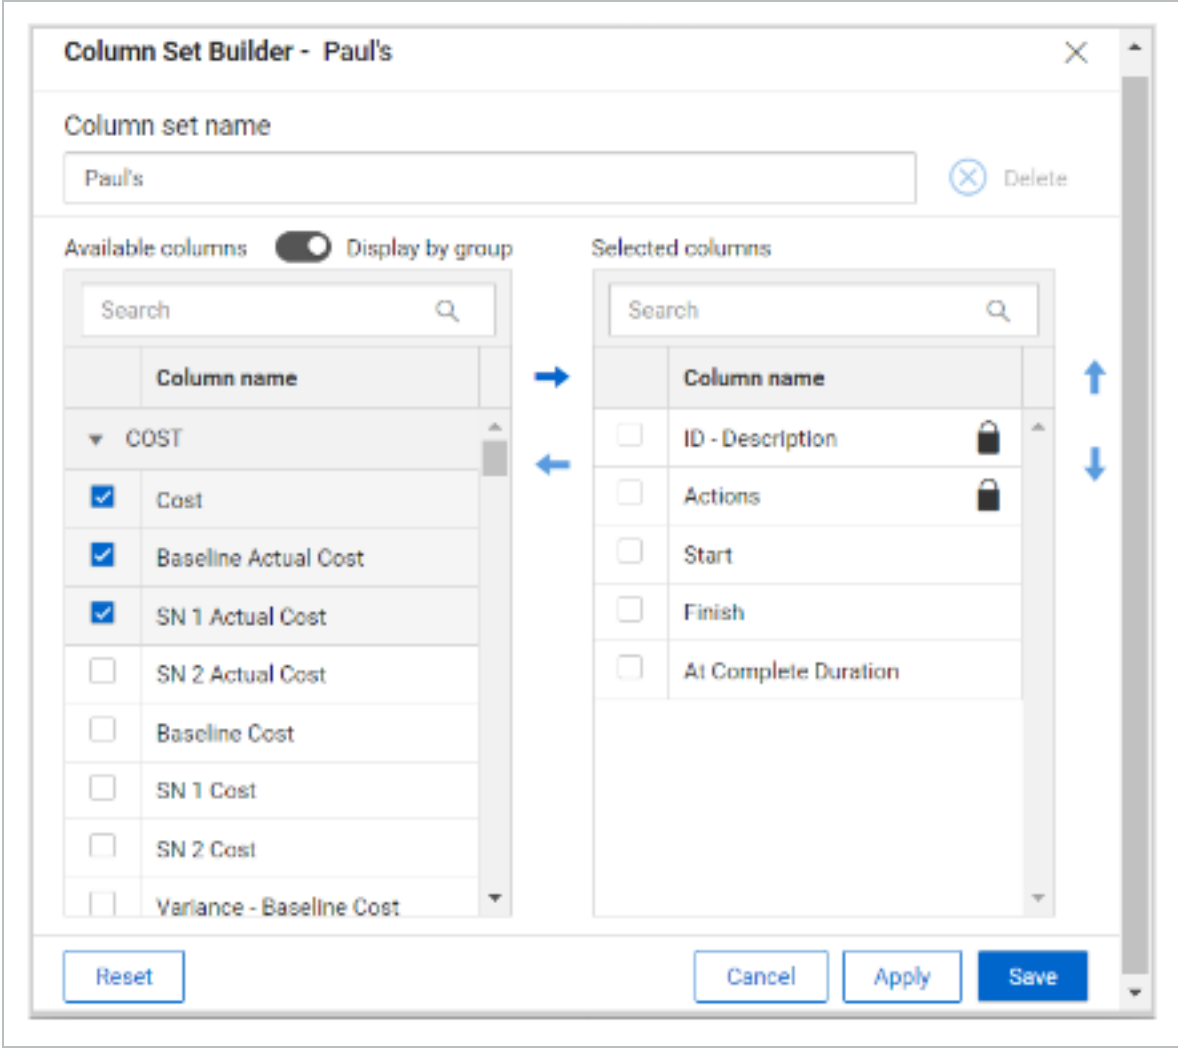


QUERY BUILDER MENU

The Query builder menu lets you set column filters in the Plan, Markup, Schedule Review, and Cost Risk views.

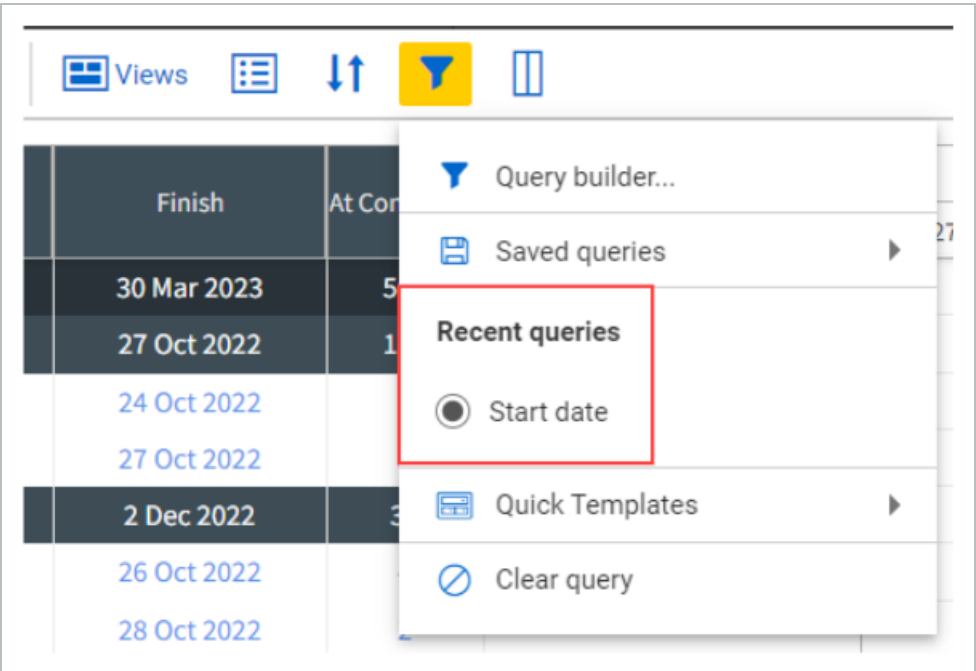


You can choose available columns in the Query builder to create customized page layout query.

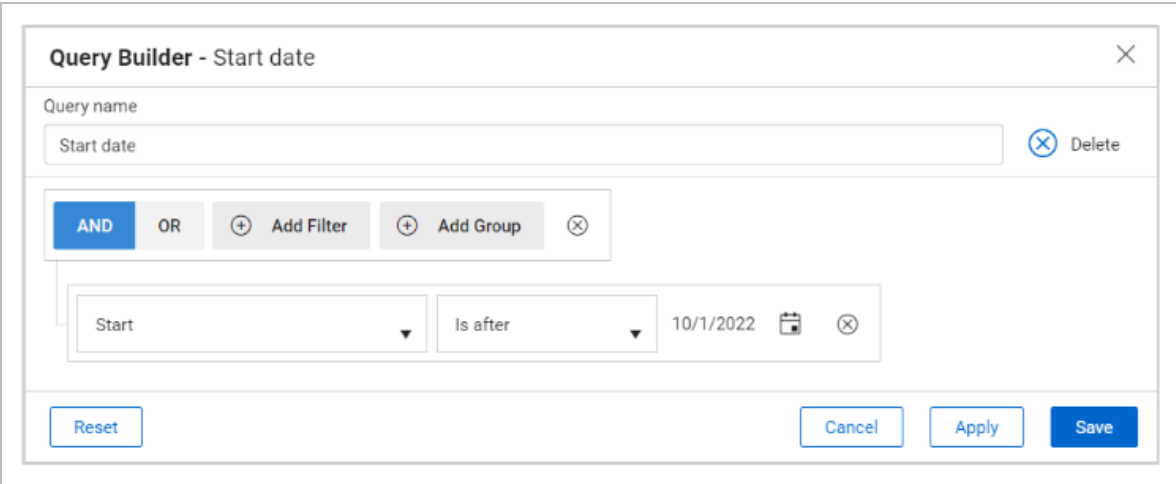


SORT BUILDER MENU

The Sort builder menu lets you sort columns in the Plan, Markup, Schedule Review, and Cost Risk views.

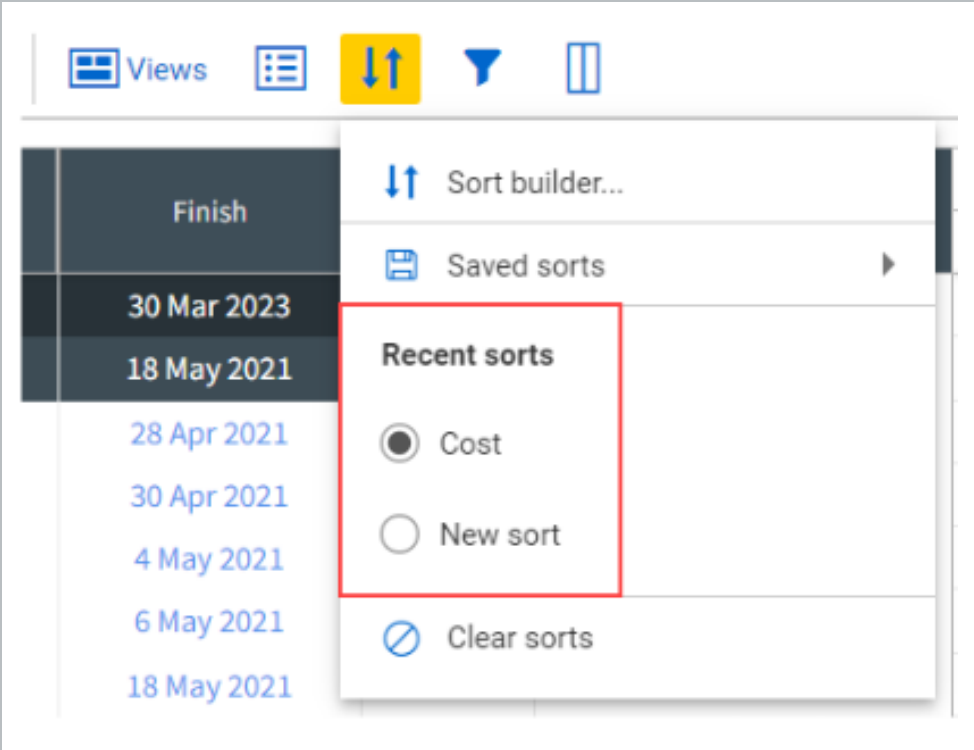


You can choose up to ten columns to sort in ascending and descending order.



GROUP BY BUILDER MENU

The Group by builder menu lets you group columns in the Plan, Markup, Schedule Review views.

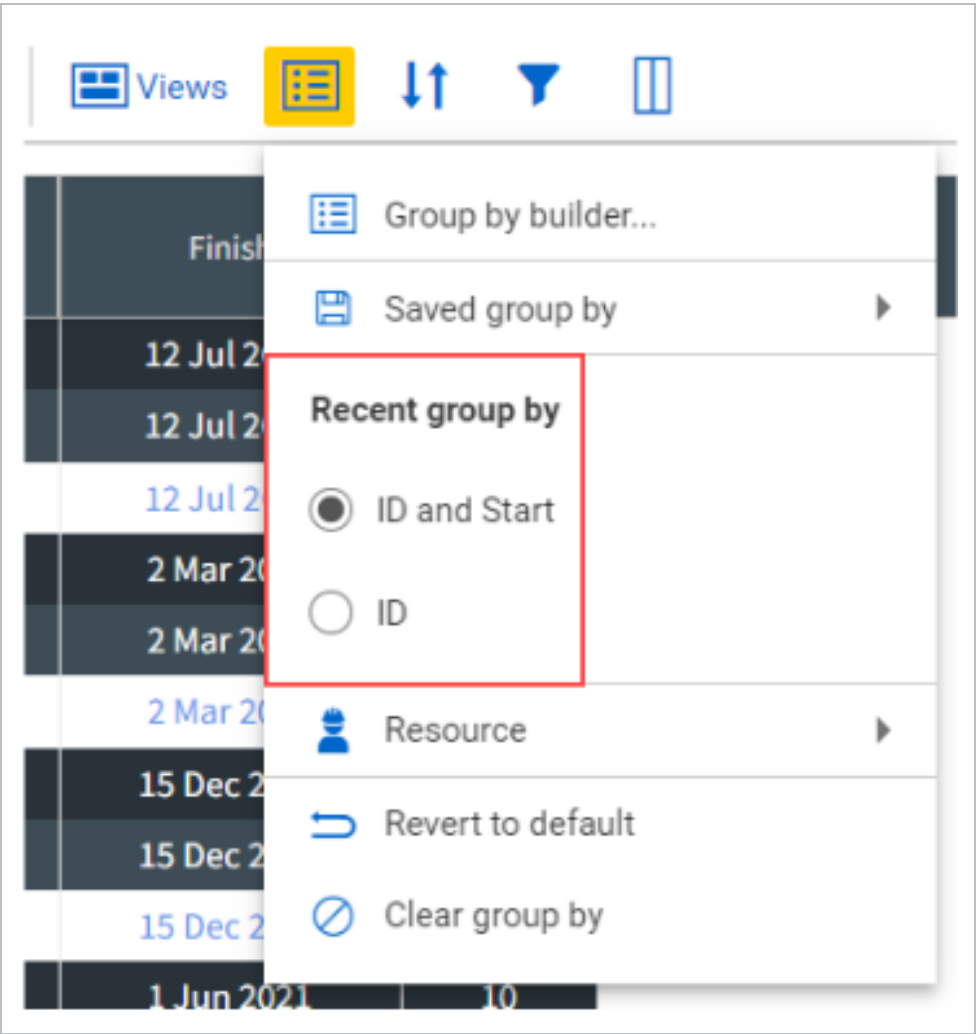

You can choose to group by one column or multiple columns.

Group by builder - Unsaved Group By

Group by name


ID and Start
Delete

Column	Levels	Position
ID	Levels	1 <div>+</div> <div>×</div>
Start	Levels	2 <div>+</div> <div>×</div>

Reset
Cancel
Apply
Save

VIEW BUILDER MENU

The View builder menu lets you combine columns from the other builder menus and show in the Plan, Markup, Schedule Review views.

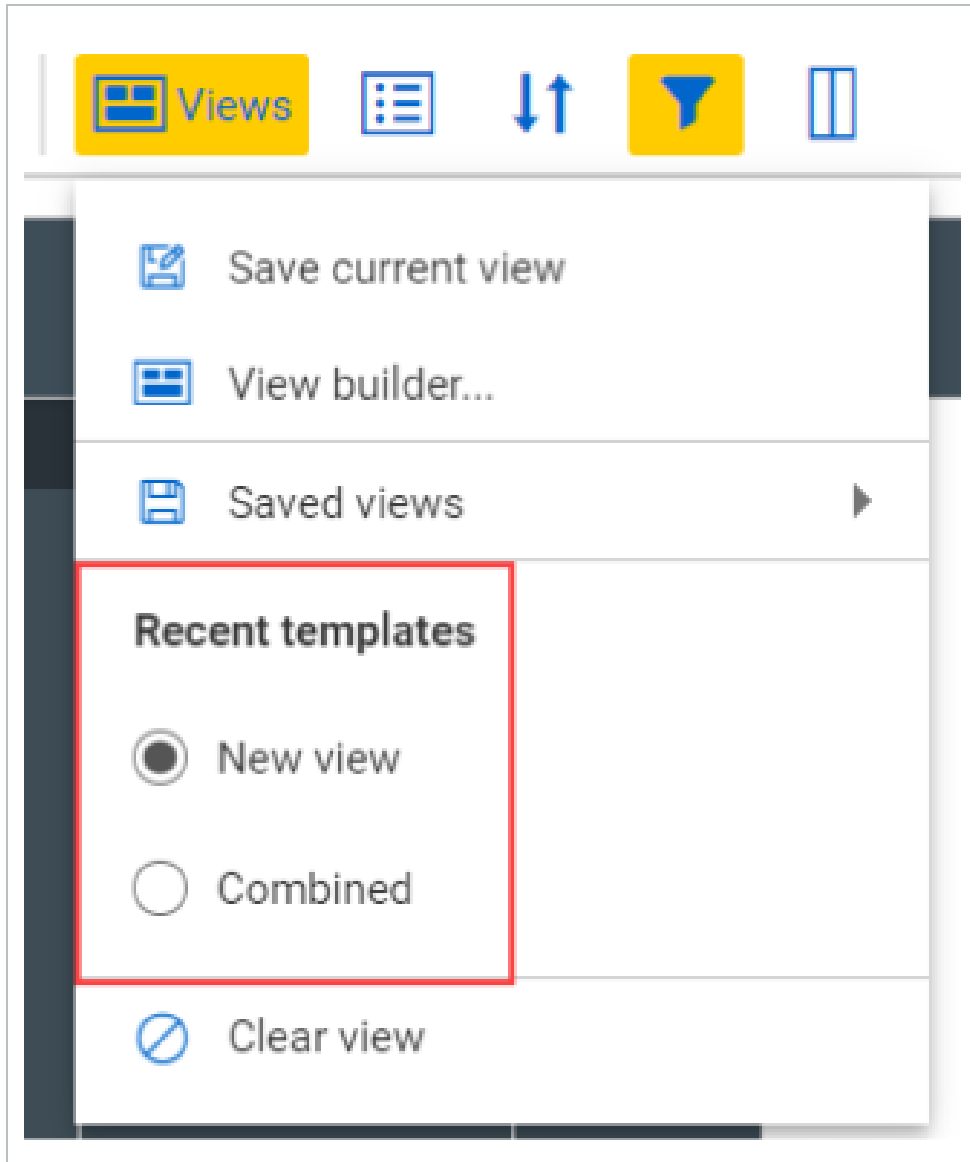

The View Builder lets you choose multiple columns from any of the builder menu columns. The chosen builder menus are highlighted on the toolbar.

View Builder - Unsaved View

Name

New view (1)

ⓧ Delete

Group by

Select one

Sort

Select one

Query

Select one

Select one

Start date

Reset

Cancel

Save

HIDE NO RESULTS

In View Options, the Hide No Results toggle lets you hide any WBS items or groupings on the Plan page that do not yield any results.


InEight | / Schedule / Commercial Building / Plan

Select an Annotation

Views

ID - Description	Actions	General	At Complet...
Commercial Building	⋮	ID	0
Preconstruction	⋮	Hide No Results	0
Design	⋮	Resources	0
Permitting	⋮	Histogram	0
Procurement	⋮	Baseline/Snapshots	0
Fabrication & Delivery	⋮	Active Baseline	0
Submittals & Approval	⋮		0

For example, Interim Milestones does not show any scheduled activities, work packages, or milestones, in the Gantt chart.

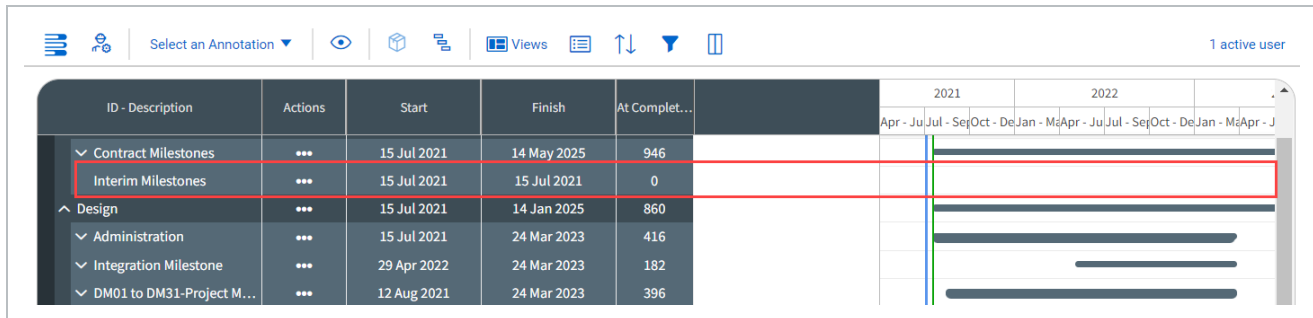

When the Hide No Results toggle is set to *On*, Interim Milestones is removed from the Plan view.



LESSON 3 – KNOWLEDGE LIBRARY

KNOWLEDGE BASE

RESOURCES IN THE KNOWLEDGE BASE

To access the Knowledge Base, click the **Knowledge Base** icon.

In the Knowledge Base, you can establish the base pool of resources for the organization. Schedule is built on top of augmented intelligence, or machine based learning. The Knowledge Base is used to enhance machine based learning and load with past schedule-related data that an organization would want to include in future schedules. Hence, this data that gets loaded should be as accurate as possible. After set up, schedulers can pull these into projects for use with the resource management functionality and analytics.

CPM SCHEDULES	ACTIVITY PRODUCTIVITY RATES	KNOWLEDGE TAGS	CALENDARS	REGISTER	RESOURCES	MACHINE LEARNING
<div> </div>						
Schedules ↓	Schedule ID		Start	Finish	Data Date	Verified
MPP Project	SCHED-17		2 Jul 2018	18 Jun 2023	2 Jul 2018	
ms proj	SCHED-18		1 Jul 2019	26 Feb 2023	1 Jul 2019	
MS project	SCHED-1		3 Jul 2018	13 Sep 2020	3 Jul 2018	
New CPM Schedule	SCHED-19		9 Jun 2021	9 Jun 2022	19 Aug 2021	
new kb	SCHED-70		12 Apr 2022	12 Apr 2023	12 Apr 2022	
New Sch on 6.27	SCHED-83		27 Jun 2022	27 Jun 2023	27 Jun 2022	
New schedule from Scratch	SCHED-54		14 Feb 2022	14 Feb 2022	14 Feb 2022	
no ID	NO ID		3 Jul 2018	13 Sep 2020	3 Jul 2018	
not	SCHED-37		27 Sep 2021	27 Sep 2021	1 Apr 2019	
Offshore Platform	SCHED-20		8 May 2019	8 May 2020	8 May 2019	
Offshore Platform [OUTLINED @ 7/15/20...	SCHED-21		8 May 2019	8 May 2019	8 May 2019	
Paradise	SCHED-22		29 Oct 2020	29 Oct 2020	26 Mar 2017	
Preconstruction	SCHED-23		2 Jul 2018	16 May 2024	27 Oct 2020	
Procurement	SCHED-24		1 Oct 2017	1 Oct 2018	1 Oct 2017	
ProjectCode Match	SCHED-80		16 Jun 2022	16 Jun 2023	16 Jun 2022	
PT	SCHED-112		26 Oct 2022	26 Oct 2023	26 Oct 2022	
Publish to KB	SCHED-49		21 Feb 2022	20 Feb 2023	19 Feb 2022	

CPM SCHEDULE

CPM schedules in the Knowledge Base contain the same information as project schedules. CPM schedules are past or current schedules where relevant schedule data can be used in future schedules. For example: if you are working on a new schedule for bridgework, you can store past bridgework schedules in the knowledge library to use later for machine learning for new projects.

The Verified column on the far right is controlled by an administrator, and represents schedules that have been certified as schedules that contain accurate data. Schedules that show a green dot are verified, and red dots are unverified schedules.

CPM SCHEDULES

ACTIVITY PRODUCTIVITY RATES

KNOWLEDGE TAGS

CALENDARS

REGISTER

RESOURCES

MACHINE LEARNING

Schedules ↓	Schedule ID	Start	Finish	Data Date	Verified
<div><div></div><div>MPP Project</div></div>	SCHED-17	<div><div></div><div>2 Jul 2018</div></div>	18 Jun 2023	2 Jul 2018	<div><div></div><div></div></div>
<div><div></div><div>ms proj</div></div>	SCHED-18	<div><div></div><div>1 Jul 2019</div></div>	26 Feb 2023	1 Jul 2019	<div><div></div><div></div></div>
<div><div></div><div>MS project</div></div>	SCHED-1	<div><div></div><div>3 Jul 2018</div></div>	13 Sep 2020	3 Jul 2018	<div><div></div><div></div></div>
<div><div></div><div>New CPM Schedule</div></div>	SCHED-19	<div><div></div><div>9 Jun 2021</div></div>	9 Jun 2022	19 Aug 2021	<div><div></div><div></div></div>
<div><div></div><div>new kb</div></div>	SCHED-70	<div><div></div><div>12 Apr 2022</div></div>	12 Apr 2023	12 Apr 2022	<div><div></div><div></div></div>
<div><div></div><div>New Sch on 6.27</div></div>	SCHED-83	<div><div></div><div>27 Jun 2022</div></div>	27 Jun 2023	27 Jun 2022	<div><div></div><div></div></div>
<div><div></div><div>New schedule from Scratch</div></div>	SCHED-54	<div><div></div><div>14 Feb 2022</div></div>	14 Feb 2022	14 Feb 2022	<div><div></div><div></div></div>
<div><div></div><div>no ID</div></div>	NO ID	<div><div></div><div>3 Jul 2018</div></div>	13 Sep 2020	3 Jul 2018	<div><div></div><div></div></div>
<div><div></div><div>not</div></div>	SCHED-37	<div><div></div><div>27 Sep 2021</div></div>	27 Sep 2021	1 Apr 2019	<div><div></div><div></div></div>
<div><div></div><div>Offshore Platform</div></div>	SCHED-20	<div><div></div><div>8 May 2019</div></div>	8 May 2020	8 May 2019	<div><div></div><div></div></div>
<div><div></div><div>Offshore Platform [OUTLINED @ 7/15/20...</div></div>	SCHED-21	<div><div></div><div>8 May 2019</div></div>	8 May 2019	8 May 2019	<div><div></div><div></div></div>
<div><div></div><div>Paradise</div></div>	SCHED-22	<div><div></div><div>29 Oct 2020</div></div>	29 Oct 2020	26 Mar 2017	<div><div></div><div></div></div>
<div><div></div><div>Preconstruction</div></div>	SCHED-23	<div><div></div><div>2 Jul 2018</div></div>	16 May 2024	27 Oct 2020	<div><div></div><div></div></div>
<div><div></div><div>Procurement</div></div>	SCHED-24	<div><div></div><div>1 Oct 2017</div></div>	1 Oct 2018	1 Oct 2017	<div><div></div><div></div></div>
<div><div></div><div>ProjectCode Match</div></div>	SCHED-80	<div><div></div><div>16 Jun 2022</div></div>	16 Jun 2023	16 Jun 2022	<div><div></div><div></div></div>
<div><div></div><div>PT</div></div>	SCHED-112	<div><div></div><div>26 Oct 2022</div></div>	26 Oct 2023	26 Oct 2022	<div><div></div><div></div></div>
<div><div></div><div>Publish to KB</div></div>	SCHED-49	<div><div></div><div>21 Feb 2022</div></div>	20 Feb 2023	19 Feb 2022	<div><div></div><div></div></div>

ACTIVITY PRODUCTIVITY RATES

Organizations can use Activity Productivity Rates deemed as being the most productive, which can be used to give you durations.

CPM SCHEDULES

ACTIVITY PRODUCTIVITY RATES

KNOWLEDGE TAGS

CALENDARS

REGISTER

RESOURCES

MACHINE LEARNING

Description	Output	UOM	Duration/Output	Duration Unit	\$/Output		
Act 1	1250	Sec		Days	\$5,000,500.00		
Act1	8500	Hours	150	Days	\$787,878,778.00		
APR 1	2	10	200	Hours	\$6,000,000.00		
Brian Test Rate	1	23	23	Days	\$230.00		
Concrete	80	Cubic Yards	144	Days	\$40,000.00		
Concrete Pour (generic)	400	Sq Feet	1	Days	\$36,000.00		
Concrete Pour (generic)	8	Cubic Yards	1	Days	\$0.00		
Concrete Pour (refinery)	6	Cubic Yards	1	Days	\$0.00		
Concrete Pour (refinery)	60	Cubic Yards	1	Days	\$52,000.00		
Controls	1	Unit	4	Days	\$20,000.00		
Controls	1	Unit	4	Days	\$0.00		
Drywall	1	1	5	Days	\$0.00		
Early Works	1	Acre	1	Days	\$0.00		
Early Works	1	Acre	1	Days	\$2,000.00		
Early Works	1	Acre	1	Days	\$2,000.00		
EIA	1	Unit	24	Days	\$30,000.00		
EIA	1	Unit	24	Days	\$0.00		
Excavation	200	Linear Feet	1	Days	\$0.00		
Excavation	0.25	Cubic Yards	0.5	Hours	\$0.00		

KNOWLEDGE TAGS

On the Knowledge Tags tab, you can review tags defined at the organization level and exclude them as necessary from consideration by the Schedule inference engine. When a new project is created, you have the option to import these knowledge tags into the new project.

CPM SCHEDULES ACTIVITY PRODUCTIVITY RATES **KNOWLEDGE TAGS** CALENDARS REGISTER RESOURCES MACHINE LEARNING

+

Codes / Project

Codes

Project

Activity

Register Event

Resource

UDFs

Project

WBS

Activity

Register Event

Resource

Project Codes		
10/7 Project Code		
7/12 T code		
7/5 - KB - Codesproject		
Business Groups		
Code 25.25-3		
CodesProject 1		
CodesProject 2		
CodesProject 3		
KB - Code Project 1		
KB - Code Project 2		
Locations		
Project Code 10/6		
ProjectCodes 1		
ProjectCodes 2		
ProjectCodes 3		
Prosjekt kode 9-16		
Regression Code		
Srini 5 C/H tag		
SriniProjectCode		

CALENDARS

On the Calendars tab, additional calendars can be created, working days can be edited, and a default calendar can be defined. This is also where holidays are defined.

CPM SCHEDULES

ACTIVITY PRODUCTIVITY RATES

KNOWLEDGE TAGS

CALENDARS

REGISTER

RESOURCES

MACHINE LEARNING

Calendar	Hours/d...	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Exceptions	Actions
2 Days	10	<input type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	4	
22 Day	10	<input type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	0	
3 Day	8	<input type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	0	
4 Day	8	<input type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input type="radio"/>	<input type="radio"/>	0	
5 Day	8	<input type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input type="radio"/>	0	
6 Day	8	<input type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	0	
7 Day	8	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	0	
Brian Default Work Schedule	1	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input checked="" type="radio"/>	<input type="radio"/>	<input type="radio"/>	0	
Global Calendar	8	<input type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input type="radio"/>	0	
My calendar	5	<input type="radio"/>	<input type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input type="radio"/>	<input type="radio"/>	2	
Tatyana's calendar	6	<input type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input checked="" type="radio"/>	<input type="radio"/>	2	

REGISTER

EVENTS REGISTER

The Events register is where you store persistent risks that occur on projects. The Events register is useful for pulling stored risks into new schedules and use them for risk workshops. The following fields can be quickly edited from the register.

Tab	Function/Description
Title	Title of the event.
Type	This describes the type of register item, for example, Risk, Opportunity, or Action Item.
Description	Items descriptions can be edited at any time.
%	The Probability an event will occur in a risk simulation.
Dur	Impact range event would have on a simulation when it occurs.
\$	Impact range event would have on a simulation when it occurs

Tab	Function/Description
Score	A score is automatically generated based on the probability and impact of items.
Mitigation	Mitigation strategies can be captured here.
Status	Indicates the status of an event in the register
Activities	The number of times the register item appears schedules. Specific Project and WBS element appearances can be reviewed by clicking on the number. You can select the All drop down to filter the list by project.
Created By	Indicates the user that created the Event.
Verified	Items can be either created directly in the Knowledge Library, or pushed from individual projects. Items pushed from projects will appear here as unverified, and will not show up as Smart Suggestion options in other projects until verified.
Delete	Deletes the Event from the register and from any assigned instances in schedules.

	CPM SCHEDULES		ACTIVITY PRODUCTIVITY RATES		KNOWLEDGE TAGS		CALENDARS		REGISTER	RESOURCES		MACHINE LEARNING	
	Events Register	Register Types	Matrix Definition										
Event Id	Title	Type	Description	%	Dur	\$	Score	Mitigation	Status	Activities	Created By	Verifi...	
O1111	Opportunity ...	General ▶	Opportunity of opp due to 1 resulting in 2					📄 Test desc...	Closed ▶		robin martin	🔌	⊗
R105	Test	Threat ▶	Test	Very High ▶	Very High ▶	Very High ▶	25	📄 qzqdhfg	Mitigated ▶		Jonathan Bo...	🔌	⊗
R114	New New	Schedule Ch...	New New					📄 M5	Mitigated ▶	1	Srinivasa Bh...	🔌	⊗
R114.2	New New	Threat ▶	New New	Very High ▶	Very High ▶	Very High ▶	25	📄 new	Unmitigated ▶	1	Kim Scott	🔌	⊗
R122	Regression T...	Threat ▶	This is going to be used for the regression testing team test effort today. Let's take a look at these mitigation modals and risks to see if this will be useful to the customer. aljsdfajlsdfljdsfdl a sfjasid flajsof flajsof alisdf alsidf alciof laisof lajsof iaj flajis dclflja clclflja lsdqlflasof adslfjalcskljfascklf a sofff asdff asddj fa jsdlfaj sofff acslf aljo flajsof ai sjtfsajd fa soff asd fsa sd as ss ss ss ss ssssssss	Very High ▶	Very High ▶	High ▶	25	📄	Unmitigated ▶		Kim Scott	🔌	⊗
R14	Risk from Co...	Threat ▶	Risk from Cost risk Desc	Very High ▶	Very High ▶	Very Low ▶	25	📄 mit	Unmitigated ▶		Srinivasa Bh...	🔌	⊗
R42	Threat 5	Threat ▶	Threat 5	Very High ▶	Very High ▶	Very High ▶	25	📄	Unmitigated ▶		Tatyana Pust...	🔌	⊗

REGISTER TYPES

Additional Register Types can be defined by selecting the register type tab.

CPM SCHEDULES

ACTIVITY PRODUCTIVITY RATES

KNOWLEDGE TAGS

CALENDARS

REGISTER

RESOURCES

MACHINE LEARNING

Events Register

Register Types

Matrix Definition

Name	Prefix	Probability	Schedule Impact	Cost Impact	Positive Impact	Edit	
Opportunity	O	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		
Idea	I	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
Srini Test	SR	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		
Tatyana Test	TP	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		
Schedule Change Request	S	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
Test 9-16	TP	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>		
Type 1	TP	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
General	GEN	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
Threat	R	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>		
Issue	U	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>		

MATRIX DEFINITION

The tenant level definition of the likelihood and range of impact for both duration and cost a register event has in the cost risk, and schedule review views on risk simulations. These can be adjusted to be project or schedule specific

CPM SCHEDULES

ACTIVITY PRODUCTIVITY RATES

KNOWLEDGE TAGS

CALENDARS

REGISTER

RESOURCES

MACHINE LEARNING

Events Register

Register Types

Matrix Definition

Description	Probability	Schedule Impact	Cost Impact	Color
Very Low	10%	≤ 11 days	≤ \$13	
Low	25%	≤ 30 days	≤ \$10,000	
Medium	50%	≤ 60 days	≤ \$100,000	
High	75%	≤ 90 days	≤ \$1,000,000	
Very High	95%	≤ 180 days	≤ \$10,000,000	

RESOURCES


Resource details such as ID, Name, Category, Default Units, and Costs can be edited in the register. The indent arrows located on the far right of the screen are used to create child resources or to move the resource to a different part of the grid.

CPM SCHEDULES ACTIVITY PRODUCTIVITY RATES KNOWLEDGE TAGS CALENDARS REGISTER RESOURCES MACHINE LEARNING

Resources Categories

ID	Name	Category	Color	UoM	Default Units/d	Cost/Unit	
Kim Test for Keith	Kim Test	Labor		Hours	8.00	1.00	
Robin Tester	Tester	Material		Each	1.00	200.00	
Project resource	project resource	Nonlabor		Each	1.00	75.00	
009	Resource 9	Nonlabor		Each	1.00	0	
Global	Global	New Category		Each	1.00	0	
Srini Import ID	Srini Import Desc	Unique		Each	1.00	0	
Indent	Indent	Labor		Hours	8.00	0	
Tatyana Reg Test	Resurs 009	Supply		Hiver	25.00	5080.00	
SB2		Labor		Hours	8.00	0	
SP	Ski Patrolter	Labor		Hours	8.00	25.00	
No UOM	UOM No	Labor			1.00	0	
Jonny B	Bonny J	Labor		Hours	8.00	0	
Baby Jon	Jonny babe	Labor		Hours	2.00	3.00	
629 Res 1	Res 1	Labor		Hours	8.00	0	
629 Res 2	Res 2	Labor		Hours	8.00	0	
7/12	Resource 3	Labor		Hours	8.00	0	

Resources can be imported from a Microsoft Excel file and also exported, which can then be edited and imported back into the Resources tab.

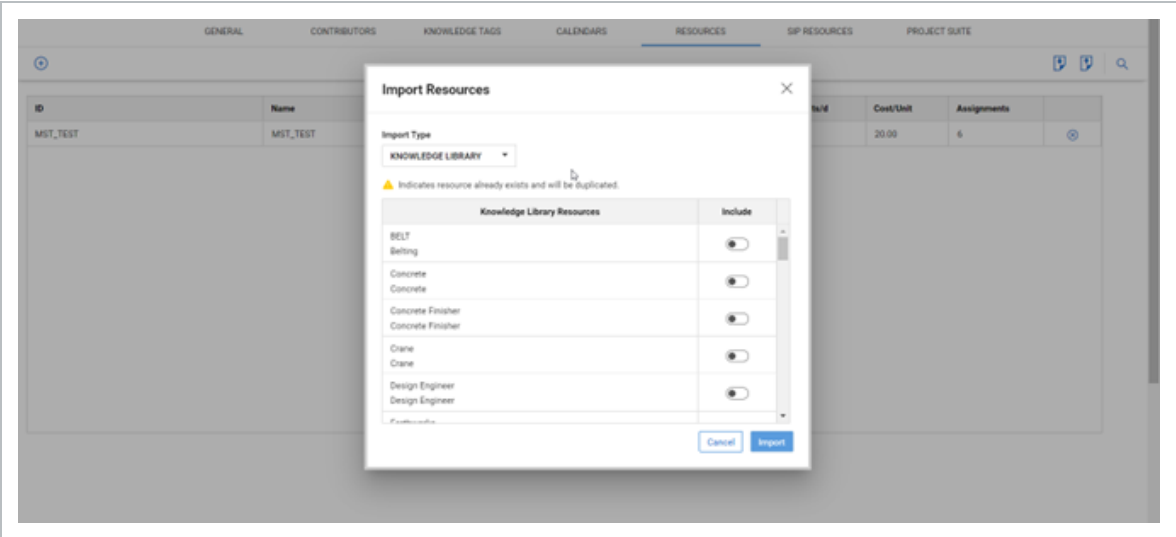

CATEGORIES

Schedule validates the Categories column in the Resources register after it is updated.

NOTE

Only System Administrators can add, edit, or delete Category types.

Category
Labor ✓ ▶
Material ▶
Nonlabor ▶
Installed Equipment ▶
Installed Material ▶
New Category ▶
Labor ▶
Supply ▶
Labor ▶
Labor ▶
Labor ▶
Labor ▶
Labor ▶
Labor ▶
Labor ▶

To modify the categories available, click on the Categories section of the Knowledge Library Resource register.

CPM Schedules

Activity Productivity Rates

Knowledge Tags

Register

Resources

Machine Learning

Resources

Categories

Search

EXPORT

IMPORT

ADD RESOURCE

Name	Description	Category	Unit	Default Units/d	Cost/Unit	Assignments	Delete
ECR110	Crane 110 Ton	Equipment	Hour	8	224	0	

CPM SCHEDULES

RESOURCES

MACHINE LEARNING

+


Resources

Categories

Name	
Labor	
Material	
Nonlabor	
Installed Equipment	
Installed Material	
New Category	
Ny kategori 1	
Supply	
Supply Non	
Unique	

To add a category, click the **Add Category** button.

Type in a new category name. Click **Add** to complete the action.

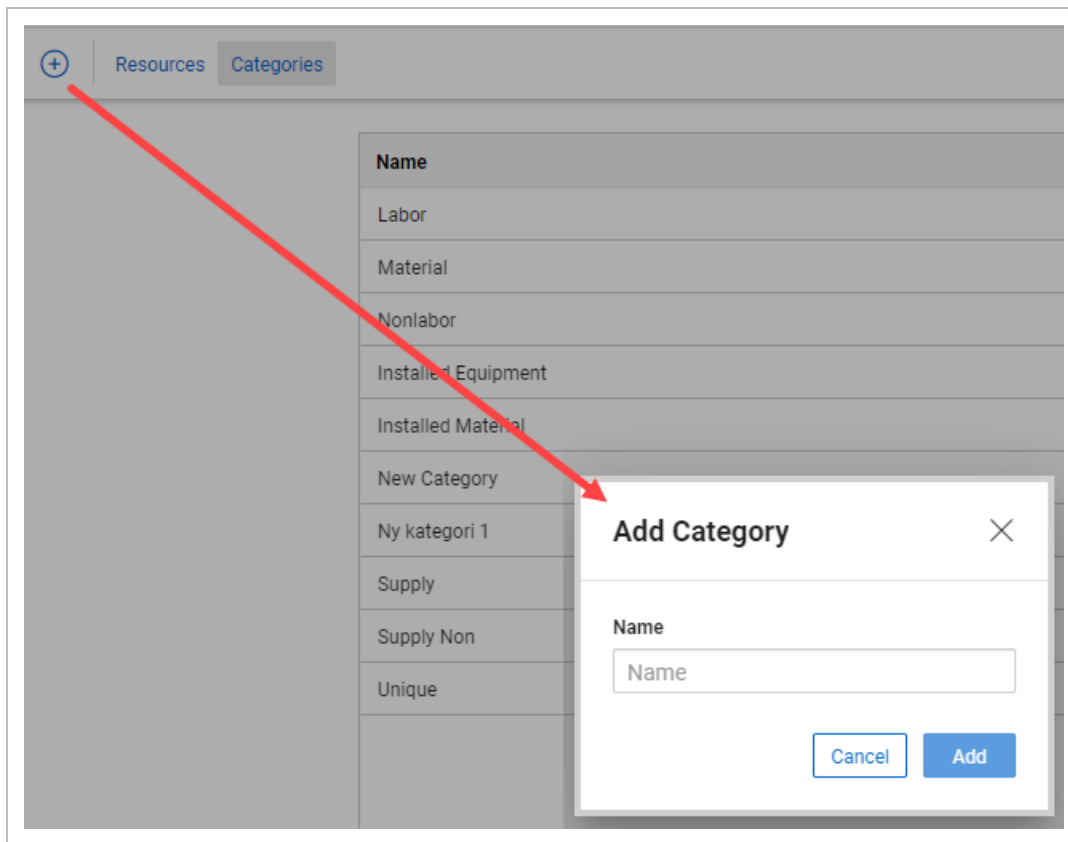

To edit a category name, click directly into the name field of the category to be modified.

If a category needs to be deleted, select the icon in the delete column.

NOTE If you are using Estimate or Control, these categories also match the default categories.

MACHINE LEARNING

Machine learning lets inference engine suggestions be automatically tuned and calibrated by the chosen selection.

CPM SCHEDULES

ACTIVITY PRODUCTIVITY RATES

KNOWLEDGE TAGS

CALENDARS

REGISTER

RESOURCES

MACHINE LEARNING

Enable Machine Learning

Schedule Machine Learning allows Inference Engine suggestions to be automatically tuned and calibrated by the selections you choose. The relative influence of each part that makes up a suggestion is detailed below.

Description

+12%

Duration

+3%

Parent Description

0%

Phase

+9%

Project Codes

-1%

Project Code Values

0%

SET UP RESOURCES

- 1. Open the Knowledge Base and then go to the Resources tab.

Acme Corp

CPM SCHEDULES

ACTIVITY PRODUCTIVITY RATES

KNOWLEDGE TAGS

CALENDARS

REGISTER

RESOURCES

MACHINE LEARNING

Resources

Categories

ID	Name	Category	Color	UoM	Default Units/d	Cost/Unit	
Kim Test for Keith	Kim Test	Labor		Hours	8.00	1.00	
Robin Testler	Tester	Material		Each	1.00	200.00	
Project resource	project resource	Nonlabor		Each	1.00	75.00	
009	Resource 9	Nonlabor		Each	1.00	0	
Global	Global	New Category		Each	1.00	0	

2. In the Resources Register, select the **Add Resource** button to establish a new resource.

Resources

Categories

CPM SCHEDULES ACTIVITY PRODUCTIVITY RATES KNOWLEDGE TAGS CALENDARS REGISTER **RESOURCES** MACHINE LEARNING

ID	Name	Category	Color	UoM	Default Units/d
Kim Test for Keith	Kim Test	Labor ▶	●	Hours	8.00
Robin Tester	Tester	Material ▶	●	Each	1.00
Project resource	project resource	Nonlabor ▶	●	Each	1.00
009	Resource 9	Nonlabor ▶	●	Each	1.00

- A dialog box opens.

Add Resource

ID

ID

Name

Name

Category

Labor ▼

Unit

Hours

Default Units/d

8

Cost/Unit

0

Color assignment

● ● ● ● ● ● ● ●

● ● ● ● ● ● ● ●

view more colors

Cancel

Add

Field	Definition
Name	Recognizable resource name or abbreviation schedulers reference when selecting resources from the register
Description	Extended description or full title of the resource
Category	Resource type classification such as Labor, equipment, and material.

Field	Definition
Unit	The resource's unit of measure
Default Units/d	Daily unit production/completion rate
Cost/Unit	Cost per unit

3. Enter in the resource details and then click **Add** when complete.

Add Resource

ID

754

Name

Electric

Category

Material

Unit

Each

Default Units/d

1

Cost/Unit

0

Color assignment

view more colors

Cancel

Add

- The new resource is added to the Resource register

CPM SCHEDULES ACTIVITY PRODUCTIVITY RATES KNOWLEDGE TAGS CALENDARS REGISTER RESOURCES MACHINE LEARNING							
Resources Categories							
ID	Name	Category	Color	UoM	Default Units/d	Cost/Unit	
754	Electric	Material		Each	1.00	0	
L61	Concrete (Labor)	Labor		Hours	8.00	100.00	
120838	Ubct Partnership	Labor		Hours	8.00	100.00	
NL-07-B Earthworks	NL-07-B (Mat) Constr ~ Earthworks	Installed Material		Square Meter	22.00	100.00	

NOTE

To edit a resource, click directly into the specific field of that resource in the register.

To delete a resource, click the icon in the Delete column.

4. Click the header of the column to sort by to sort resources by field.

- Clicking the header initially sorts ascending/A-Z
- Clicking the header a second time sorts descending/Z-A
- Clicking the header a third time clears the sort function

IMPORT/EXPORT

In addition to using the Resources register to set up individual resources, you can also import and export resources in bulk.

1. In the Knowledge Library Resource register, click the **Export** button.


- Once selected, an Excel file downloads to your local drive. The file contains the list of resources currently in the organization's Resource register.

	A	B	C	D	E	F	G
1	REQUIRED	Field is required for import					
2	OPTIONAL	Field is optional for import					
3	VALIDATED	Field must match master data available in application					
4	IGNORED	Field not to be populated					
	Notes:						
	1. Create New Resources - To create a new Resource enter valid input for the required fields. Rows that are left blank with required fields will not be entered into Schedule as a new Resource.						
	2. The default Category is Labor						
	3. Colors are defined using predefined set of hexadecimal characters, the default Color is 0066CC						
6	ID	Name	Category	Color	Unit	Default Units Per Day	Cost Per Unit
7	Text	Text	Text: "Labor", "Construction Equi	Text: "0066CC", "800000"	Text	Numeric: > 0	Numeric: > 0
8	256	256		7			
9	Kim Test for Keith	Kim Test	Labor	a5a5a5	Hours	8	1
10	Robin Tester	Tester	Material	D85C57	Each	1	200
11	Project resource	project resource	Nonlabor	D8A6E2	Each	1	75


2. In Excel, populate the columns with additional resources and details.

- Once complete, save the .xlsx file

3. In the Knowledge Library Resource Register, click the **import** icon.

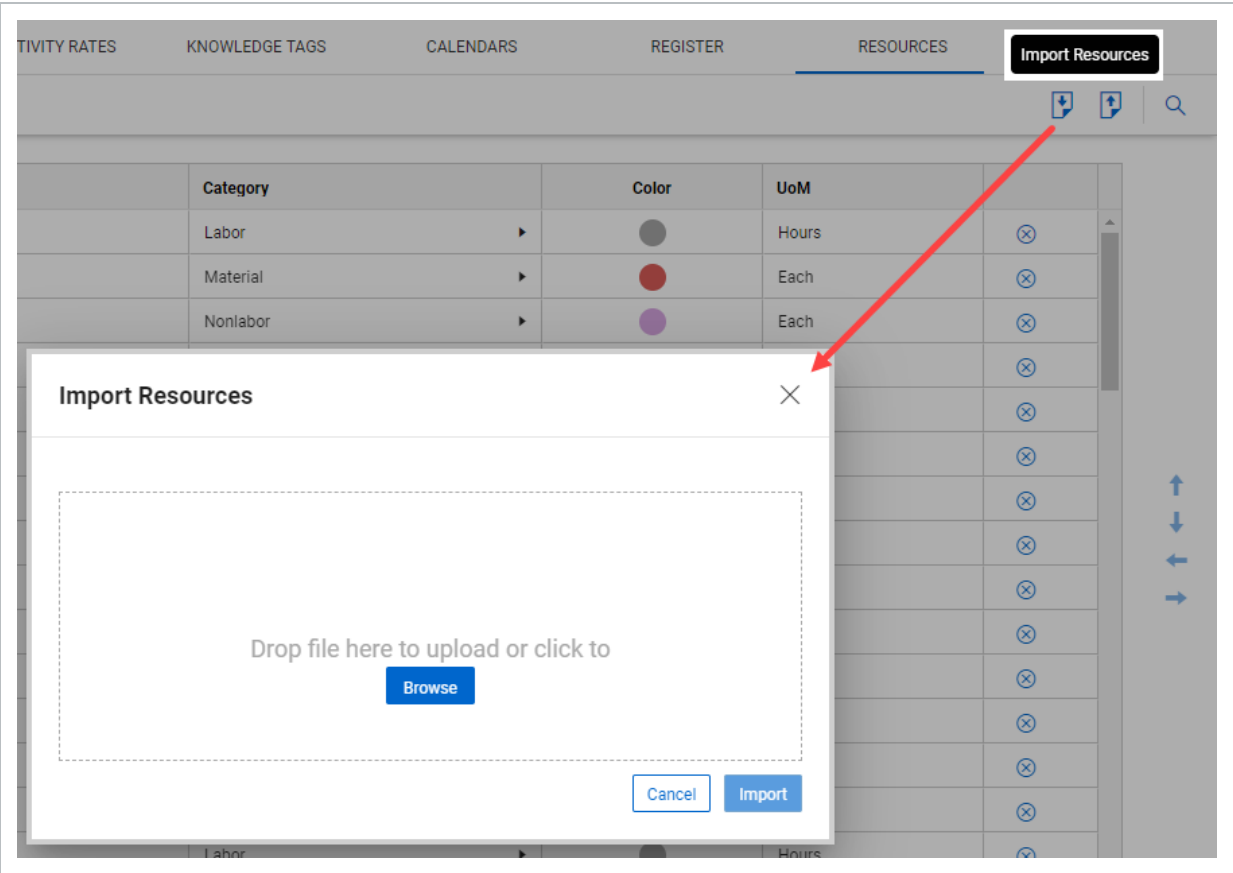

4. A dialog box opens where you select the updated .xlsx file. Select the file, and, click **Open**.

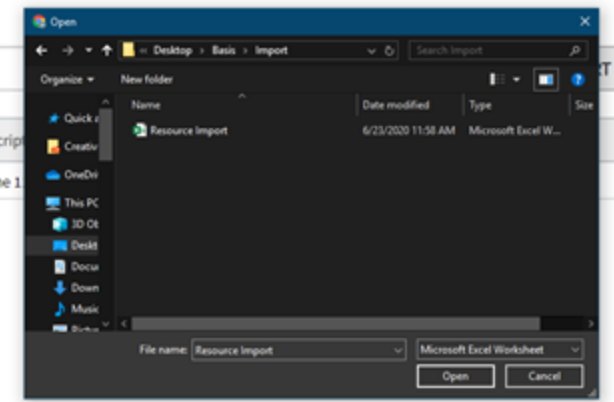


- Schedule processes the data and updates the register with new items and changes.

ID	Name	Category	Color	UoM	Default Units/d	Cost/Unit	
Kim Test for Keith	Kim Test	Labor		Hours	8.00	1.00	
Robin Tester	Tester	Material		Each	1.00	200.00	
Project resource	project resource	Nonlabor		Each	1.00	75.00	
009	Resource 9	Nonlabor		Each	1.00	0	
Global	Global	New Category		Each	1.00	0	
Site Import ID	Site Import Desc	Unique		Each	1.00	0	

SITE ADMINISTRATION

You can access the Application settings by clicking the **Site Administration** button, and can also be accessed in the upper right corner in a project.

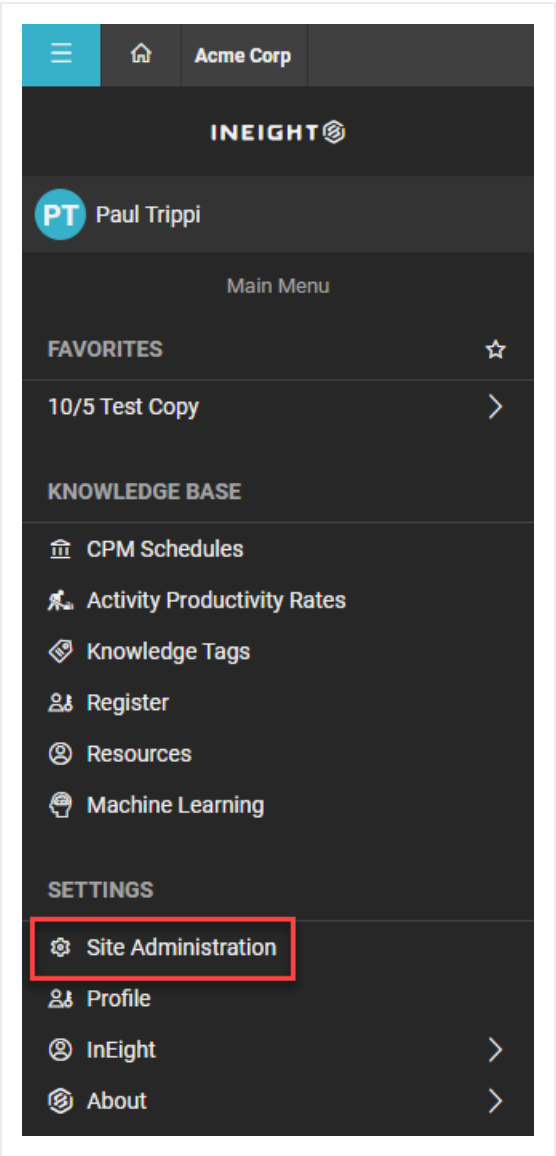

GENERAL SETTINGS

From the General tab, project name, Cost Unit and Allow Project Administrators to invite Non-Schedule Users can be updated.

GENERAL

USERS

Cancel

Save

Name

InEight

249 characters remaining

Cost Unit

\$

Allow Project Administrators to Invite Non-Schedule Users

☐

USERS

You can add both external and internal users to the project. You can also remove users or update their access levels.

GENERAL

USERS


	Name ↑	Email	Status	Permissions	Projects
	<div></div>	<div></div>	<div>(All)</div>	<div>(All)</div>	<div></div>
<input type="checkbox"/>	aananthan	aan_@pkglobal.com	Active	Project Member	9
<input type="checkbox"/>	Aaquibulla	Aaquibulla_@INEIGHT.COM	Active	Project Member	6
<input type="checkbox"/>	Aaron Julien	Aaron_@INEIGHT.COM	Active	Project Member	2
<input type="checkbox"/>	abdul	abdul_@ineight.com	Active	Project Member	0
<input type="checkbox"/>	abdulghani	abdulghani_@ineight.com	Active	Administrator, Knowledge Base Administrator, Schedule Creator, Project Member	2
<input type="checkbox"/>	Adam	Adam_@INEIGHT.COM	Active	Project Member	0
<input type="checkbox"/>	Adesh	Adesh_@INEIGHT.COM	Active	Project Member	3

LESSON 4 – PROJECT CREATION

IMPORT A SCHEDULE

IMPORTING A SCHEDULE

1. From the Schedule home page, click the **Import** icon.

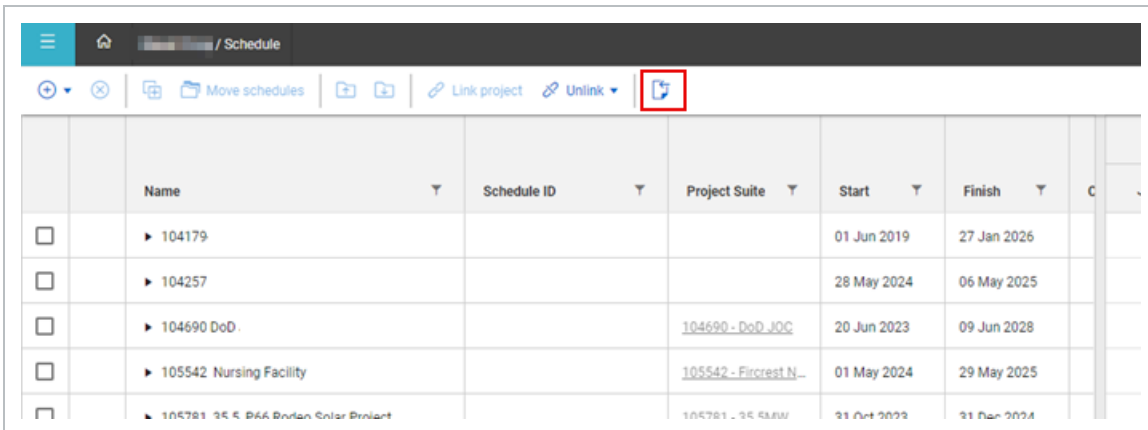

	Name	Schedule ID	Project Suite	Start	Finish	C
<input type="checkbox"/>	▶ 104179			01 Jun 2019	27 Jan 2026	
<input type="checkbox"/>	▶ 104257			28 May 2024	06 May 2025	
<input type="checkbox"/>	▶ 104690 DoD		104690 - DoD JOC	20 Jun 2023	09 Jun 2028	
<input type="checkbox"/>	▶ 105542 Nursing Facility		105542 - Fincrest N...	01 May 2024	29 May 2025	
<input type="checkbox"/>	▶ 105781 35 E D&K Brian Solar Brilliant		105781 - 35 E D&K	21 Oct 2022	21 Mar 2024	

2. Select a folder on your computer or external source, and then drag and drop the schedule to upload into the Schedule import dialog box.
3. Enter a schedule ID and schedule name. Select a project workspace and folder from the drop-down lists.

Schedule import

×

Select a Primavera XER or MS Project file to be imported as either a New Schedule or as Knowledge to be stored in the Knowledge Base

↑

Drag and drop file here to upload

Only .XER, .MPP files are allowed. (Max file size: 60mb)

Select Files...

Drop files here to select

Schedule ID

Schedule Name

Project Workspace

Folder

Cancel

Import

4. Click **Import**.


Page 72 of 291

InEight Inc. | Release 25.1


EXPORT A SCHEDULE

EXPORTING A SCHEDULE

1. In Plan view, click the **Export** icon at the top right of the page.

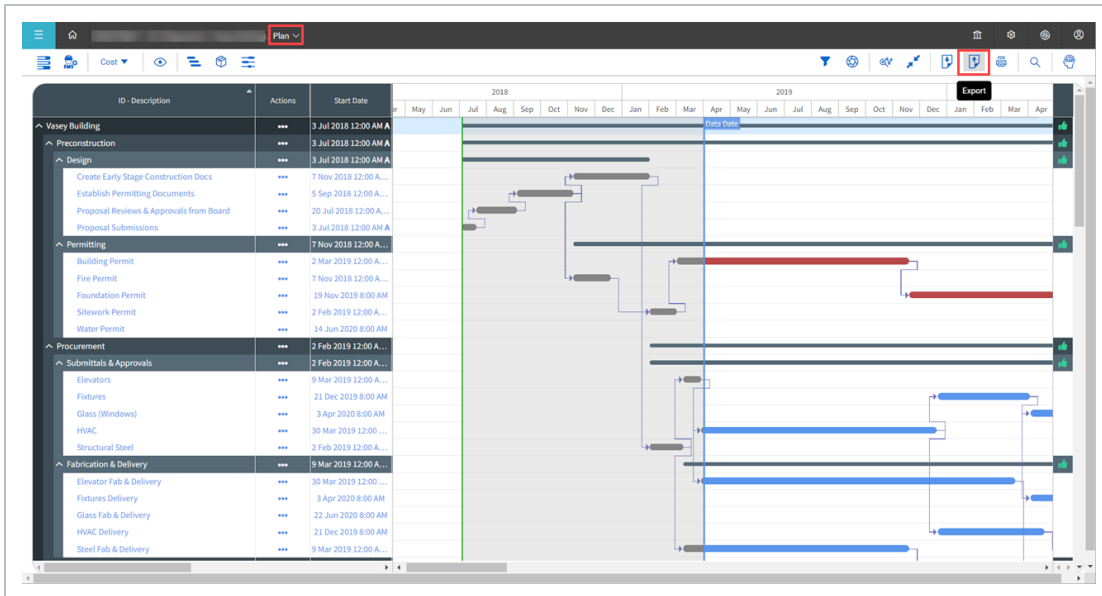

2. Select the export type from the Export Type drop-down options. Click **Export**.

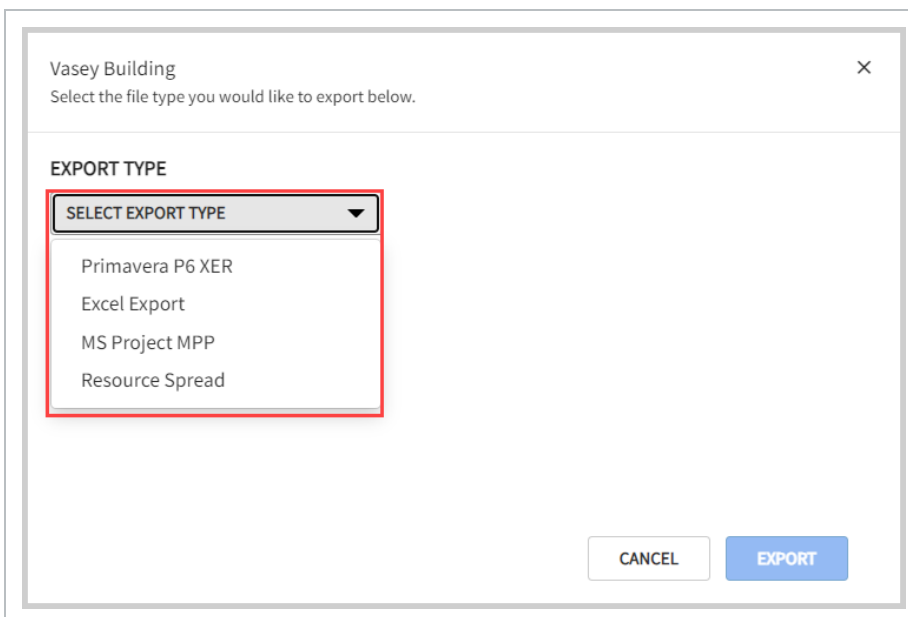


The export file is downloaded to your browser's download folder.

CREATE A SCHEDULE FROM SCRATCH

When you create a new schedule, there are two key sections to fill out: Details and Outline.

To start, click **Add New Schedule** in the Schedule register. This opens a window so that you can begin to fill out the schedule details.

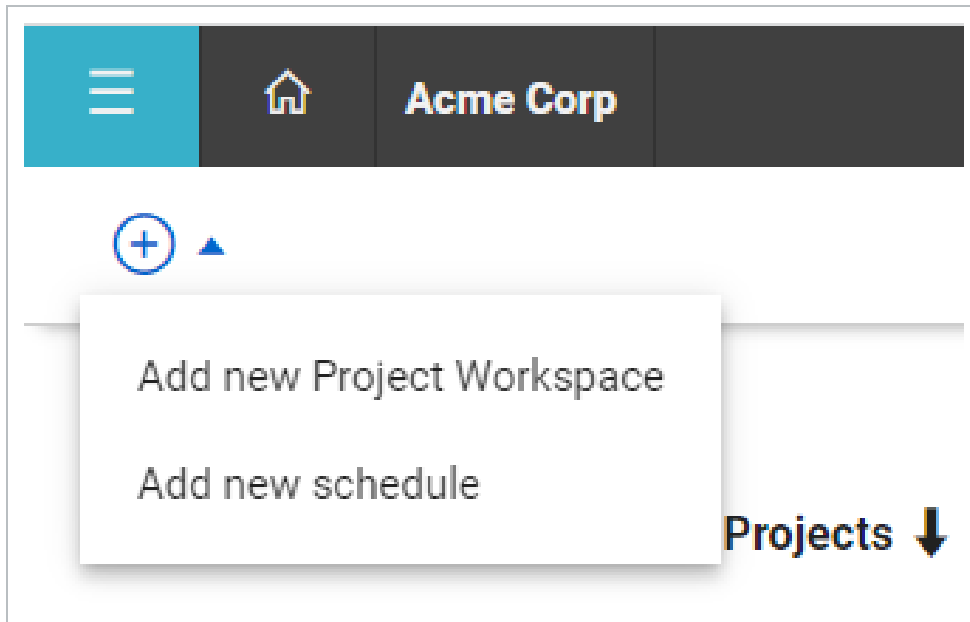

DETAILS

The Details section is the first stage for creating a new schedule.

Add a new schedule

Details

Context

Outline

Schedule ID

SCHED

Schedule Name

PT1

Project Workspace

22.10 Brian Group

Start Date

8 Dec 2022

NEXT


In the details section, complete the following information:

Field	Description
Schedule ID	Unique ID used for schedule identification.
Schedule Name	Official name of the schedule.
Project Workspace	Grouping of multiple schedules.
Start Date	Date the project starts.

Select **Next**.

CONTEXT

The second stage in creating a schedule is Context. Context lets you select existing project codes and UDFs to apply on a newly created schedule. These selections help with Knowledge Base suggestions throughout the Schedule application.

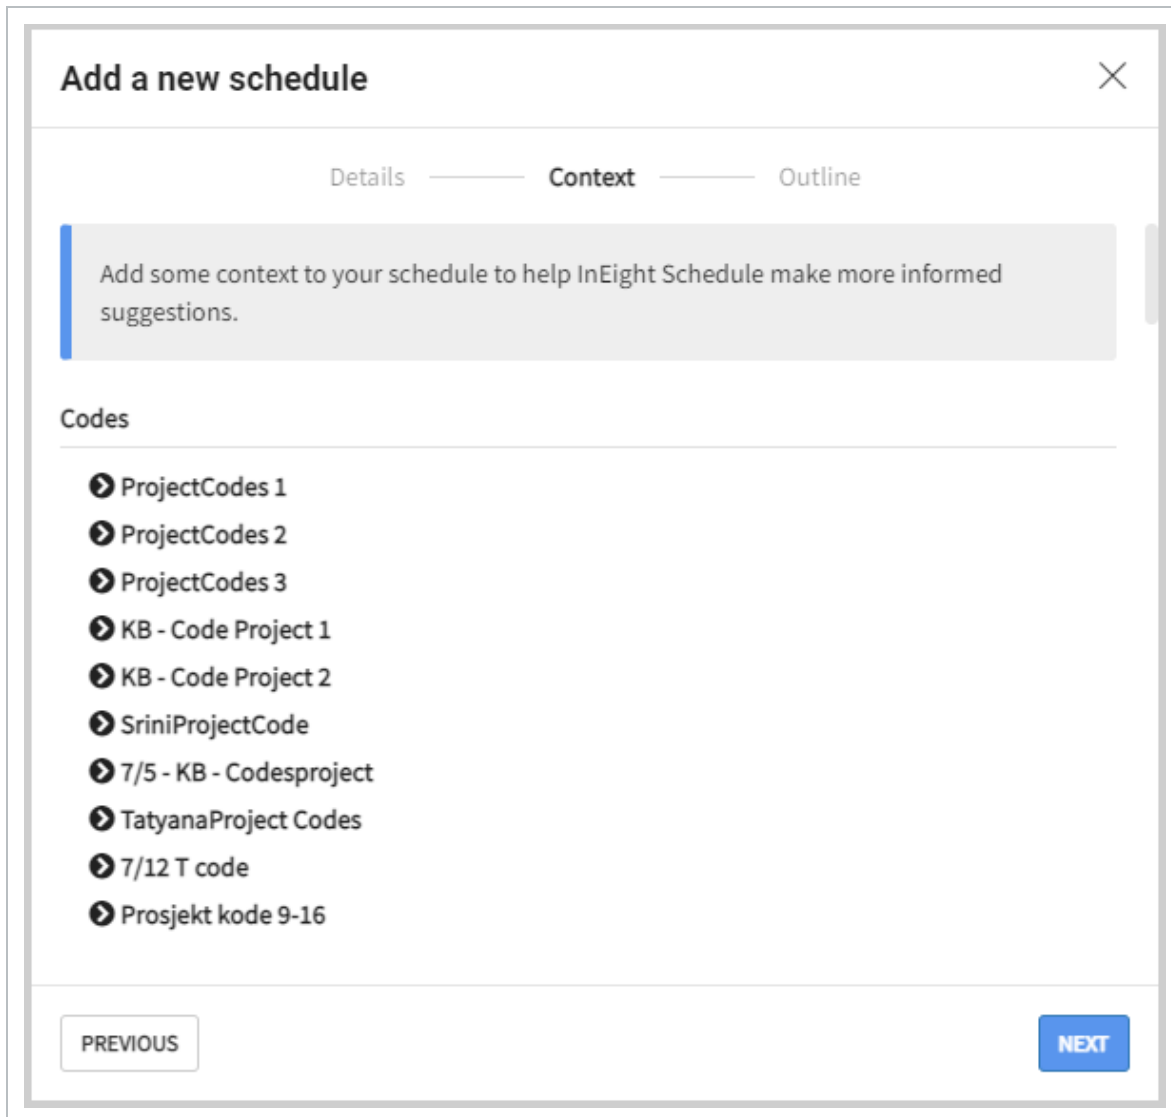

The screenshot shows a dialog box titled "Add a new schedule" with a close button (X) in the top right corner. Below the title bar, there are three tabs: "Details", "Context" (which is selected and highlighted), and "Outline". A light gray instruction box with a blue vertical bar on the left contains the text: "Add some context to your schedule to help InEight Schedule make more informed suggestions." Below this, under the heading "Codes", there is a list of ten project codes, each preceded by a right-pointing arrow icon. At the bottom of the dialog, there are two buttons: "PREVIOUS" on the left and "NEXT" on the right.

Add a new schedule [X]

Details — **Context** — Outline

Add some context to your schedule to help InEight Schedule make more informed suggestions.


Codes

- ProjectCodes 1
- ProjectCodes 2
- ProjectCodes 3
- KB - Code Project 1
- KB - Code Project 2
- SriniProjectCode
- 7/5 - KB - Codesproject
- TatyanaProject Codes
- 7/12 T code
- Prosjekt kode 9-16

PREVIOUS NEXT

OUTLINE

The third stage in creating a schedule is Outline. In this section, you select an existing Knowledge Library Schedule as reference for the new schedule being built.

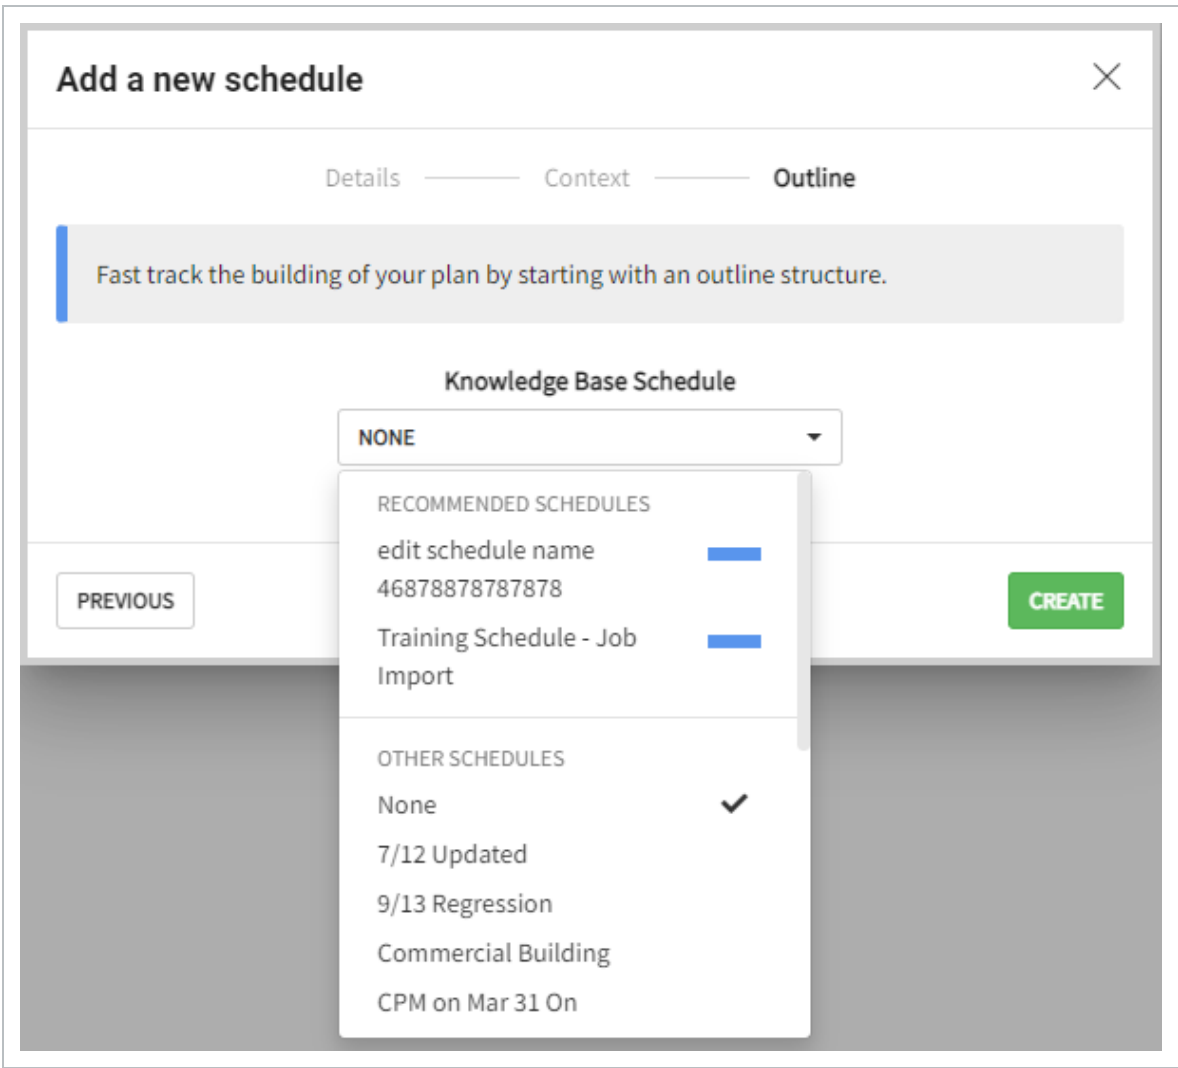

Select a schedule to bring in the work package structure from the Knowledge Base project.

Add a new schedule

Details — Context — **Outline**

Fast track the building of your plan by starting with an outline structure.

Knowledge Base Schedule

COMMERCIAL BUILDING

Include Risk Register

Include Levels

ALL

Commercial Building

Preconstruction

Procurement

Construction

Closeout

Summary

Include


PREVIOUS

CREATE


You can select all or parts of the structure levels to use in the schedule being created. This is done by selecting a level from the Include Levels drop-down or by manually toggling work packages in the Include column.

NOTE

Turning off a Superior work package will turn off its subordinates.

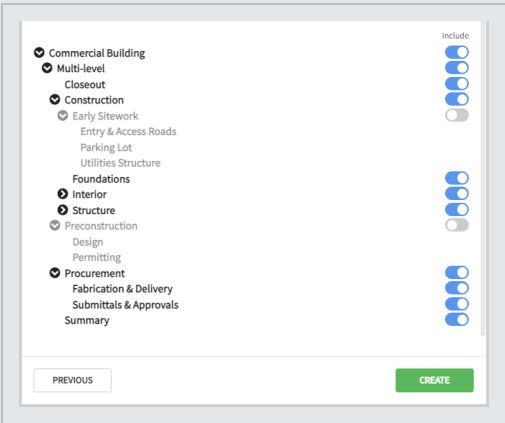

Also, the include Risk Register toggle lets you specify whether to include risks, and if so, the level of risk to include.




Any risks assigned to the Knowledge Library schedule are brought into the new schedule. Include Risk Register brings in the risk register items from the Knowledge Library Schedule into the new schedule.

NOTE

The available risk levels are configured at the organization level.


SCHEDULE CONFIGURATION SETTINGS

Schedule settings lets you adjust the data date, switch schedule modes, switch how out of sequence progress is handled. These functions can be accessed via the secondary toolbar at the top of Plan view.



SCHEDULE CONFIGURATION

Schedule Configuration contains the general information and settings for the current project.

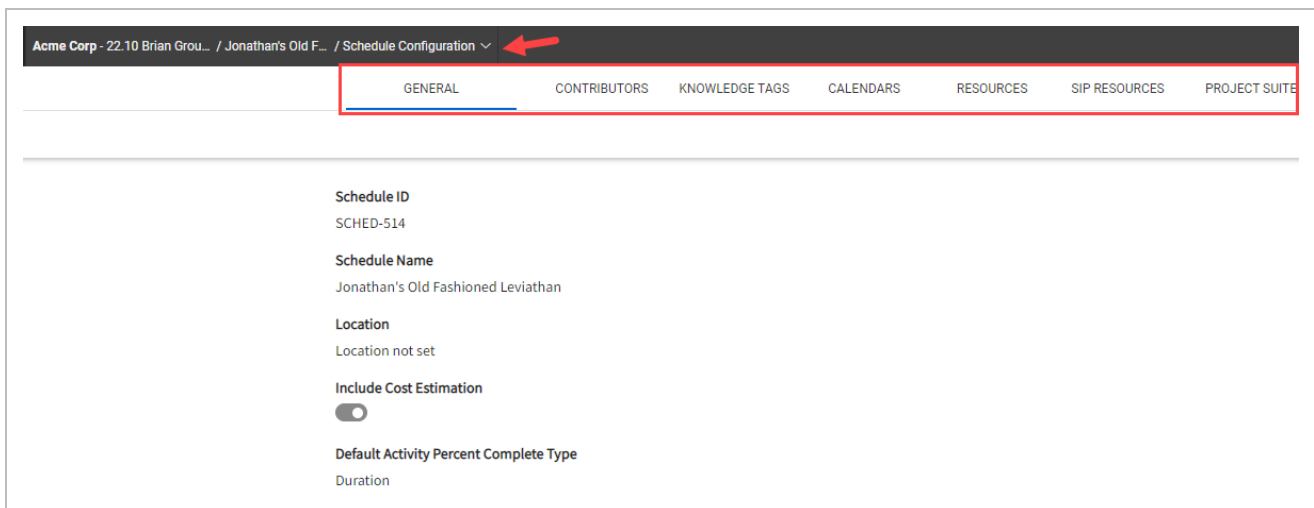

Depending on the tab selected, information and settings pertaining to the tab heading are shown.

Tab	Function/Description
General	Schedule details, such as Project Name, Location, Estimate, Benchmark and work hours.
Contributors	Add, remove, and edit project contributors.
Crews	Set up standard crews for the project.
Knowledge Tags	Manage knowledge tags on the project.
Calendars	Define project calendars and non-workdays.
Resources	Manage project resources.
SIP Resources	Activities from the CPM Schedule show in the Short Interval Planning (SIP) view that are grouped, based on how the Plan view WBS is organized.
Project Suite	Connectivity to other InEight Project Suite Solutions (as needed).

GENERAL

On the General tab, you can configure the project details.

GENERAL
CONTRIBUTORS
KNOWLEDGE TAGS
CALENDARS
RESOURCES
SIP RESOURCES
PROJECT SUITE

Schedule ID
SCHED-512

Schedule Name
Test Schedule

Location
Location not set

Include Cost Estimation
☐

Default Activity Percent Complete Type
Duration

CONTRIBUTORS

On the Contributors tab, both external and internal users can be added to the project. Existing contributors can be removed or have their access level updated.

GENERALCONTRIBUTORSKNOWLEDGE TAGSCALENDARSRESOURCESSIP RESOURCESPROJECT SUITE

Email	Name	Permissions	Steps	Actions
ben@basispm.com	Ben Heights	Markup	0	
david@ineight.com 1 day ago	David	Scheduler Short Interval Planner Markup	0	
Paul@ineight.com	Paul	Short Interval Planner	0	

KNOWLEDGE TAGS

On the Knowledge Tags tab, organizational defined tags can be reviewed, and excluded from consideration by the Schedule inference engine.

GENERALCONTRIBUTORSKNOWLEDGE TAGSCALENDARSRESOURCESSIP RESOURCESPROJECT SUITE

Codes / Project

Codes

Project

Activity

Register Event

Resource

UDFs

Project

WBS

Activity

Register Event





















Resource

Project Codes		
Business Unit / Region		
Default for Scheduled Svcs		
Development		
Development Manager		
MAdshead		
Major Projects		
Project Lead Planner / Scheduler		

CALENDARS

On the Calendars tab, additional calendars can be created, working days can be edited, and a default calendar can be defined. This is also where holidays are defined.

GENERALCONTRIBUTORSKNOWLEDGE TAGSCALENDARSRESOURCESSIP RESOURCESPROJECT SUITE

★	Calendar	Hours/d...	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Exceptions	Actions
●	724 Su-Sa 12:00A-12:00A No Hol	24	●	●	●	●	●	●	●	0	 
○	*508 M-F 8:00A-5:00P US Hol	8	○	●	●	●	●	●	○	1431	 
○	0.Standard 5 Day w/ Hol	8	○	●	●	●	●	●	○	1377	 
○	24 hours / 7 days	24	●	●	●	●	●	●	●	9	 
○	24x7 w/ Turtle Season	24	●	●	●	●	●	●	●	6642	 
○	24x7 w/ Turtle Season	24	●	●	●	●	●	●	●	6642	 
○	510 M-F No Holidays	10	○	●	●	●	●	●	○	477	 
○	510 Su-Th 7:00A-5:00P No Hol	10	●	●	●	●	●	○	○	477	 
○	7d-24h (no holidays continuous)	24	●	●	●	●	●	●	●	0	 
○	KOS G 5d x 10hr w Holidays	10	○	●	●	●	●	●	○	657	 

RESOURCES

On the Resources tab, additional resources can be added and searched. Resource details such as ID, Name, Category, Unit, Default Units, and Costs can be edited in the grid by double-clicking the cell. Use the indent arrows on the right to create a child resource from the selected resource or to move the resource to a different part of the grid.


GENERALCONTRIBUTORSKNOWLEDGE TAGSCALENDARSRESOURCESSIP RESOURCESPROJECT SUITE

ID	Name	Category	Color	UoM	Default Units/d	Cost/Unit	Assignments	
*EXPT	Export Vessel	Labor	●	Hours	80.00	500000.00	1	⊖
*SURV	Survey Vessel	Labor	●	Hours	80.00	500.00	2	⊖
*FLAY	Flowline Vessel	Labor	●	Hours	80.00	100000.00	1	⊖
SPL-1	Subsea Package Lead - Doiron	Labor	●	Hours	80.00	1.00	47	⊖
SPL-2	Subsea Package Lead - Pyron	Labor	●	Hours	80.00	1.00	167	⊖
SPL-3	Subsea Package Lead - Timte	Labor	●	Hours	80.00	1.00	81	⊖
SPL-4	Subsea Package Lead - Gaston	Labor	●	Hours	80.00	1.00	40	⊖
SPL-5	Subsea Package Lead - Blochhus	Labor	●	Hours	80.00	1.00	36	⊖
SPL-6	Subsea Package Lead - Anderson	Labor	●	Hours	80.00	1.00	17	⊖
SPL-8	Subsea Package Lead - Blockhus	Labor	●	Hours	80.00	1.00	4	⊖
SPL-9	Subsea Package Lead - Tavassoli	Labor	●	Hours	80.00	1.00	10	⊖
Nbl Ops & Eng Serv	Noble Operations and Engineering Services	Labor	●	Hours	8.00	0	0	⊖

Use the indent arrows on the right to create a child resource from the selected resource or to move the resource to a different part of the grid.

ID	Name	Category	Color	UoM	Default Units/d	Cost/Unit	
Kim Test for Keith	Kim Test	Labor ▶	●	Hours	8.00	1.00	⊗
Robin Tester	Tester	Material ▶	●	Each	1.00	200.00	⊗
Project resource	project resource	Nonlabor ▶	●	Each	1.00	75.00	⊗
009	Resource 9	Nonlabor ▶	●	Each	1.00	0	⊗
Global	Global	New Category ▶	●	Each	1.00	0	⊗
Srini Import ID	Srini Import Desc	Unique ▶	●	Each	1.00	0	⊗
Tatyana Reg Test	Ressurs 009	Supply ▶	●	Hver	25.00	5080.00	⊗
Indent	Indent	Labor ▶	●	Hours	8.00	0	⊗
SB2		Labor ▶	●	Hours	8.00	0	⊗
SP	Ski Patroller	Labor ▶	●	Hours	8.00	25.00	⊗
No UOM	UOM No	Labor ▶	●		1.00	0	⊗
✓ Jonny B	Bonny J	Labor ▶	●	Hours	8.00	0	⊗
Baby jon	jonny babe	Labor ▶	●	Hours	2.00	3.00	⊗
629 Res 1	Res 1	Labor ▶	●	Hours	8.00	0	⊗
629 Res 2	Res 2	Labor ▶	●	Hours	8.00	0	⊗
7/12	Resource 3	Labor ▶	●	Hours	8.00	0	⊗

Resources can be imported using the Excel or Knowledge Library import type. Use the toggles from the Knowledge Library import to select resources to import.

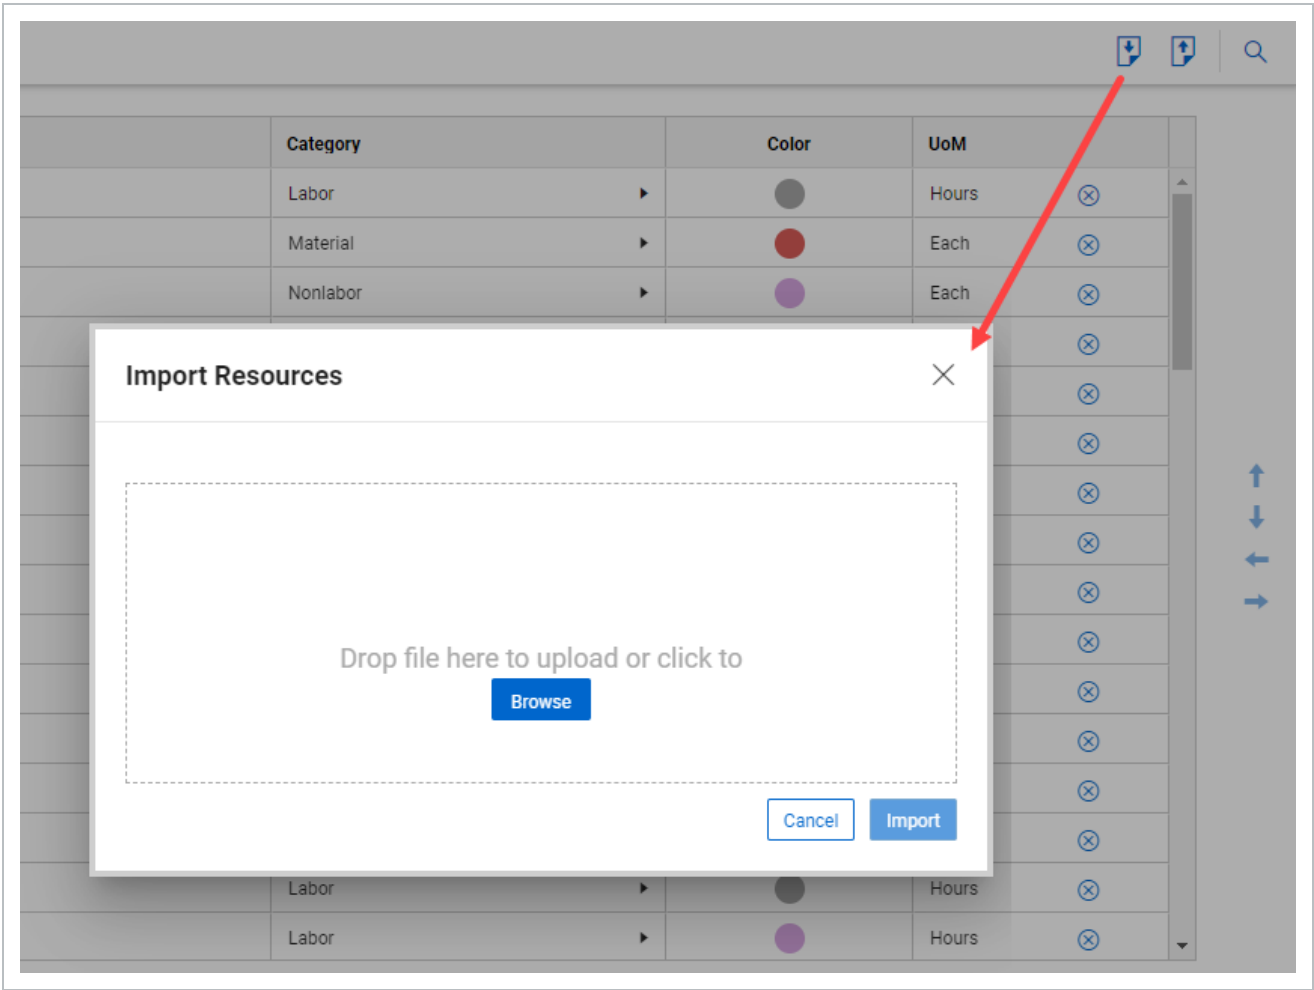

SIP RESOURCES

On the SIP Resources tab, SIP Resources can be created, edited, deleted, and searched. SIP Resources also shows which step each resource is being used.



PROJECT SUITE

GENERAL

CONTRIBUTORS

KNOWLEDGE TAGS


CALENDARS

RESOURCES

SIP RESOURCES

PROJECT SUITE

Select a project to connect to

Type or select...

FERMI Carrying Job

FERMI Carrying Job Int'l Payroll

FERMI LBNF

FMI Lone Star

FN

FORECAST NOTES

FW Hill WRF Tertiary-Pretreat Membranes

FWC - PIIC Micro Piles & Drilled Piers

FWC - Small Cap Jobs

FWC 5B

FWC Arbutus Rd Attenuation Tank - Anchor TESTT...

FWC Big Bar Billing

PRINT VIEW

The Go To Print View button lets you save a printable version to a PDF file and also customize printable output by modifying the settings in the Page Setup and Gantt Setup tabs.

1 active user

24

March 2024

April 2024

May 2024

19

26

04

11

18

25

01

08

15

22

29

06

13

20

27

03

1

Save to PDF

Print settings

2

Page Setup

3

Gantt Setup

Paper Size

Letter (8.5 x 11.0 in)

Orientation

Landscape

Scaling

Default

Header

None

Footer

None

Revert to default

Letter (8.5 x 11.0 in) Landscape - 8 pages

ID - Description	Actions	Start	Finish	At Complet...	September	October 2023				
					18	25	02	09	16	23
EPC - 123	...	20 Dec 2023	18 Apr 2024	87						
WBS SCHED-70.1	...	20 Dec 2023	18 Apr 2024	87						
Activity A1000.1.1	...	20 Dec 2023	29 Jan 2024	29						
Activity A1010	...	30 Jan 2024	8 Mar 2024	29						
Activity A1020	...	11 Mar 2024	18 Apr 2024	29						
WBS SCHED-70.1.1	...	20 Dec 2023	30 Jan 2024	30						
WBS SCHED-70.1.2	...	20 Dec 2023	30 Jan 2024	30						
WBS SCHED-70.1.3	...	20 Dec 2023	30 Jan 2024	30						
WBS SCHED-70.2	...	20 Dec 2023	18 Apr 2024	87						
Activity A1030	...	20 Dec 2023	29 Jan 2024	29						
Activity A1040	...	30 Jan 2024	8 Mar 2024	29						
Activity A1050	...	11 Mar 2024	18 Apr 2024	29						
WBS SCHED-70.2.1	...	20 Dec 2023	30 Jan 2024	30						
WBS SCHED-70.2.2	...	20 Dec 2023	30 Jan 2024	30						
WBS SCHED-70.2.3	...	20 Dec 2023	30 Jan 2024	30						
WBS SCHED-70.3	...	20 Dec 2023	18 Apr 2024	87						
Activity A1060	...	20 Dec 2023	29 Jan 2024	29						
Activity A1070	...	30 Jan 2024	8 Mar 2024	29						
Activity A1080	...	11 Mar 2024	18 Apr 2024	29						

PAGE SETUP OPTIONS

The Paper Size drop-down menu lets you choose several different types of paper sizes.

Print settings

Page Setup

Gantt Setup

Paper Size

Letter (8.5 x 11.0 in)

Letter (8.5 x 11.0 in)

Legal (8.5 x 14.0 in)

Tabloid (11.0 x 17.0 in)

ANSI C (17.0 x 22.0 in)

ANSI D (22.0 x 34.0 in)

ANSI E (34.0 x 44.0 in)

ARCH A (9.0 x 12.0 in)

ARCH B (12.0 x 18.0 in)

ARCH C (18.0 x 24.0 in)

ARCH D (24.0 x 36.0 in)

ARCH E (36.0 x 48.0 in)

ARCH E1 (30.0 x 42.0 in)

ISO A0 (841 x 1189 mm)


ISO A1 (594 x 841 mm)

ISO A2 (420 x 594 mm)

ISO A3 (297 x 420 mm)

ISO A4 (210 x 297 mm)

The Orientation drop-down menu lets you choose between a landscape or a portrait orientation.



Scaling for the PDF can be set at High, Default, Low or Very low settings.

Print settings

Page Setup

Gantt Setup

Paper Size

Letter (8.5 x 11.0 in)

Orientation

Landscape

Scaling

Default

High


Default

Low


Very Low

All pages

The header drop-down menu lets you add headers to the PDF.

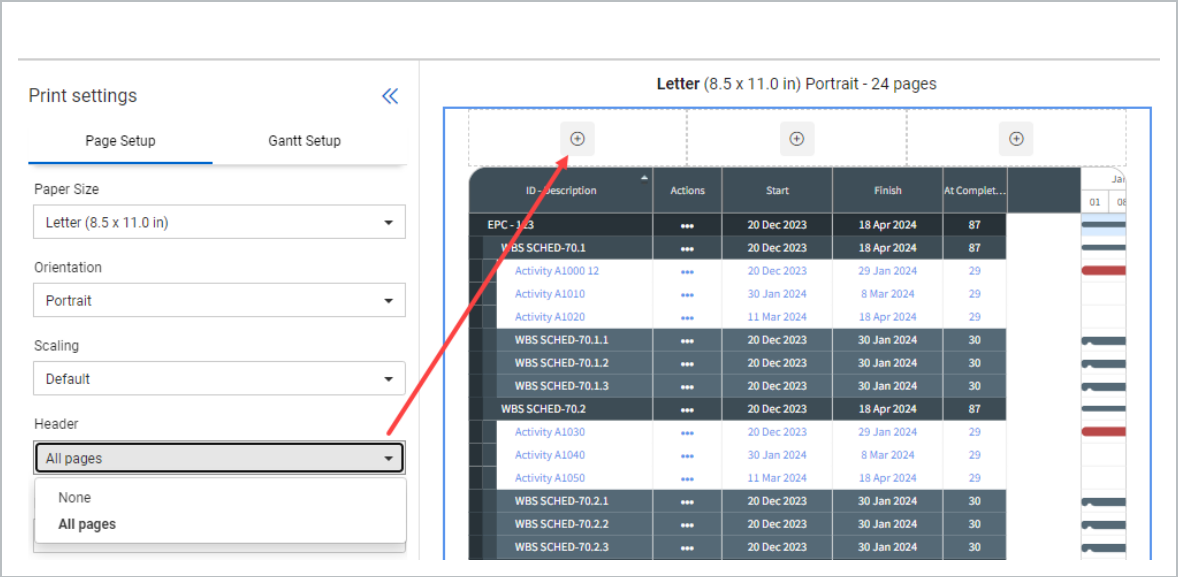

Select one of the three header add icons to insert one of the header content types from the drop-down menu.

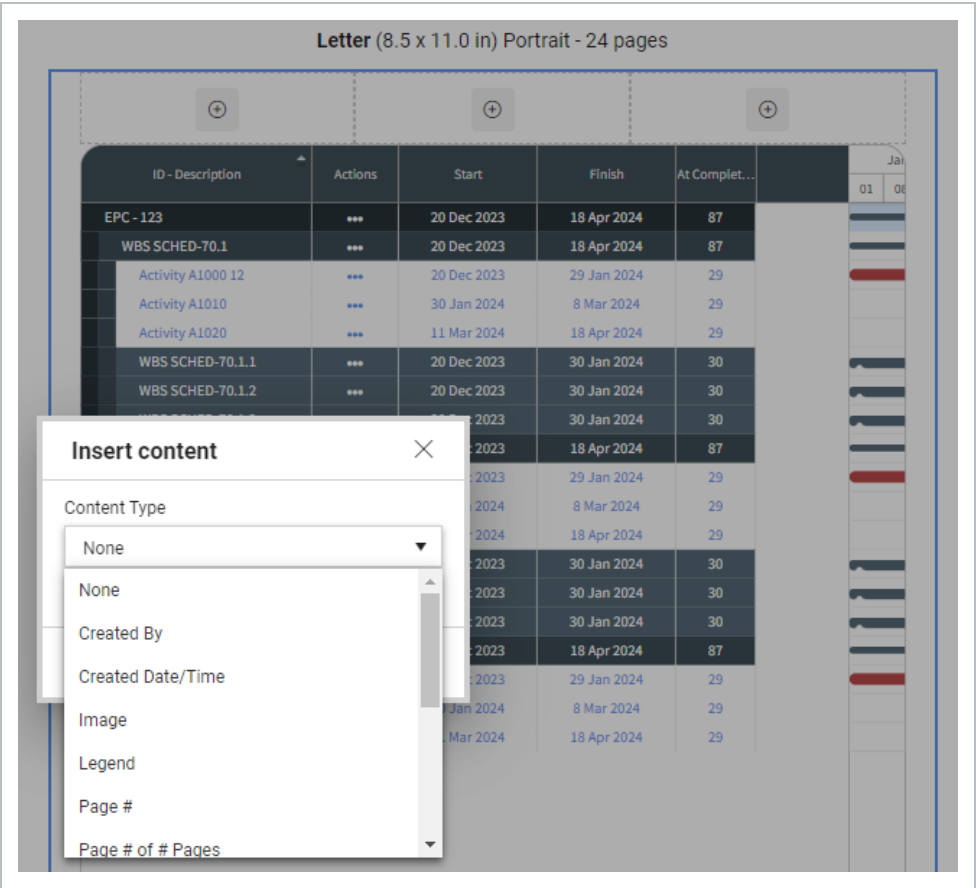

The footer drop-down menu lets you add footers to the PDF.

Print settings

Page Setup

Gantt Setup

Paper Size

Letter (8.5 x 11.0 in)

Orientation

Portrait

Scaling

Default

Header

All pages

Footer

All pages

None

All pages


Revert to default

Letter (8.5 x 11.0 in) Portrait - 24 pages

Schedule ID: SCHED-70

ID - Description	Actions	Start	Finish	At Complet...	
EPC - 123	...	20 Dec 2023	18 Apr 2024	87	
WBS SCHED-70.1	...	20 Dec 2023	18 Apr 2024	87	
Activity A1000.12	...	20 Dec 2023	29 Jan 2024	29	
Activity A1010	...	30 Jan 2024	8 Mar 2024	29	
Activity A1020	...	11 Mar 2024	18 Apr 2024	29	
WBS SCHED-70.1.1	...	20 Dec 2023	30 Jan 2024	30	
WBS SCHED-70.1.2	...	20 Dec 2023	30 Jan 2024	30	
WBS SCHED-70.1.3	...	20 Dec 2023	30 Jan 2024	30	
WBS SCHED-70.2	...	20 Dec 2023	18 Apr 2024	87	
Activity A1030	...	20 Dec 2023	29 Jan 2024	29	
Activity A1040	...	30 Jan 2024	8 Mar 2024	29	
Activity A1050	...	11 Mar 2024	18 Apr 2024	29	
WBS SCHED-70.2.1	...	20 Dec 2023	30 Jan 2024	30	
WBS SCHED-70.2.2	...	20 Dec 2023	30 Jan 2024	30	
WBS SCHED-70.2.3	...	20 Dec 2023	30 Jan 2024	30	
WBS SCHED-70.3	...	20 Dec 2023	18 Apr 2024	87	
Activity A1060	...	20 Dec 2023	29 Jan 2024	29	
Activity A1070	...	30 Jan 2024	8 Mar 2024	29	
Activity A1080	...	11 Mar 2024	18 Apr 2024	29	

Select one of the three footer add icons to insert one of the footer content types from the drop-down menu.

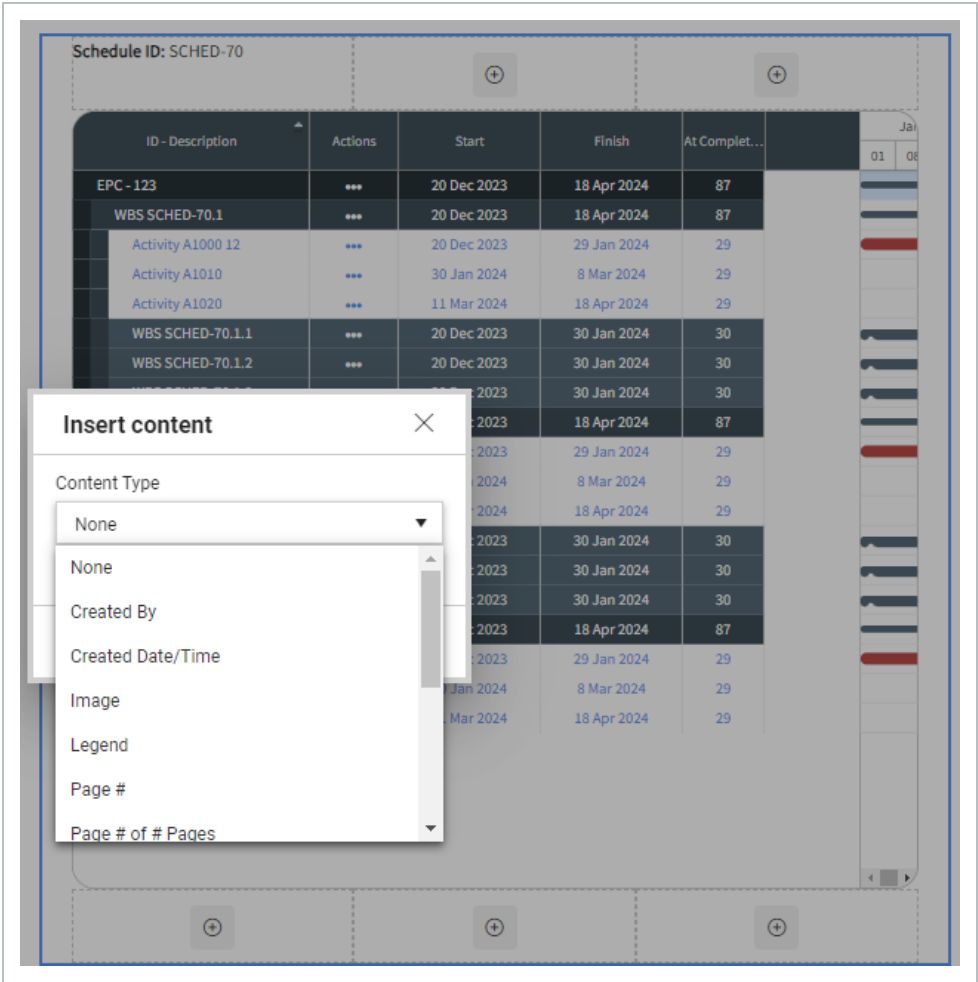

GANTT SETUP OPTIONS

The Gantt Start Date and Gantt End Dates lets you choose beginning and end dates to show on the Gantt chart.

Print settings

Page Setup

Gantt Setup

Gantt Start Date

1 Jan 2024

Gantt End Date

29 Feb 2024


Timescale

Week


Hide Gantt

Histogram


The Timescale drop-down menu lets you select a period of time to show on the Gantt chart.

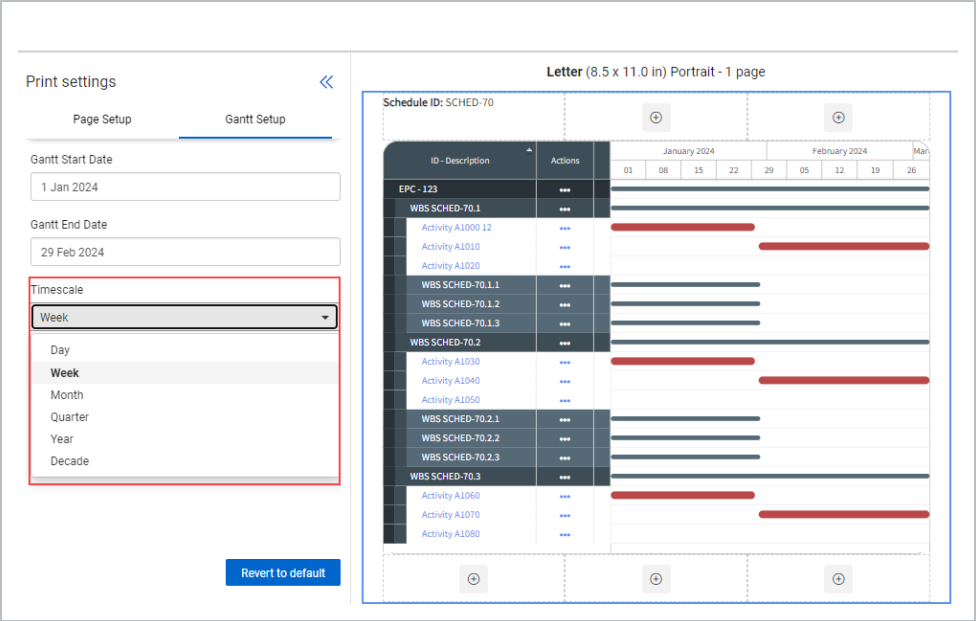


The Hide Gantt toggle lets you hide the Gantt chart from the PDF.

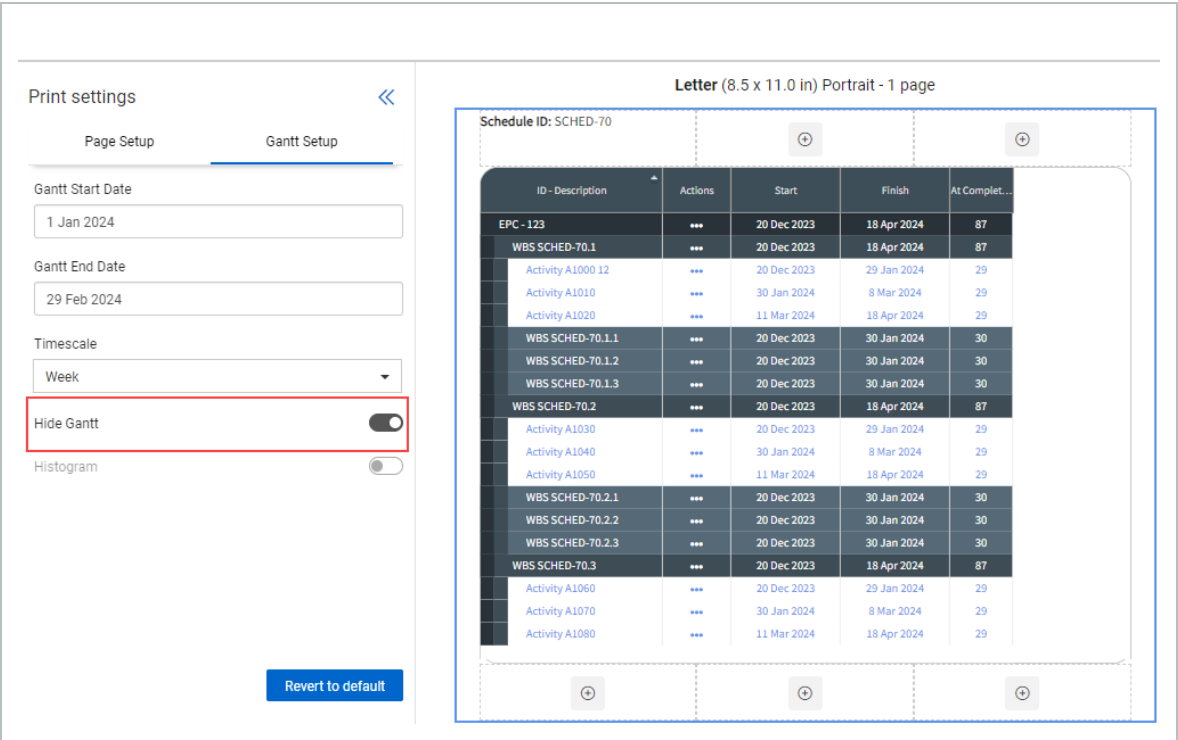

The Histogram toggle controls the display of the histogram in the PDF.

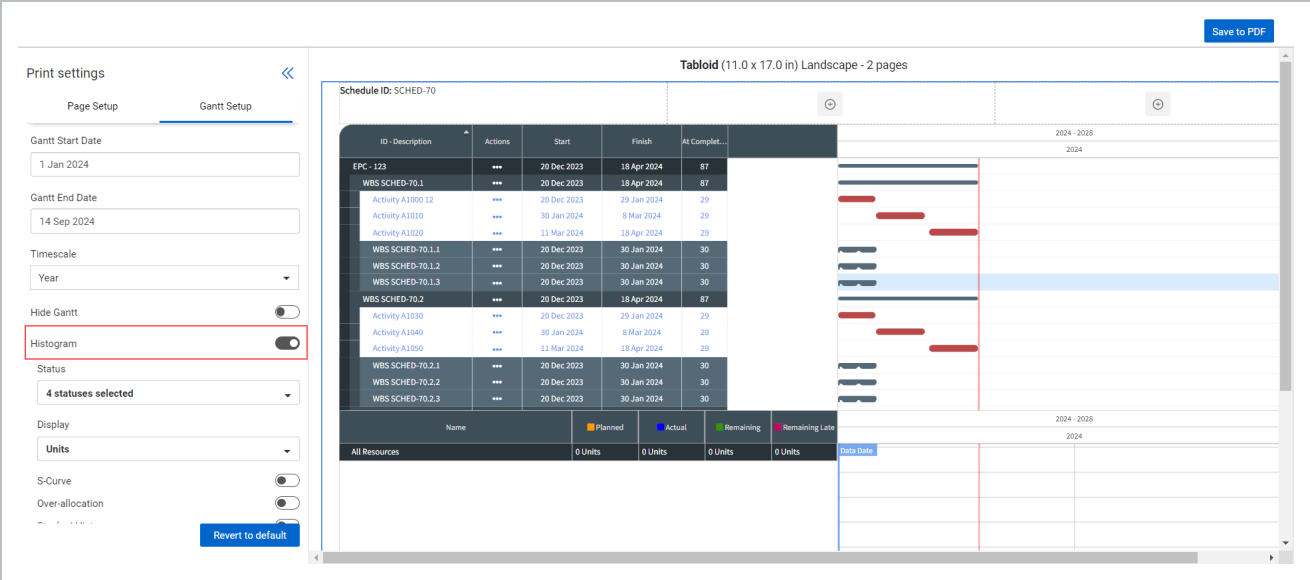

The Status field under Histogram lets you show the Planned, Actual, Remaining and Remaining Late columns in the PDF.

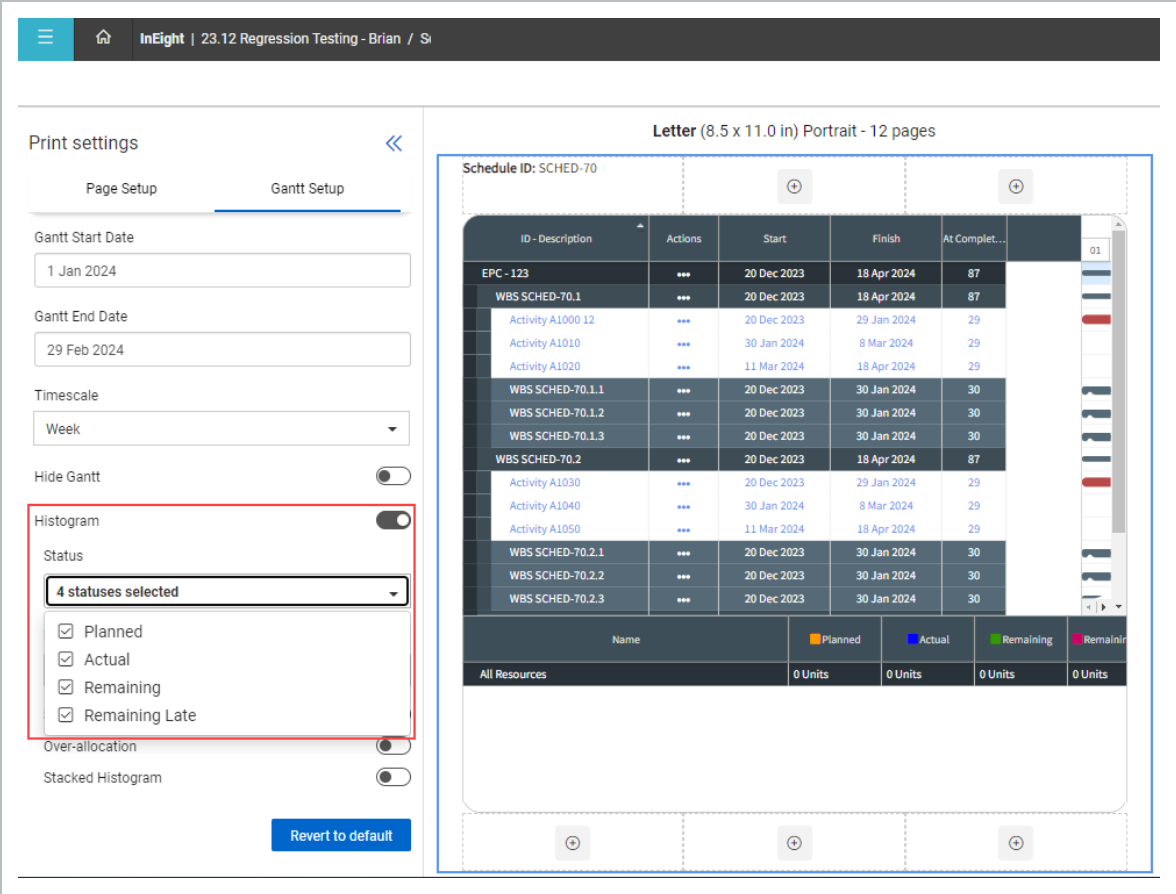

Resources can be displayed as Units, FTE, Cost or Burn Rate in the Display drop-down.

Print settings

Page Setup

Gantt Setup

Gantt Start Date

Jan 2024

Histogram

Status

4 statuses selected

Display

Units

Units ✓

FTE

Cost

Burn rate

Toggles for S-Curve, Over-allocation and Stacked Histogram can also be turned On or Off.

Print settings

Page Setup

Gantt Setup

Gantt Start Date

Jan 2024

4 statuses selected

Display

Units


S-Curve

Over-allocation


Stacked Histogram

SAVE TO PDF

- 1. In Plan view, click the **Go to print view** icon at the top right of the page.




The print view defaults to the Page Setup tab where you can change the page setup paper size, orientation, scaling, header and footer settings.

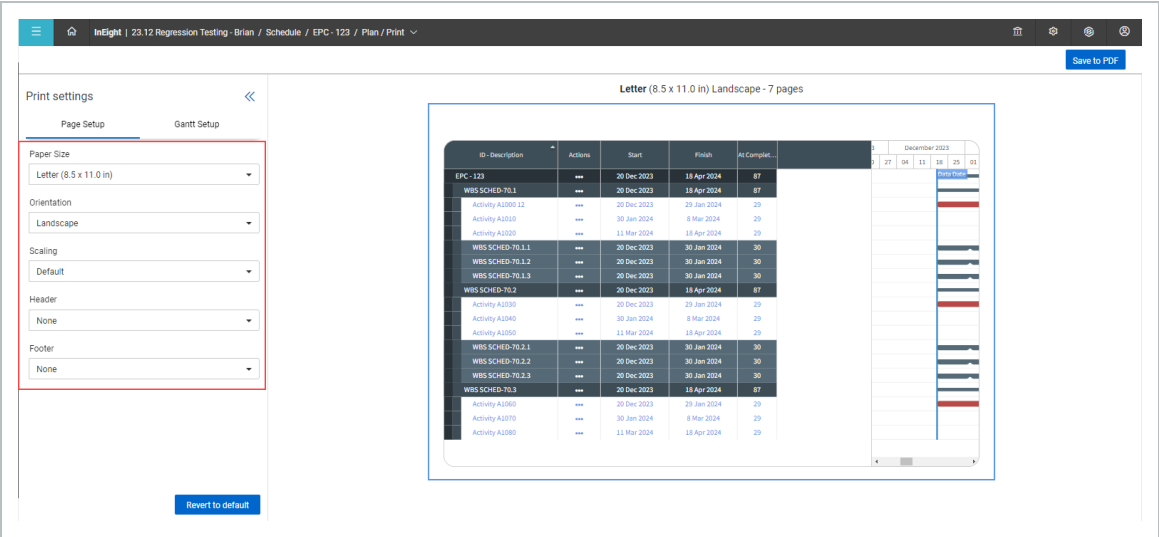


On the Gantt tab, you can select Gantt start and end dates, a timescale time period, an


option to show or hide the Gantt chart, and the option to show the histogram.

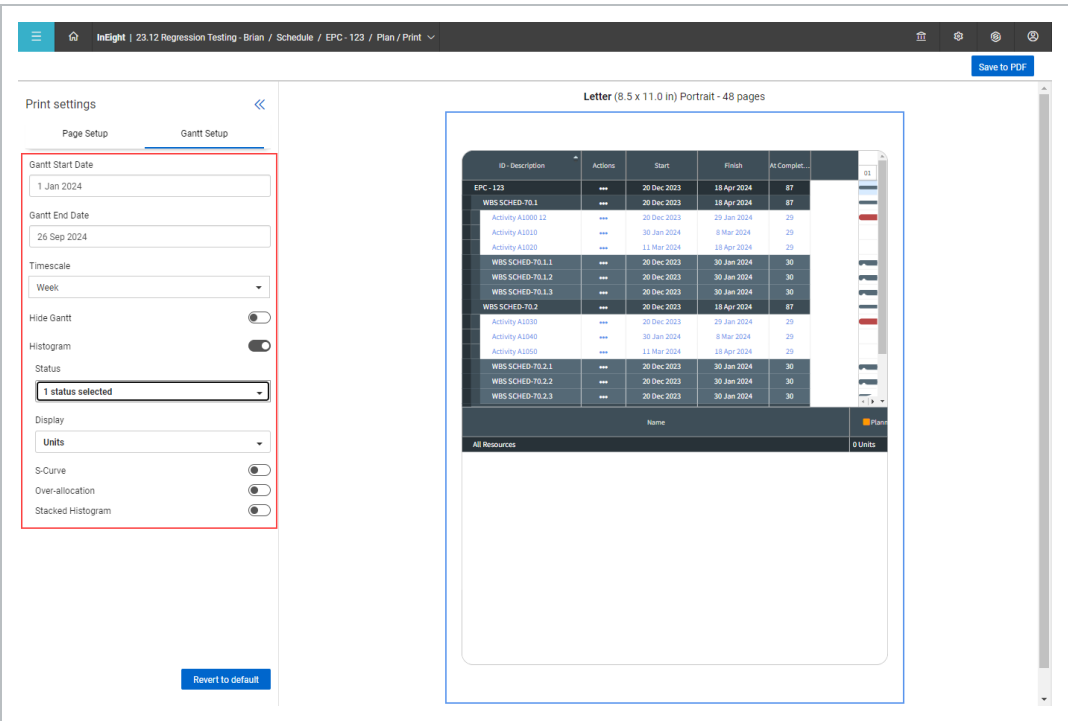


- 2. Click **Save to PDF**.
- 3. In the Save As window, select a file name and choose a file location, then select **Save**.

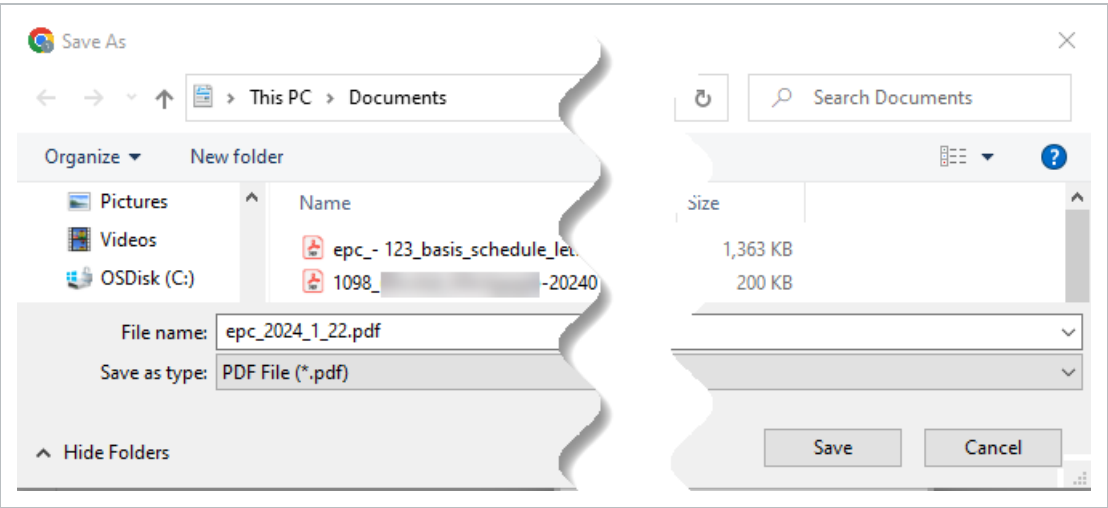

The Print to PDF windows will show printing status.



A success message will show when the PDF printing is complete.



This page intentionally left blank.

LESSON 5 – PACKAGES AND ACTIVITIES

ACTIVITY PRODUCTIVITY RATES

Productivity rates allow schedulers to establish a productivity factors for activities and thus scale durations accordingly.

NOTE

These rates also aid in generating a bottom-up cost for the project.

To set the productivity factor, use the built-in application in the Iris’ Smart Planning Section.

SET THE PRODUCTIVITY FACTOR

- 1. Select an **activity**.

Construction	05 Jul 21 12 Apr 23	463	...					
Early Sitework	05 Jul 21 29 Apr 22	215	...					
Foundations	16 Mar 22 09 Aug 22	105	...				1	
Grade & Support Be...	16 Mar 22 12 Apr 22	20	...					24
Stub-in Utilities	13 Apr 22 03 May 22	15	...					24
Drainage	04 May 22 24 May 22	15	...					24
Pour & Cure	25 May 22 26 Jul 22	45	...					24
Enclosures	27 Jul 22 09 Aug 22	10	...					24

- 2. In Iris > **Smart Planning** section, select the **set productivity rate** option for the activity duration field.

ID

A1000

Description

Activity A1000

Calendar

Project Default

Smart Planning

Planned (d)

0

Cost (\$)

0

Remaining (d)

0

R

Start

0

Actual (d)

0

Finish

0

At Complete (d)

0

Percent Complete

Dur ▾0

Early Start

6 Oct 2022

Early Finish

6 Oct 2022

Late Start

31 Dec 1969

Late Finish

31 Dec 1969

Planned Start

6 Oct 2022

Planned Finish

6 Oct 2022

Total Float

Free Float

- A new window opens with the Productivity Rate Calculator and Knowledge Library Suggestions

R

Estimate the duration and cost of this activity using a Productivity Rate.

Unit Rate

Manhour Rate

Rate

Description

Engineering

Output ?*

UOM ?

Hours/unit *

\$/unit

1

Hours ▾

328

0

Work

How many units?*

Crew/Equip Count *

1

1

Remaining duration is currently 41 days

1 unit of Engineering with 1 crew will take 41 days

Productivity Rate Suggestions

Act 1

days @ \$5MM per 1,250.00 Sec

1 Sec will take 0 days and cost \$4K

Srin new act

555.0000 hours @ \$2 per Sec

1 Sec will take 555 days (555 hours) and cost \$2

ADOPT

ADOPT

CANCEL

APPLY RATE

USING THE PRODUCTIVITY RATE CALCULATOR

In the top section, schedulers establish the package of work to be conducted. Here, you enter the values for the calculator to use to determine the base productivity rate:

When you select the Unit Rate method, the following fields are shown.

R

Estimate the duration and cost of this activity using a Productivity Rate.

Unit Rate

Manhour Rate

Rate

Description

Engineering

Output ?*

UOM ?

Hours/unit *

\$/unit

1

Hours ▾ 328

0

Work

How many units?*

Crew/Equip Count *

1

1

Remaining duration is currently **41 days**
1 unit of **Engineering** with **1** crew will take **41 days**

Productivity Rate Suggestions

Act 1

days @ \$5MM per 1,250.00 Sec

1 Sec will take **0 days** and cost **\$4K**

Srin new act

555.0000 hours @ \$2 per Sec

1 Sec will take **555 days** (555 hours) and cost **\$2**

ADOPT

ADOPT

CANCEL

APPLY RATE


Field	Description
Activity Description	Activity this Productivity Rate is for
Output	Output quantity for a single package (in the respective Unit of

Page 104 of 291

InEight Inc. | Release 25.1

Field	Description
	Measure)
UOM	Unit of Measure description
Time/ "Output & UoM"	Time (Hours/Days/Weeks) to complete the output established
\$/ "Output & UoM"	Cost to complete the output established

When you select the Manhour Rate method, the following fields are shown.



Estimate the duration and cost of this activity using a Productivity Rate.


Unit Rate


Manhour Rate

Rate

Description

WBS SCHED-99.2

Output *

UOM 

Manhours

\$/unit

1

2920

0

Work

How many manhours?*

Crew/Equip Count *

2920


1


Remaining duration is currently **365 days**

1 unit of **WBS SCHED-99.2** with **1** crew will take **365 days**

Productivity Rate Suggestions

No suggestions found.







CANCEL

APPLY RATE

All of the Manhour Rate fields are the same as the Unit Rate Fields, with the exception that the Manhour Rate uses Manhours and the work calculates with manhours instead of units.

Output *

UOM 

Manhours

\$/unit

1

2920

0

Work

How many manhours?*

Crew/Equip Count *

2920

1

Under the Work subheader, schedulers can define the variables on the current project that the productivity rate will be factored against:

Field	Description
How many “manhours”?	Total quantity of manhours of effort to be expended
Crew/Equipment Count	Total Crews or Equipment assigned to complete the work

After all the variables have been entered, Schedule provides a summary of the calculation.

USING THE KNOWLEDGE BASE SUGGESTED RATES

The Knowledge Base pulls in suggested productivity rates based on past packages that are similar in their descriptions, associated knowledge tags , and benchmark selection.

R

Estimate the duration and cost of this activity using a Productivity Rate.

Unit Rate

Manhour Rate

Rate

Description

Engineering

Output ?*

UOM ?

Hours/unit *

\$/unit

1

Hours ▾328

0

Work

How many units?*

Crew/Equip Count *

1

1

Remaining duration is currently 41 days

1 unit of Engineering with 1 crew will take 41 days

Productivity Rate Suggestions

Act 1

days @ \$5MM per 1,250.00 Sec

1 Sec will take 0 days and cost \$4K

Srin new act

555.0000 hours @ \$2 per Sec

1 Sec will take 555 days (555 hours) and cost \$2

ADOPT

ADOPT

CANCEL

APPLY RATE


To select a suggestion, click **Adopt**. This will automatically fills in the Productivity Rate Calculator with the values from the Knowledge Library.

NOTE

You can still make adjustments to the rate for the current project after adopting the suggestion.

CALCULATE PRODUCTIVITY RATES

1. Go to the Knowledge Base productivity rate suggestions and **Adopt** a productivity rate.
2. Set or change the amount of work and crew size.



Estimate the duration and cost of this activity using a Productivity Rate.

Unit Rate

Manhour Rate

Rate

Description

Engineering

Output ?*	UOM ?	Hours/unit *	\$/unit
1		Hours ▾ 328	0

Work

How many units?*

Crew/Equip Count *

1

1

Remaining duration is currently **41 days**
1 unit of **Engineering** with **1** crew will take **41 days**

Productivity Rate Suggestions

Act 1
days @ \$5MM per 1,250.00 Sec
1 Sec will take **0 days** and cost **\$4K**

Srin new act
555.0000 hours @ \$2 per Sec
1 Sec will take **555 days** (555 hours) and cost **\$2**

ADOPT

ADOPT


CANCEL

APPLY RATE


NOTE

Pay attention to how this impacts the activity duration and cost

3. Click **Apply Rate** when complete.
4. Open the Annotation drop-down menu and select **Cost**.

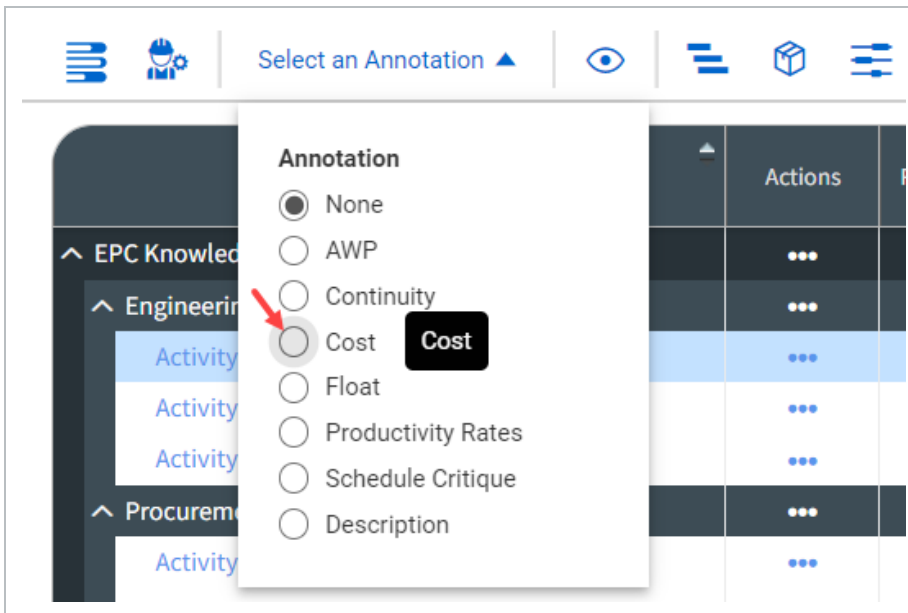

- Now, you can view your project's bottom-up and top-down costs



CREATE ACTIVITIES

There are two ways to conceptualize activity creation within InEight Schedule and depending on your intended outcome, there are benefits to each process:


- Knowledge subnet
- Create form scratch

KNOWLEDGE SUBNETS


Schedule leverages the Knowledge Base to rapidly build a schedule based on historical projects or existing templates. This feature enables you to pull in similar activities from Knowledge Base projects and adjust them based on the parameters of the project being created.

BUILDING A SCHEDULE

1. Select a planning package.
2. From the Iris > **Smart Planning**, under the first Schedule Suggestion, click **Import Knowledge Subnet**.

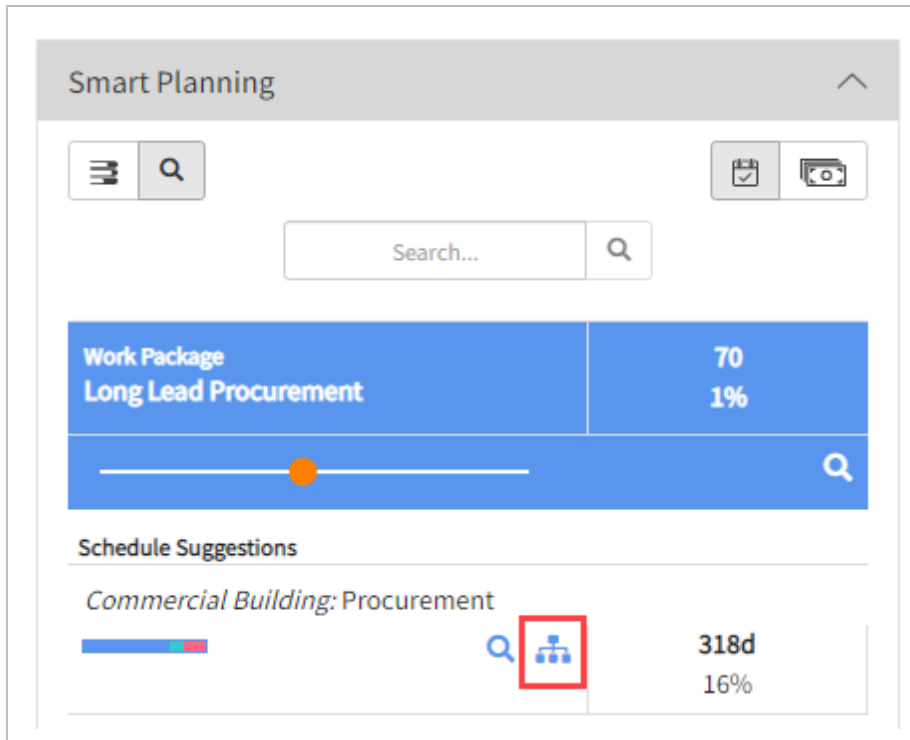


- The merge window opens, letting you customize your selection of planning packages and activities. For this example include all packages and activities in the subnet switched on
3. After the subnet selection is made, the option to bring in Knowledge Base subnet as *Native Import* or *Size to Fit* is available.




- Native Import: it will bring in the selected subnet with the original durations from the Knowledge Base
- Size to Fit: it will proportionally adjusts the subnet to fit within the duration of the Superior planning package in the current schedule

4. Select either **Native Import** or **Size to Fit**.
5. When complete, click **Preview**.

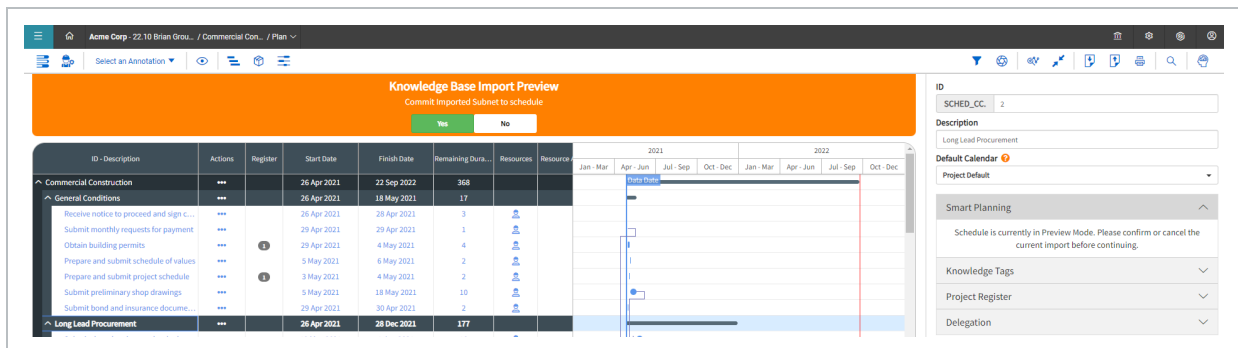

- Schedule merges in the Knowledge Subnet into the project and presents it as a preview.
6. If the preview looks good for merge, select **Yes** to commit the import in Schedule.




ACTIVITIES FROM SCRATCH


The second way to create activities is from scratch. This allows activities not yet in the Knowledge Library to be created on the project. Additionally, it provides schedulers total manual control when creating an activity.

BUILD ACTIVITIES FROM SCRATCH


1. Click the **Actions** icon for the planning package which the subordinate activity falls under.

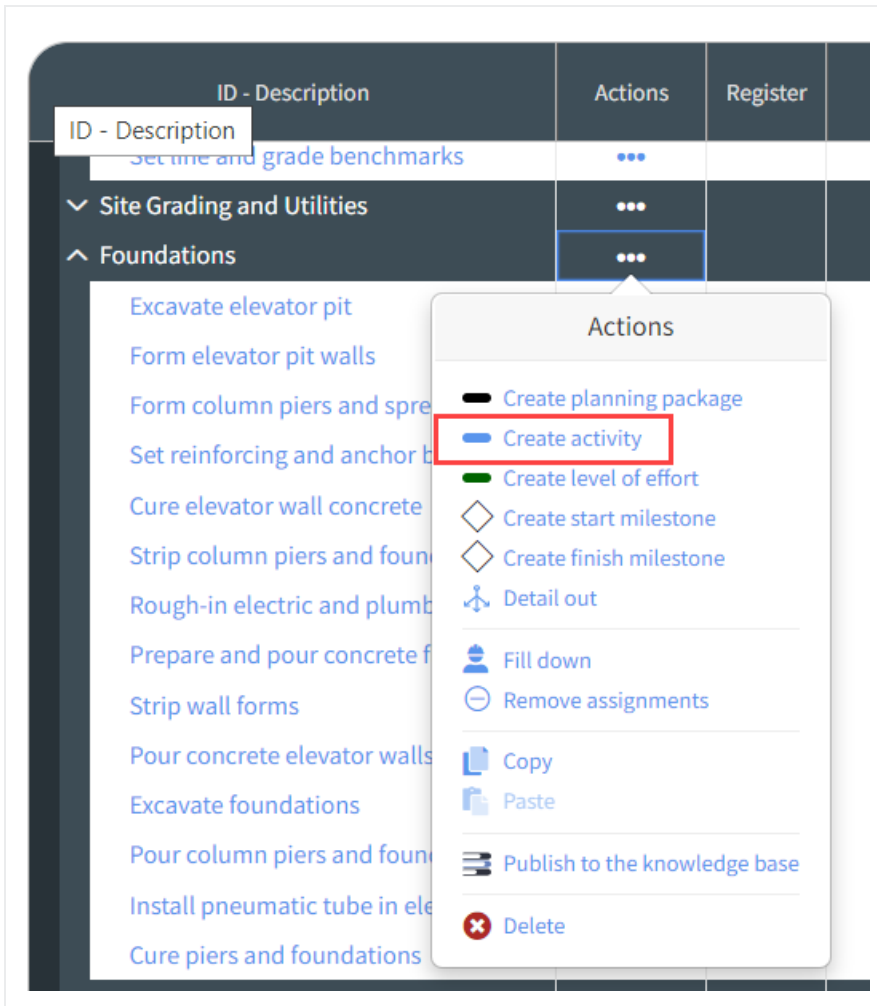

2. Select **Create Activity**.
 - A new activity will appear as a subordinate




3. Rename your activity by either selecting the description field in the Gantt View or by going to the Iris and adjusting the description there.

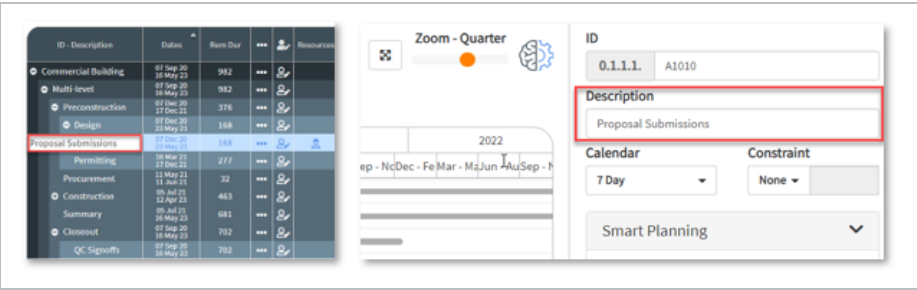


WBS SUMMARY ACTIVITY TYPE

In Schedule > **Plan**, you can create a WBS summary activity. Primavera XER imports support the WBS summary activity type and does not convert these summaries to Planning packages.

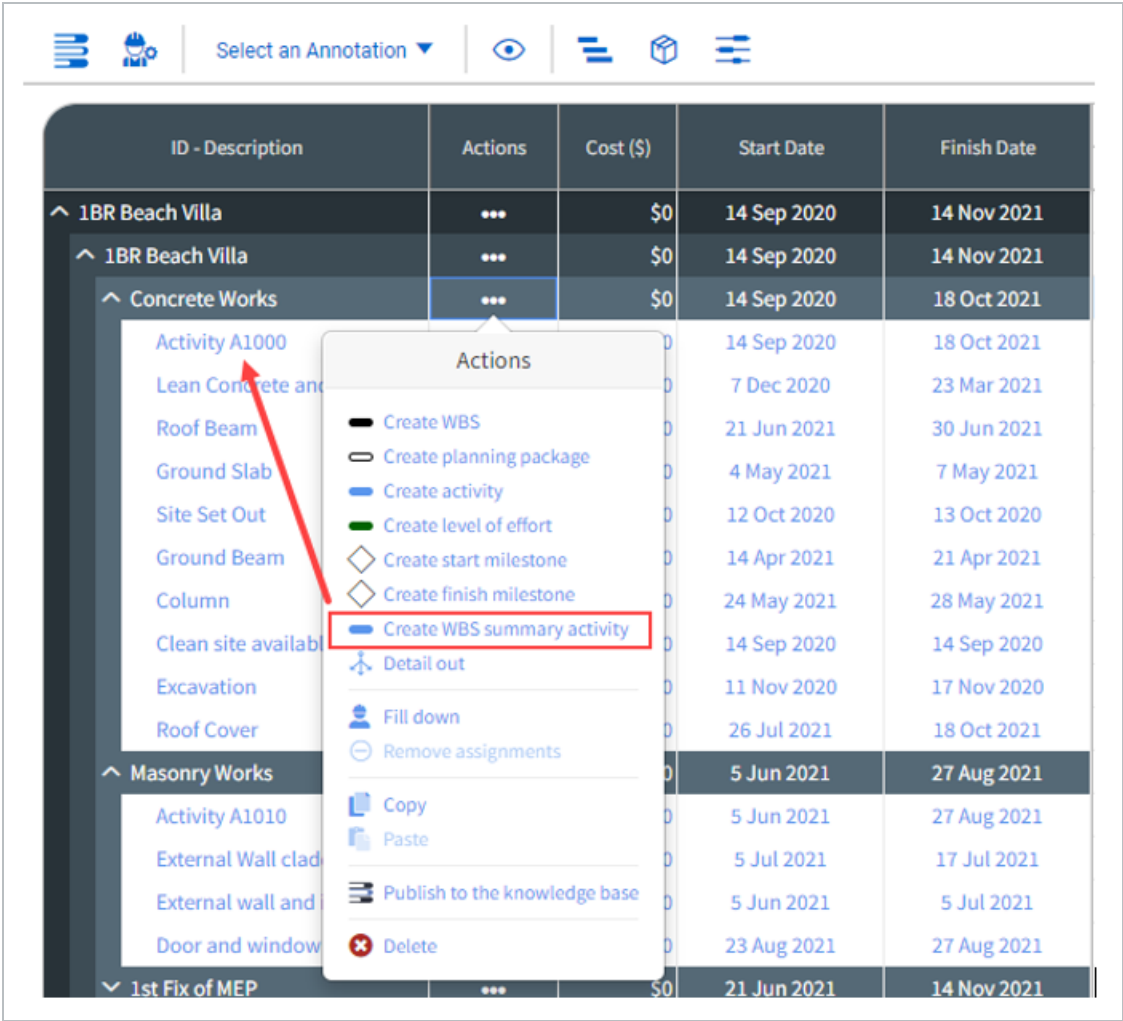

When you increase or decrease the duration of a portion of your WBS in your schedule, the WBS summary activity dynamically reacts to the modified duration changes.

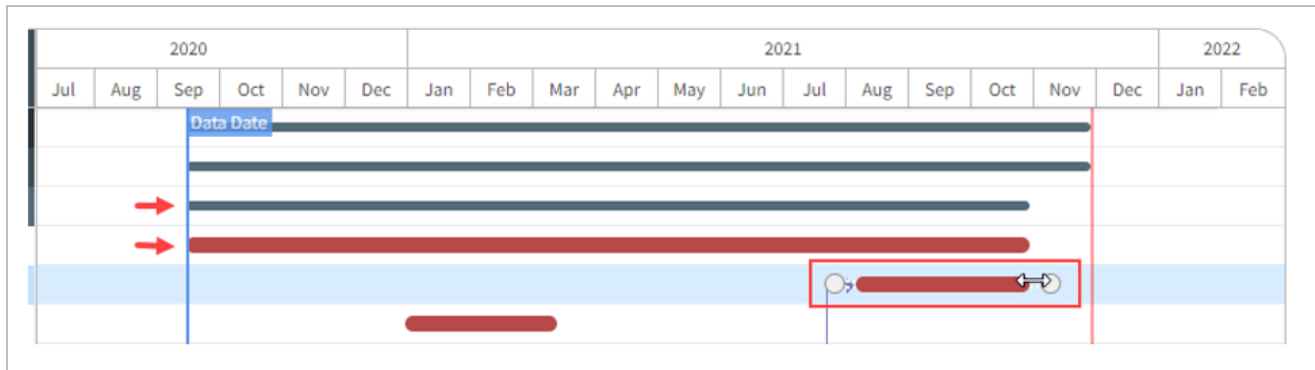

You can load resources into WBS summary activities to help linearly spread units over a specific time frame. Different calendars can be assigned to the WBS summary activity for tracking.

CHANGE ACTIVITY TYPE

You can select an Activity Type in the plan schedule and change it from one type to another via a drop-down menu, which lets change an activity type without having to leave the page.

CHANGE ACTIVITY TYPE

1. From the Schedule Plan view select an (terminal level) **Activity**.
2. Click on **Show/Hide Iris**.

☰

🏠

InEight | 23.8 Regression testing - Tatyana / Schedule / 8-24 / Plan

☰

🔍

Select an Annotation

👁️

☰

📦

☰

ID - Description	Actions	Start Date	Finish Date
WBS SCHED.3	...	4 Sep 2023	2 May 2024
Activity A1000	...	4 Sep 2023	22 Nov 2023
Activity A1010	...	23 Nov 2023	12 Feb 2024
Activity A1020	...	13 Feb 2024	2 May 2024

ve user

🔍

📦

🔍

📄

📄

🖨️

🔍

🧠

ID

A1010

Description

Activity A1010

Activity Type ⚠️

Task dependent

Calendar

Project Default

Constraint

None

Smart Planning

Logic

3. Click on **Activity type drop-down**, and select an activity type.

The screenshot shows a web form for creating activities. At the top is a toolbar with icons for user selection, filters, a globe, a speech bubble, a double arrow, a download, an upload, a printer, a search, and a brain icon. Below the toolbar are three input fields: 'ID' with the value 'A1010', 'Description' with the value 'Activity A1010', and 'Activity Type' with a warning icon and a dropdown arrow. The 'Activity Type' dropdown is open, showing a list of options: 'Select one...', 'Start milestone', 'Finish milestone', 'Task dependent' (which is highlighted), 'Level of effort', and 'WBS summary'. Below the dropdown are six expandable sections: 'Logic', 'Knowledge Tags', 'Project Register', 'Delegation', and 'Resource Assignments', each with a downward arrow.

BULK ACTIVITIES FROM SCRATCH

If multiple activities are to be created from scratch, the detail out function can be used as well.

CREATE ACTIVITIES IN BULK

1. Click the **Actions** icon for the planning package that the subordinate activities fall under.
2. From the Actions menu, click **Detail Out**.
3. Create your activities as needed.
4. Set the Work or Scope option to **Activity**.
5. Set the Sequence option to **In Succession**.
6. Set the Duration to **Automatic**.
7. Set your **Quantity**.
8. Click **Build**.

Quickly build more detailed schedules by creating multiple activities or planning packages. Establish as a logical sequence or in parallel (concurrent).

Work or Scope

Activity Planning Package

Sequence

In Succession Parallel

Duration

Automatic Manual

Quantity

4

Lag Duration

0

Schedule will create **4 Activities In Succession** each with a duration of **31 days** under **WBS SCHED-379.2**.

Cancel Build

9. Change the activity names and their respective duration.

ID - Description	Actions	Register	Start Date	Finish Date	Remaining Dura...	Resources	Resource A...	2022	2023	2024
SCHED-379000	...		11 Jul 2022	15 May 2024	675			Apr - Jun	Jul - Sep	Oct - Dec
Cost Risk-WBS Import	...									
SCHED-379000.1	...	2	11 Jul 2022	15 May 2024	675			Apr - Jun	Jul - Sep	Oct - Dec
WBS SCHED-379.1	...									
A1000	...	2	27 Apr 2023	15 May 2024	385					
Activity A1020	...	2	11 Jul 2022	29 Nov 2022	142					
A1000	...	2	30 Nov 2022	26 Apr 2023	148					
Activity A1010	...	2								
SCHED-379000.2	...		10 Nov 2022	13 Mar 2023	124					
WBS SCHED-379.2	...									
A1110	...		10 Nov 2022	10 Dec 2022	31					
Activity A1110	...		11 Dec 2022	10 Jan 2023	31					
A1120	...		11 Jan 2023	10 Feb 2023	31					
Activity A1120	...									
A1130	...									
Activity A1130	...									

ASSIGN KNOWLEDGE TAGS

Knowledge Tags connect the data between the Knowledge Base, schedules, and activities. Assigning Knowledge Tags to planning packages and activities aid in associating schedules of similar scope, cost, duration, location, discipline etc. for InEight Schedule to generate suggestions and benchmarks.

NOTE


The process of associating Knowledge Tags to activities is fundamentally the same for planning packages.

ASSIGNING KNOWLEDGE TAGS IN THE IRIS

- Select an activity. Open the Iris and go to the Knowledge Tags Section.
 - Knowledge Tags will appear in the Iris based on what is set up in the Knowledge Base & the Configuration Knowledge Tags Register.


The screenshot displays the InEight Schedule Iris interface. On the left, a table lists activities with columns for ID, Description, Actions, Register, Start Date, Finish Date, Remaining Duration, Resources, and Resource A. The activity 'Ceiling installation and paint finish...' is highlighted in blue. On the right, a 'Knowledge Tags' panel is open, showing a list of tags grouped by categories like 'As-Built Performance', 'AWP Structure', 'Brian Activity Code Test', 'CALENDAR', 'Kansas Animals', and 'Kansas Towns and Villages'. Each group has a 'SHOW' button. A red box highlights the 'Knowledge Tags' panel.

- Click on the **arrow** to expand the Knowledge Tags available within each group.



NOTE Some tags have “Inherited” values. These are rolled down from a superior level (i.e. assigned at the project level, assigned at the planning package level)

3. Select a tag from the drop-down menu to assign it to the activity.

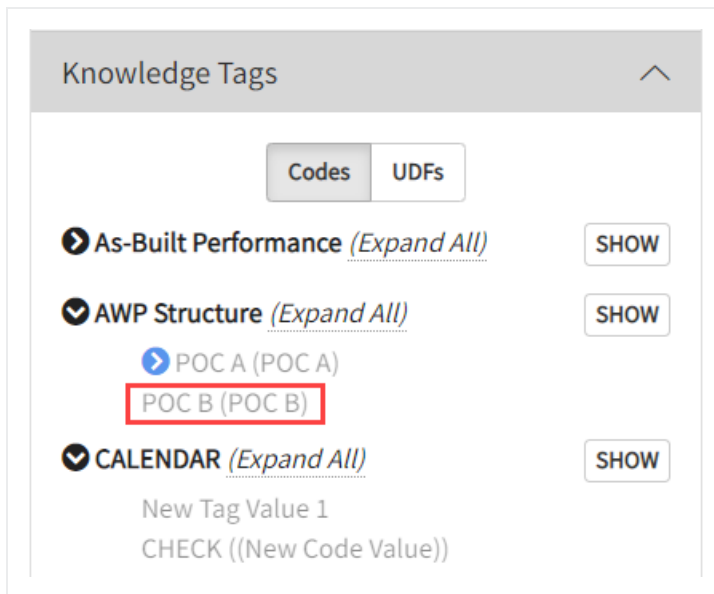

ASSIGNING LOGIC

Logic is what links planning packages, activities, and milestones together throughout the schedule, for example when:


- an activity finishes, another starts
- two activities kick off at the same time
- multiple activities must be completed before another begins

Within Schedule, there are two ways to setup schedule logic: via the Gantt Chart or the Iris.

USING THE GANTT CHART TO ASSIGN LOGIC


The Gantt Chart has built-in functionality allowing activity logic to be tied together directly in the visual. This is great for quickly adding or adjusting logic in the schedule.

When hovering over any activity bar in the Gantt chart, two dots will appear at the beginning and end of the activity:



Clicking and dragging either dot from what activity to another will create a logic tie.

- Dot at the beginning of an activity: the start logic of the activity
- Dot at the end of an activity: the end logic of the activity

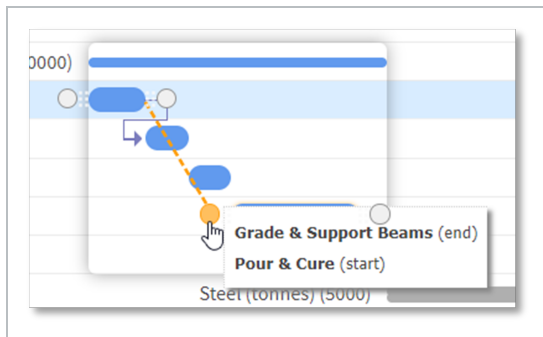

Connecting dots between activities, define the type of logic being applied.

Function (Connect the Dots)	Logic (How to Connect)	
	Start-to-Start (SS)	Connect the start of one activity to the start of another activity
	Finish-to-Start (FS)	Connect the end of one activity to the start of another activity
	Finish-to-Finish (FF)	Connect the end of one activity to the end of another activity
	Start-to-Finish (SF)	Connect the start of one activity to the end of another activity

NOTE

The first activity dot selected is treated as the predecessor to the second activity dot. Thus, the second activity will be a successor to the first activity.

RELEVANT LINKS

[Course - Schedule Detailed Planning](#)

[Add Schedule Detail](#)

PLANNING MODE

At the start of the project or phase, non-schedulers identify the key items to be planned for and create a rough timeline of the plan. InEight Schedule gives you the ability to do this in a way that easily carries forward into a full schedule.

TIP


Planning mode lets users freely move around planning items. In this mode, planning packages and milestones can be added, but not activities.

CREATE A NEW PLANNING PACKAGE


NOTE

Planning packages brought in from the outline during project creation are automatically populated.

1. To create a new planning package from scratch, click the **Schedule** icon in the far left corner and select **Planning** Schedule mode.

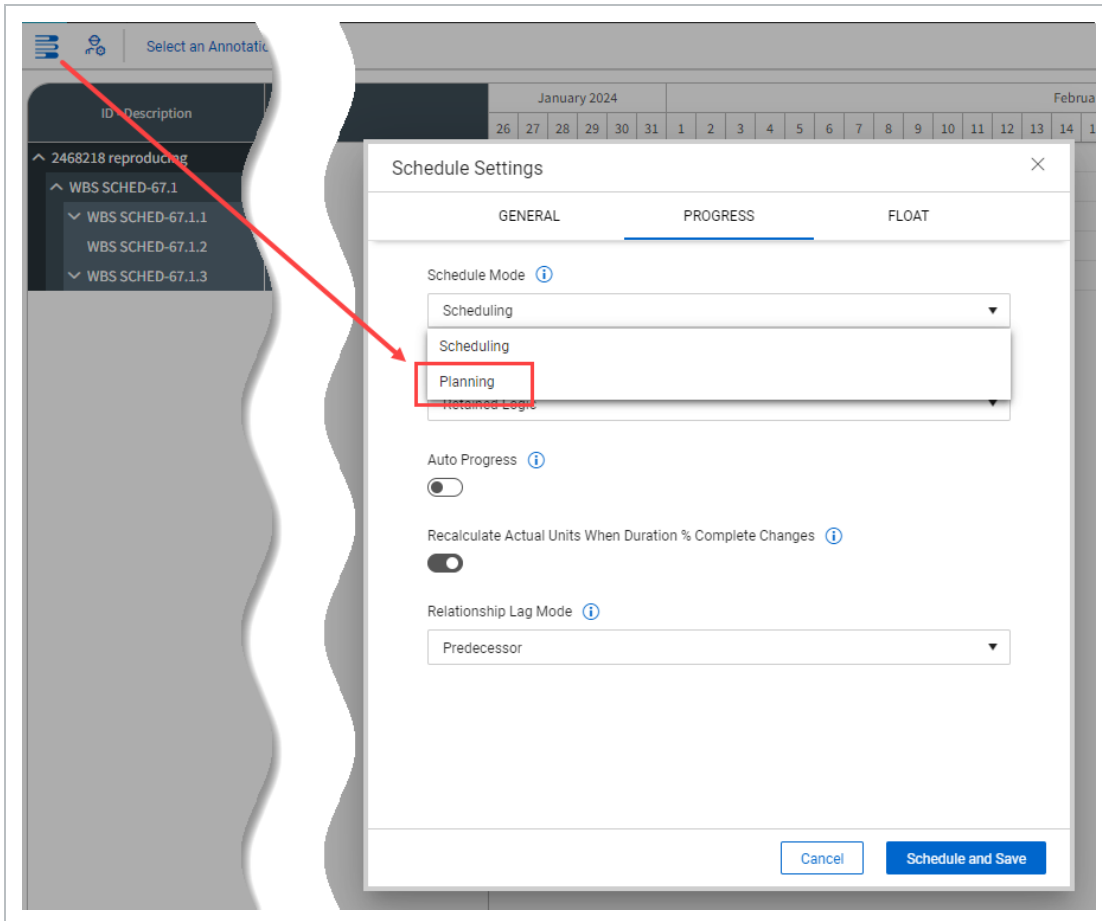

2. Scroll down to select **Schedule and Save** at the bottom far right on the Schedule Settings window.

**NOTE**

New planning packages are created as subordinates under the open or selected parent package.

ID - Description	Dates	Rem Dur	...	👤	Resources	Resource As	🟡	Float
Commercial Building	07 Sep 20 16 May 23	982	...	👤				
Multi-level	07 Sep 20 16 May 23	982	...	👤				
Preconstruction	07 Sep 20 25 Jul 21	322	...	👤				660
Procurement	22 Feb 21 14 Sep 21	205	...	👤			1	609
Construction	05 Jul 21 12 Apr 23	647	...	👤				34
Summary	05 Jul 21 16 May 23	681	...	👤				0
Closeout	08 Mar 23 16 May 23	70	...	👤				0
WBS 0.1.6	07 Sep 20 16 May 23	702	...	👤				0

TIP

If the Actions icon is not available, you can bring it into view using the **Customize Gantt View** icon at top.

1. Click in the **Description** column to rename your new planning package.
2. Organize planning packages by clicking and dragging the rows.

Commercial Building	07 Sep 20 16 May 23	982	...	👤				
Multi-level	07 Sep 20 16 May 23	982	...	👤				
Preconstruction	07 Sep 20 25 Jul 21	322	...	👤				660
Procurement	22 Feb 21 14 Sep 21	205	...	👤			1	609
Construction	05 Jul 21 12 Apr 23	647	...	👤				34
Summary	05 Jul 21 16 May 23	681	...	👤				0
Closeout	07 Sep 20 16 May 23	702	...	👤				0
QC Signoffs	07 Sep 20 16 May 23	702	...	👤				0
QC Signoffs	07 Sep 20 16 May 23	702	...	👤				0

NOTE

When dragging rows in the Gantt chart, either a white dot or a blue line shows where in the hierarchy the row is being moved. Or, a row is boxed in blue, signifying the planning package being dragged will become a subordinate to the boxed work package.

3. You can continue adjusting planning packages using the bars in the Gantt chart.

NOTE


You can adjust a planning package's duration in the Rem Dur column. This will adjust its duration while holding the current start date.




BULK CREATION OF PLANNING PACKAGES

Add planning packages individually or in bulk with the Detail Out function.

- 1. Select the **Actions** icon on an existing planning package.
- 2. From the drop-down menu, select **Detail Out**.

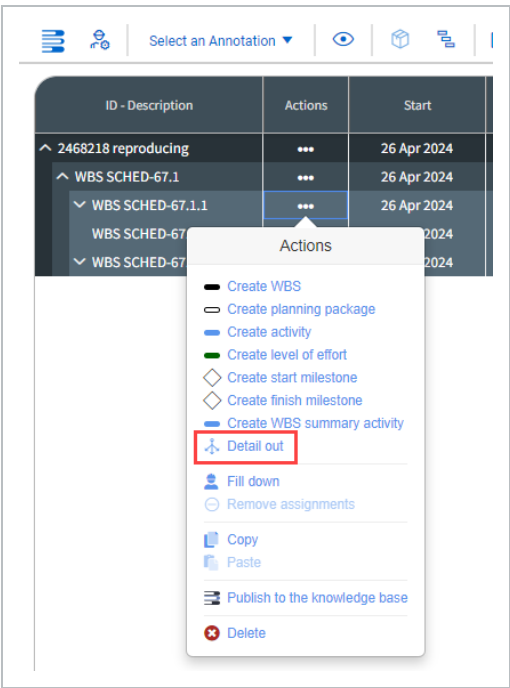

- From here you can select how you want to add your new planning packages



×

Quickly build more detailed schedules by creating multiple activities or planning packages. Establish as a logical sequence or in parallel (concurrent).

Work or Scope

Activity

Planning Package

Sequence

In Succession

Parallel

Duration

Automatic

Manual

Quantity

3

Lag Duration

0

Schedule will create 3 Activities In Succession each with a duration of 2 days under WBS SCHED-67.1.1.

Cancel

Build

Field	Description
Sequence	Sets the new planning packages to occur in succession or parallel.
Duration (Automatic)	Schedule will distribute the superior duration evenly across the subordinate planning packages.
Duration (Manual)	Manually set a custom base duration.
Quantity	Number of subordinate planning packages are being created.
Use Logic (On)	Logic is tied from one package to the next.
Use Logic (Off)	Logic is not assigned. Additionally, the option to set a scope gap is provided.

NOTE

The values set here are for the default/initial creation of packages and can be changed as needed later .

3. Set the **quantity**.
4. Click **Build**.


NOTE

At the bottom of the Detail Out window is a summary of what will be added to the schedule.

5. Your new WBS planning package is created, and you can rename your planning packages accordingly.

ADVANCED WORK PACKAGING

The integration with Project Suite is built primarily for the Project Suite migration. For new users or non-connected workspaces, you can navigate to the Project List page, select a workspace and link a project. You can then select a project in Project Suite to connect and link a project schedule in Schedule.

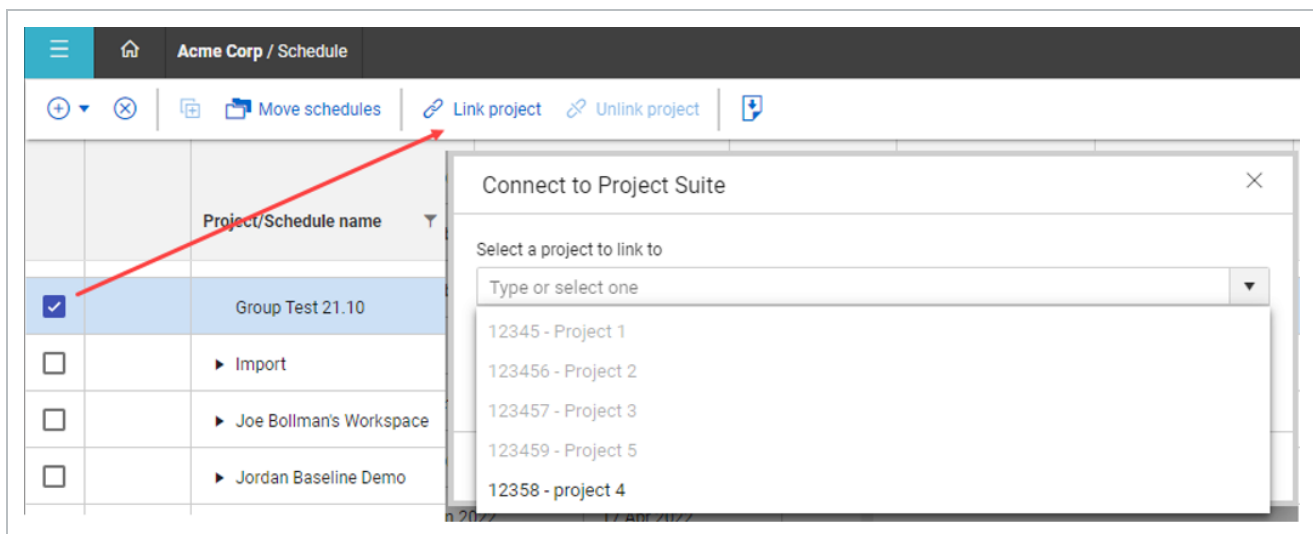

When linked, the Project Suite field becomes populated with a selected project.

Acme Corp / Schedule							
<div><div><div></div><div></div></div><div><div>Move schedules</div><div>Link project</div><div>Unlink project</div></div><div></div></div>							
		Project/Schedule name	Schedule ID	Project Suite	Start	Finish	C
<input type="checkbox"/>		▶ 23.4 Group Test - Regression		123459 - Project 5	01 Jun 2015	21 Nov 2020	
<input type="checkbox"/>		▶ 00001 BUG TEST			24 Apr 2023	24 Apr 2024	
<input type="checkbox"/>		▶ 001. Baseline Regression		123456 - Project 2	23 Dec 2013	07 Dec 2034	
<input type="checkbox"/>		▶ 1			30 Mar 2021	06 Oct 2028	
<input type="checkbox"/>		▶ 22_2_Brian_Group_Testing			20 May 2022	23 Nov 2023	


When you go to AWP, you see Plan and Progress data in that schedule.

NOTE

The availability of AWP data from Plan is determined by the Advanced work and scheduling features toggle in InEight cloud platform > project > Settings > General > **Global Options**. The toggle must be set to *ON* for projects that want to use the AWP feature in Schedule.

Advanced Work Packaging																																																																																																																																															
Associate your schedule structure with AWP elements																																																																																																																																															
<div><div>Search Schedule</div><div><table><thead><tr><th>Name</th><th>ID</th><th>Type</th><th>Start</th><th>End</th><th></th></tr></thead><tbody><tr><td>Ring Road interchange Upgrade</td><td></td><td>WBS</td><td>16 Jan ...</td><td>2 Jan 2...</td><td></td></tr><tr><td>Preconstruction</td><td></td><td>WBS</td><td>16 Jan ...</td><td>7 Feb 2...</td><td></td></tr><tr><td>Design</td><td></td><td>WBS</td><td>16 Jan ...</td><td>4 Sep 2...</td><td></td></tr><tr><td>Permitting</td><td></td><td>WBS</td><td>8 Jun 2...</td><td>7 Feb 2...</td><td></td></tr><tr><td>Procurement</td><td></td><td>WBS</td><td>5 Sep 2...</td><td>4 Apr 2...</td><td></td></tr><tr><td>Submittals & Approvals</td><td></td><td>WBS</td><td>5 Sep 2...</td><td>17 Jan ...</td><td></td></tr><tr><td>Fabrication & Delivery</td><td></td><td>WBS</td><td>10 Oct ...</td><td>4 Apr 2...</td><td></td></tr><tr><td>Construction</td><td></td><td>WBS</td><td>16 Jan ...</td><td>2 Jan 2...</td><td></td></tr><tr><td>Key Milestones</td><td></td><td>WBS</td><td>16 Jan ...</td><td>2 Jan 2...</td><td></td></tr><tr><td>Early Sitework</td><td></td><td>WBS</td><td>17 Jan ...</td><td>21 Nov ...</td><td></td></tr><tr><td>Foundations</td><td></td><td>WBS</td><td>3 Oct 2...</td><td>23 Jan ...</td><td></td></tr><tr><td>Structure</td><td></td><td>WBS</td><td>24 Jan ...</td><td>7 Aug 2...</td><td></td></tr><tr><td>External</td><td></td><td>WBS</td><td>6 May ...</td><td>6 Oct 2...</td><td></td></tr></tbody></table></div><div><div>Search AWP Structure</div><div><table><thead><tr><th>Name</th><th>Description</th><th>Type</th><th>Task</th><th>Start</th><th>End</th></tr></thead><tbody><tr><td>S100.01</td><td>Zone S100 Bulleen R...</td><td>CWA</td><td></td><td></td><td></td></tr><tr><td>WBP-Bulleen Roa...</td><td>Bulleen Road Temp...</td><td>CWP</td><td></td><td></td><td></td></tr><tr><td>WBP-Concrete - F...</td><td>Concrete for Bulleen ...</td><td>WBP</td><td></td><td></td><td></td></tr><tr><td>WBP-Temporary D...</td><td>Temporary Diversion ...</td><td>WBP</td><td></td><td></td><td></td></tr><tr><td>S100.02</td><td>Zone S100 Bulleen R...</td><td>CWA</td><td></td><td></td><td></td></tr><tr><td>CWP-BR101 - Bulleen...</td><td>BR101 - Bulleen Rd O...</td><td>CWP</td><td></td><td></td><td></td></tr><tr><td>S100.03</td><td>Zone S100 Bulleen R...</td><td>CWA</td><td></td><td></td><td></td></tr><tr><td>S100.10</td><td>Zone S100 EF IB Entr...</td><td>CWA</td><td></td><td></td><td></td></tr></tbody></table></div></div></div>						Name	ID	Type	Start	End		Ring Road interchange Upgrade		WBS	16 Jan ...	2 Jan 2...		Preconstruction		WBS	16 Jan ...	7 Feb 2...		Design		WBS	16 Jan ...	4 Sep 2...		Permitting		WBS	8 Jun 2...	7 Feb 2...		Procurement		WBS	5 Sep 2...	4 Apr 2...		Submittals & Approvals		WBS	5 Sep 2...	17 Jan ...		Fabrication & Delivery		WBS	10 Oct ...	4 Apr 2...		Construction		WBS	16 Jan ...	2 Jan 2...		Key Milestones		WBS	16 Jan ...	2 Jan 2...		Early Sitework		WBS	17 Jan ...	21 Nov ...		Foundations		WBS	3 Oct 2...	23 Jan ...		Structure		WBS	24 Jan ...	7 Aug 2...		External		WBS	6 May ...	6 Oct 2...		Name	Description	Type	Task	Start	End	S100.01	Zone S100 Bulleen R...	CWA				WBP-Bulleen Roa...	Bulleen Road Temp...	CWP				WBP-Concrete - F...	Concrete for Bulleen ...	WBP				WBP-Temporary D...	Temporary Diversion ...	WBP				S100.02	Zone S100 Bulleen R...	CWA				CWP-BR101 - Bulleen...	BR101 - Bulleen Rd O...	CWP				S100.03	Zone S100 Bulleen R...	CWA				S100.10	Zone S100 EF IB Entr...	CWA			
Name	ID	Type	Start	End																																																																																																																																											
Ring Road interchange Upgrade		WBS	16 Jan ...	2 Jan 2...																																																																																																																																											
Preconstruction		WBS	16 Jan ...	7 Feb 2...																																																																																																																																											
Design		WBS	16 Jan ...	4 Sep 2...																																																																																																																																											
Permitting		WBS	8 Jun 2...	7 Feb 2...																																																																																																																																											
Procurement		WBS	5 Sep 2...	4 Apr 2...																																																																																																																																											
Submittals & Approvals		WBS	5 Sep 2...	17 Jan ...																																																																																																																																											
Fabrication & Delivery		WBS	10 Oct ...	4 Apr 2...																																																																																																																																											
Construction		WBS	16 Jan ...	2 Jan 2...																																																																																																																																											
Key Milestones		WBS	16 Jan ...	2 Jan 2...																																																																																																																																											
Early Sitework		WBS	17 Jan ...	21 Nov ...																																																																																																																																											
Foundations		WBS	3 Oct 2...	23 Jan ...																																																																																																																																											
Structure		WBS	24 Jan ...	7 Aug 2...																																																																																																																																											
External		WBS	6 May ...	6 Oct 2...																																																																																																																																											
Name	Description	Type	Task	Start	End																																																																																																																																										
S100.01	Zone S100 Bulleen R...	CWA																																																																																																																																													
WBP-Bulleen Roa...	Bulleen Road Temp...	CWP																																																																																																																																													
WBP-Concrete - F...	Concrete for Bulleen ...	WBP																																																																																																																																													
WBP-Temporary D...	Temporary Diversion ...	WBP																																																																																																																																													
S100.02	Zone S100 Bulleen R...	CWA																																																																																																																																													
CWP-BR101 - Bulleen...	BR101 - Bulleen Rd O...	CWP																																																																																																																																													
S100.03	Zone S100 Bulleen R...	CWA																																																																																																																																													
S100.10	Zone S100 EF IB Entr...	CWA																																																																																																																																													

When a project schedule is identified as an Active Update Schedule Type, it becomes the Project Suite connected schedule.

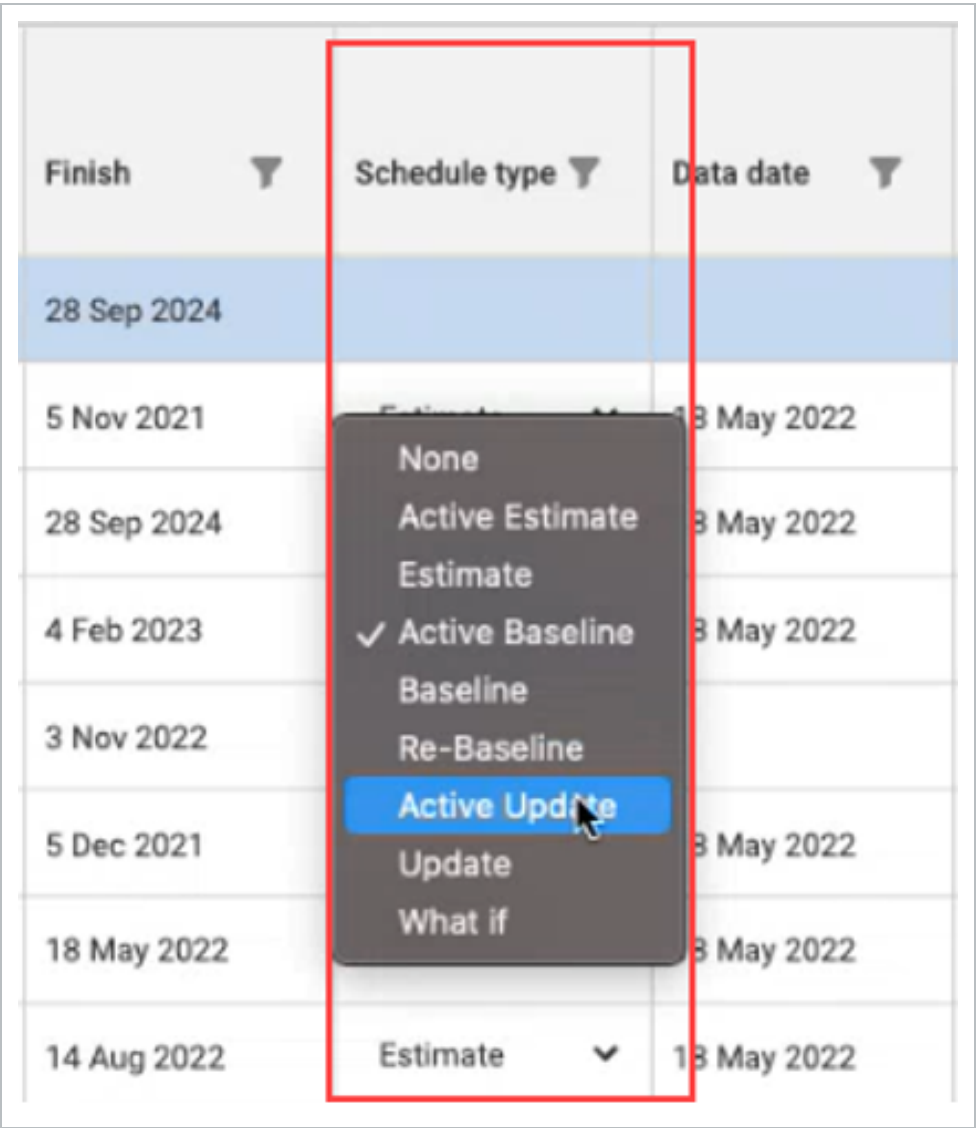


An InEight icon shows next to the project schedule name to signify that the schedule is now linked with a project in Project Suite.

<input type="checkbox"/>		Melbourne Airport...	SCHED-45	06 Dec 2021
<input type="checkbox"/>		Metropolitan ring r...	NEL-002	06 Dec 2021
<input type="checkbox"/>		Linked to Ridgeway Campus Ring Road intercha...	NEL-001	16 Jan 2023
<input type="checkbox"/>		Ring Road intercha...	NEL-005	16 Jan 2023


UNLINK A PROJECT SUITE PROJECT

You can select **Unlink project** to disconnect a Project suite project from Schedule. All the AWP associations will be deleted, and any changes cannot be undone.

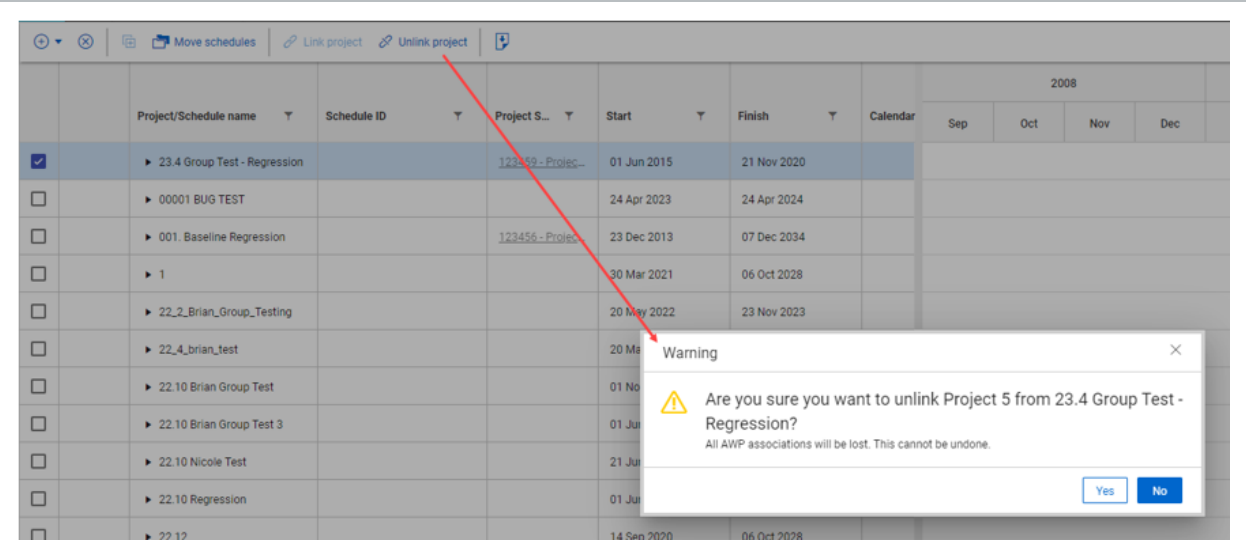


SCHEDULE CONFIGURATION

Schedules that are housed under the *None* project workspace do not support a Project Suite project connection via the Project Suite tab in Schedule Configuration.




If a connection is required, you can move the schedule file to a new or existing workspace to enable this feature.



LESSON 6 – RESOURCE MANAGEMENT

PROJECT RESOURCES

The Resource Management function provides schedulers with the ability to account for and report on the project resources (for example, labor, materials, or equipment) that are needed to plan the scheduled work.

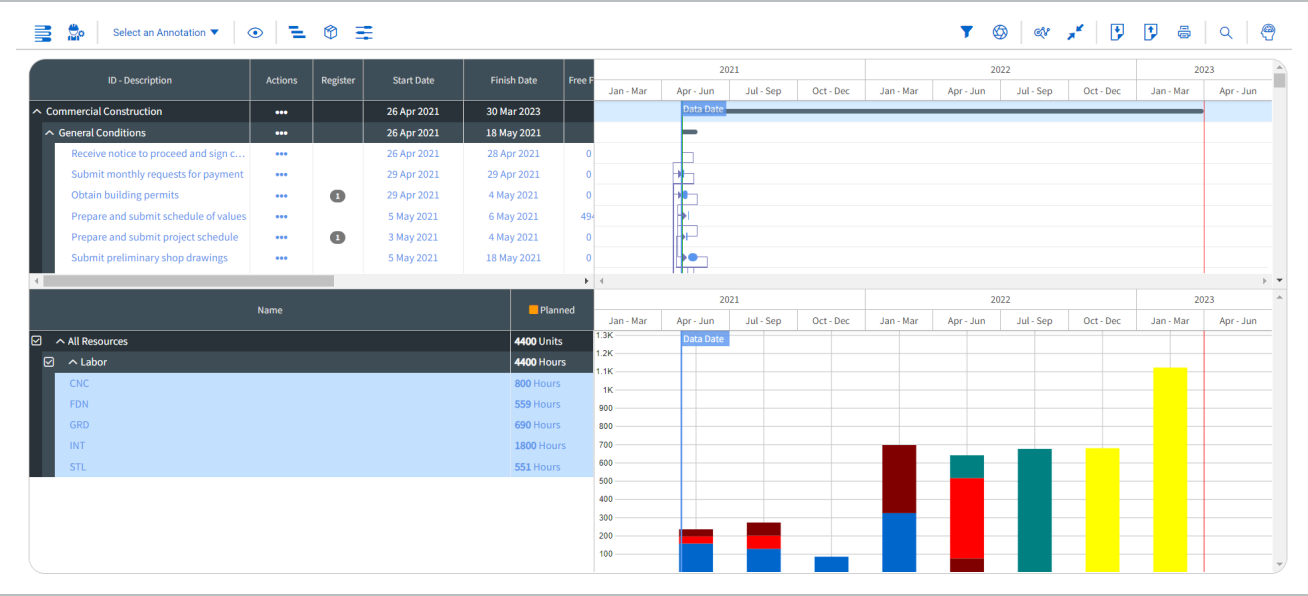

From a shared organization resource pool, schedulers can assign the required resources to activities. With the resource utilization data, InEight Schedule can assess cost and time impacts in a time-phased manner.


CPM SCHEDULES ACTIVITY PRODUCTIVITY RATES KNOWLEDGE TAGS CALENDARS REGISTER RESOURCES MACHINE LEARNING

Resources Categories

ID	Name	Category	Color	UoM	Default Units/d	Cost/Unit	
Kim	Kim Test	Labor		Hours	8.00	1.00	
Robin	Tester	Material		Each	1.00	200.00	
Project resource	project resource	Nonlabor		Each	1.00	75.00	
009	Resource 9	Nonlabor		Each	1.00	0	
Global	Global	New Category		Each	1.00	0	
Import ID	Srini Import Desc	Unique		Each	1.00	0	
Tatyana	Ressurs 009	Supply		Hver	25.00	5080.00	
Indent	Indent	Labor		Hours	8.00	0	
SB2		Labor		Hours	8.00	0	
SP	Ski Patroller	Labor		Hours	8.00	25.00	
No UOM	UOM No	Labor			1.00	0	
Jonny B	Bonny J	Labor		Hours	8.00	0	

IMPORT RESOURCES FROM KNOWLEDGE BASE RESOURCE REGISTER INTO PROJECT RESOURCES REGISTER

- 1. Click on the **Import Resources** icon, and then select **Knowledge Base** from the Import Type drop-down menu.

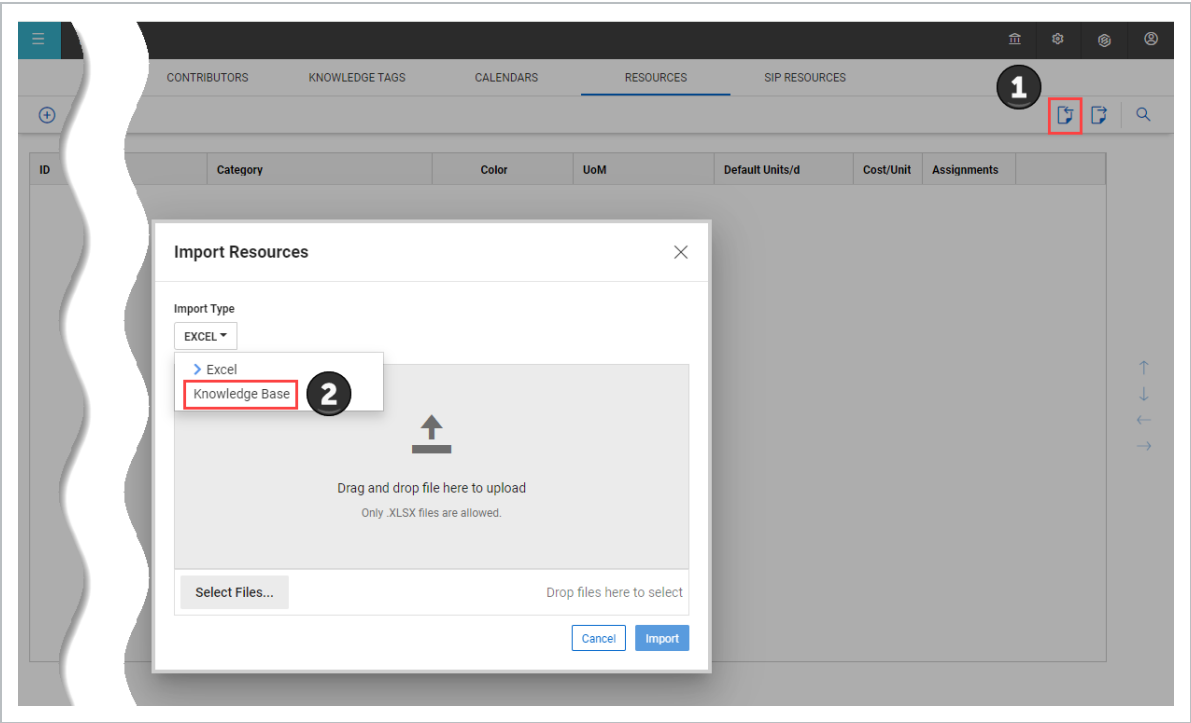

- 2. Select the **Knowledge Base resources** that you want to include in your project, and then click **Import**.

Import Resources

Import Type

KNOWLEDGE BASE

⚠ Indicates resource already exists and will be duplicated.

Knowledge Base Resources	Include
13149-CC008 CC008 - Const of Interior Walls at 2700S, Riter, SR201	<div>1</div> <div><input checked="" type="checkbox"/></div>
13149-RAL 13149-Revenue Aesthetics and Landscape	<div><input checked="" type="checkbox"/></div>
13149-CC003 CC003 - Opticom for WVC	<div><input checked="" type="checkbox"/></div>
13149-CC004 CC004 - Polymer Overlay - Utah/Salt Lake Canal	<div><input type="checkbox"/></div>
13149-RCO 13149-Revenue Compensable Overhead	<div><input type="checkbox"/></div>
13149-CC007 CC007 - HMA Fill for WVC at 2700 South	<div><div>2</div><div><input type="checkbox"/></div></div>

Cancel


Import

NOTE

⚠

The symbol indicates that the resource already exists and will be duplicated.

- 3. You will see an Import Successful message. Select **OK**.

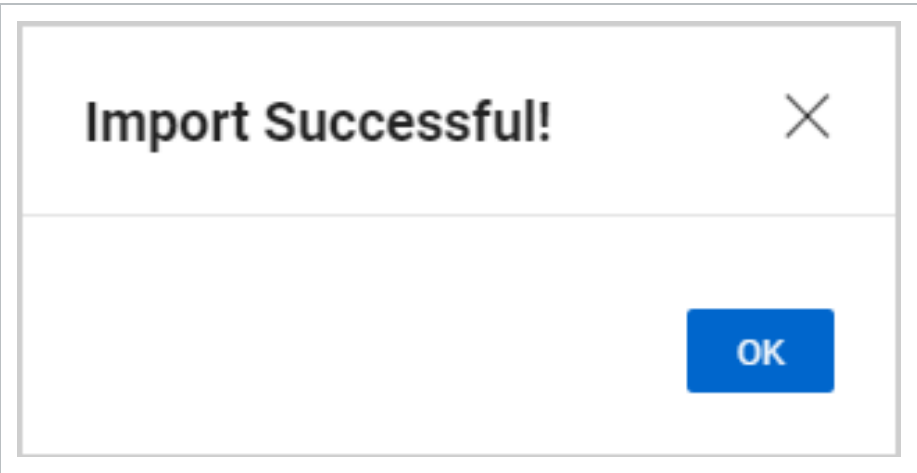

The selected resources are now imported into the project from the Knowledge Base Resource register.

GENERAL CONTRIBUTORS KNOWLEDGE TAGS CALENDARS RESOURCES SIP RESOURCES								
⊕ ⌂ 📄 🔍								
ID	Name	Category	Color	UoM	Default Units/d	Cost/Unit	Assignments	
13149-CC008	CC008 - Const of Interior Walls at 2700S, Riter, SF	Material ▶	●	Dollars	1.00	1.00	0	⊗
13149-RAL	13149-Revenue Aesthetics and Landscape	Material ▶	●	Dollars	1.00	1.00	0	⊗
13149-CC003	CC003 - Opticom for WVC	Nonlabor ▶	●	Each	1.00	1.00	0	⊗

RESOURCE ASSIGNMENTS

Resources are assigned to activities (activity level) but can also be set via work packages (summary level) in the schedule.

ASSIGN RESOURCES AT THE ACTIVITY LEVEL

From Plan view, access the resource assignments of the assigned by using the options below:

- You can open an Activity’s details in the Iris, expanding the Resource Assignments section, and selecting **Modify**.

Project Register

Delegation

Resource Assignments


ID	Category	Curve	Plan	Remaining	Actual
SCE_COST	Nonlabor	Linear	1	1	0
SCE-CRE	Labor	Linear	0	0	0

Modify


- You can customize the Gantt Chart view to include the Resources Column and selecting the **Resources** icon directly in the Gantt Chart.

ID - Description	Actions	Register	Start Date	Finish Date	Remaining Dura...	Resources	Resource Assignments
ABC Building Project Baseline	...	4	21 Jun 2021	14 Jul 2022	268		
ABC Building	...	4	21 Jun 2021	14 Jul 2022	268		
Summary & Milestones	...	4	21 Jun 2021	14 Jul 2022	268		
Pre-Construction	...	4	21 Jun 2021	24 Nov 2021	110		
Construction	...	4	4 Aug 2021	11 Jul 2022	234		
Mobilization	...	1 4	4 Aug 2021	16 Aug 2021	9		
Temp Trailer Install	...	5	11 Aug 2021	11 Aug 2021	1		SCE_COST, SCE-CRE
Temporary Electric Install	...	5	5 Aug 2021	11 Aug 2021	5		SCE_COST, SCE-CRE
Existing Conditions Document...	...	5	4 Aug 2021	6 Aug 2021	3		SCE_COST, SCE-CRE
Install Temporary Barricades	...	5	9 Aug 2021	10 Aug 2021	2		SCE_COST, SCE-CRE
Temp Sanitary Facilities Install	...	5	11 Aug 2021	11 Aug 2021	1		SCE_COST, SCE-CRE
Dig Alert	...	5	4 Aug 2021	6 Aug 2021	3		SCE_COST, SCE-CRE

- When either of these options have been selected, the resource assignment window appears:

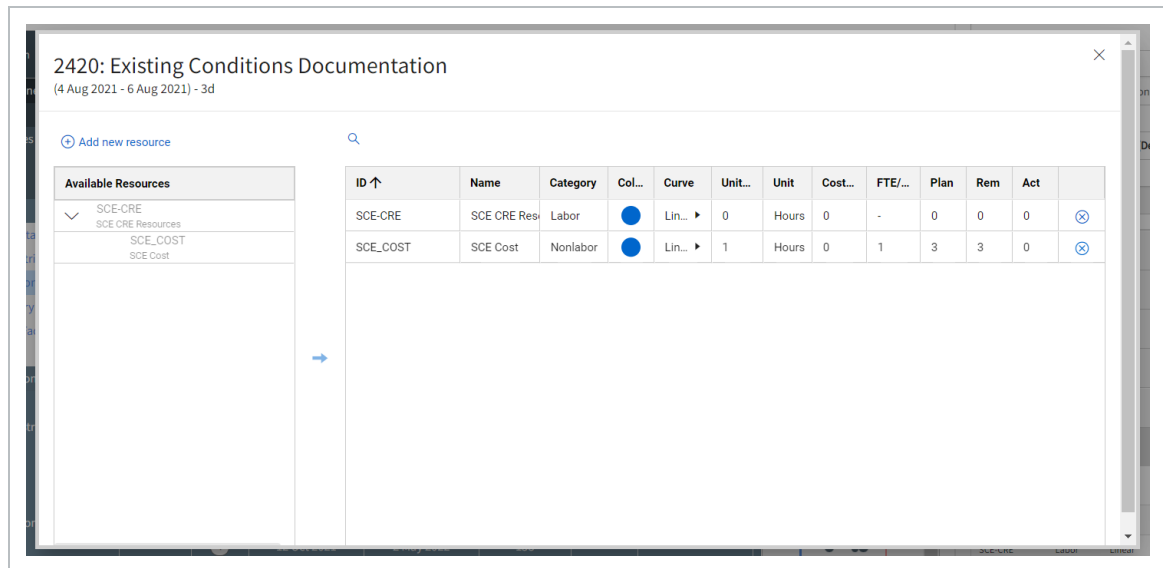


- In the resource window, under Available Resources, select the resource.

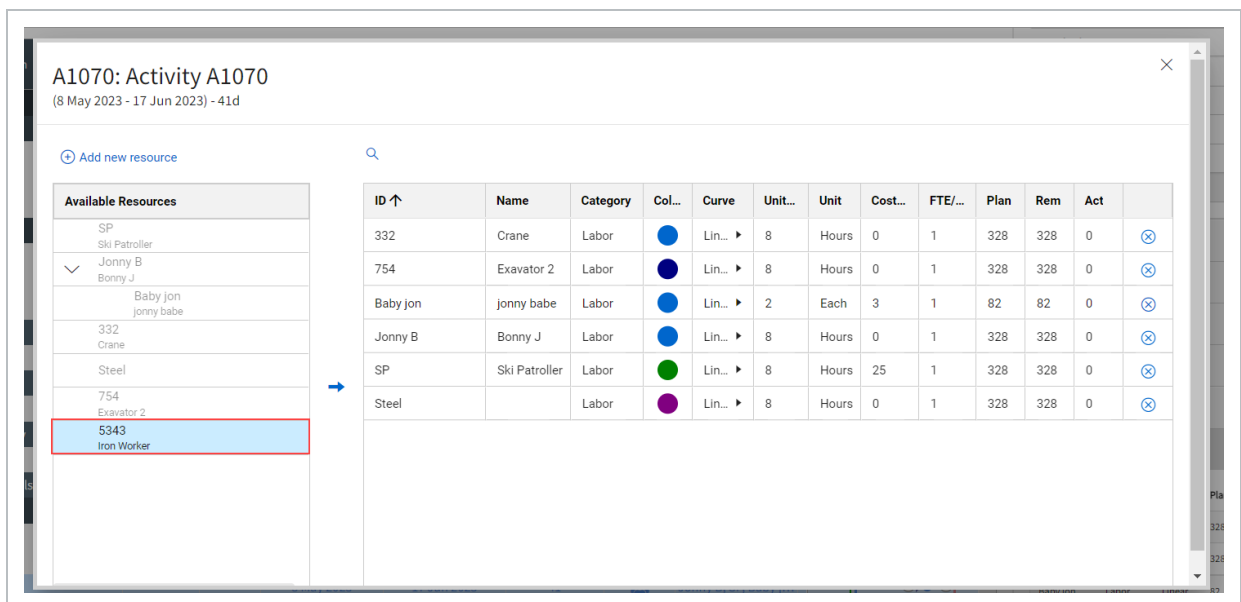**NOTE**

All available resources can be quickly found using the search function in the resource assignment window. If a resource cannot be found or a project-specific resource is to be made, see “Creating Project Resources via Resource Assignment” on for more information.

3. Once selected, click the **right arrow** to add the resource to the activity's Resource register.

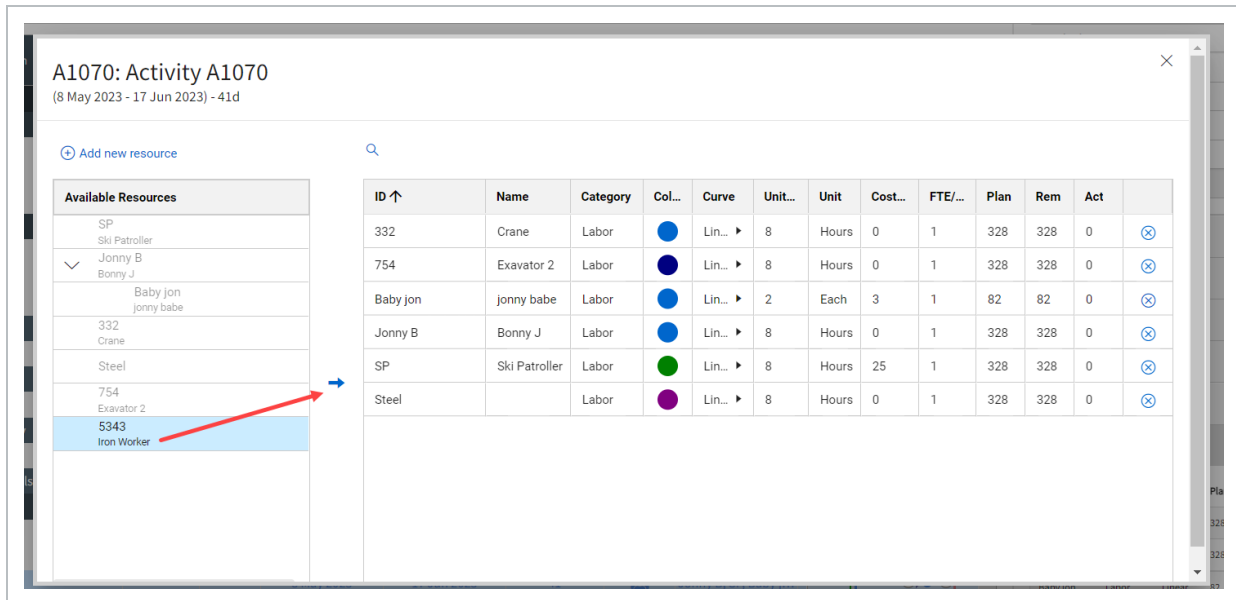**TIP**

Double clicking a resource will also add it to the activity's Resource register.

4. Once added, details for each resource can be modified for the activity. Fields that can be adjusted at this level include Curve, Units/d, Cost/Unit, FTE/Qty, and Plan.


ID ↑	Name	Category	Col...	Curve	Unit...	Unit	Cost...	FTE/...	Plan	Rem	Act	
332	Crane	Labor	●	Lin... ▶	8	Hours	0	1	328	328	0	⊗
5343	Iron Worker	Labor	●	Lin... ▶	8	Hours	0	1	328	328	0	⊗
754	Exavator 2	Labor	●	Lin... ▶	8	Hours	0	1	328	328	0	⊗
Baby jon	jonny babe	Labor	●	Lin... ▶	2	Each	3	1	82	82	0	⊗
Jonny B	Bonny J	Labor	●	Lin... ▶	8	Hours	0	1	328	328	0	⊗
SP	Ski Patroller	Labor	●	Lin... ▶	8	Hours	25	1	328	328	0	⊗
Steel		Labor	●	Lin... ▶	8	Hours	0	1	328	328	0	⊗

NOTE

If a resource is not available in the Project's resource register, a new resource can be created directly from the Resource Assignment window. See "Creating Project Resources via Resource Assignment" topic.

FILL DOWN

The Fill Down function lets you fill down a calendar, code or resource from the summary level. You select the items to fill down, the system fills down the selections and processes the items to all child level elements.

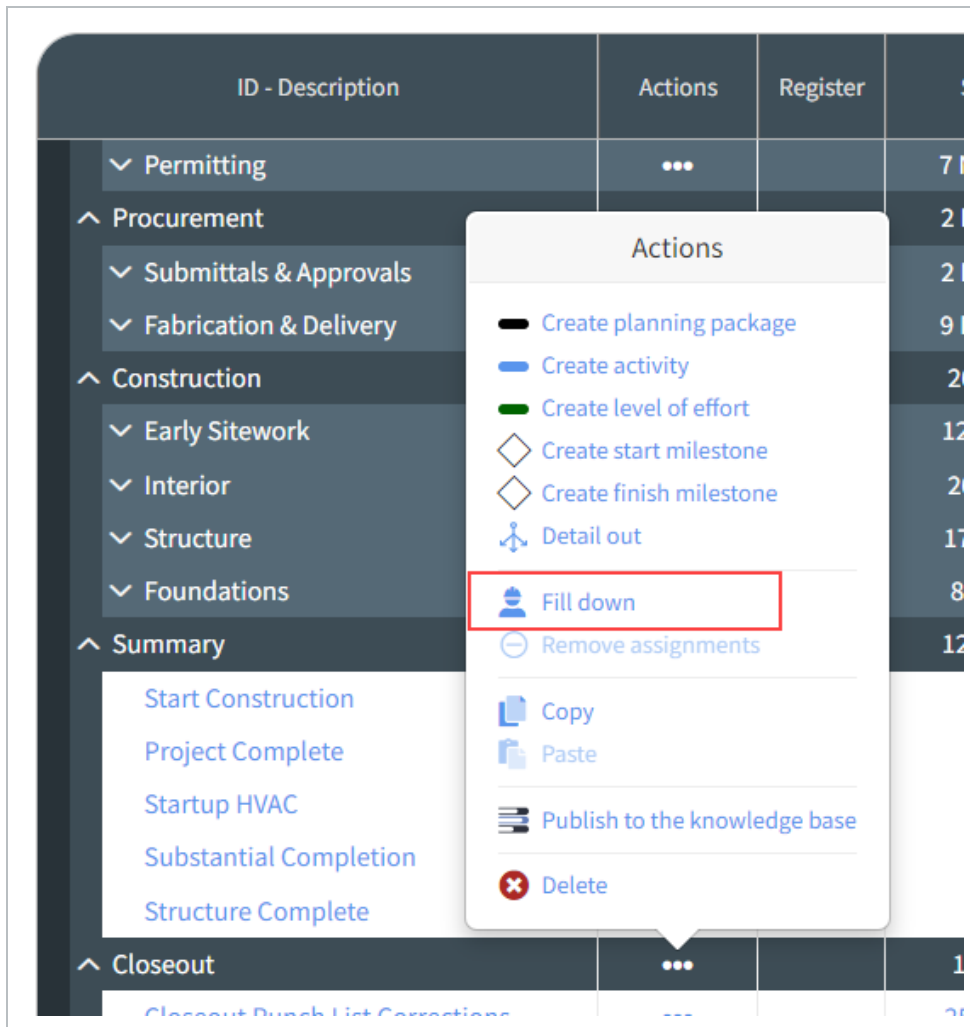


FILL DOWN FROM THE SUMMARY LEVEL

1. Identify the summary level planning package to assign resources to, and select the **Actions** icon.

Construction		11 Nov 19 30 Dec 21	557	...	👤	
Early Sitework		11 Nov 19 09 Nov 20	259	...	👤	
Entry & Access Roads		11 Nov 19 22 Jan 20	53	...	👤	

2. In the Actions menu, select **Fill Down**.

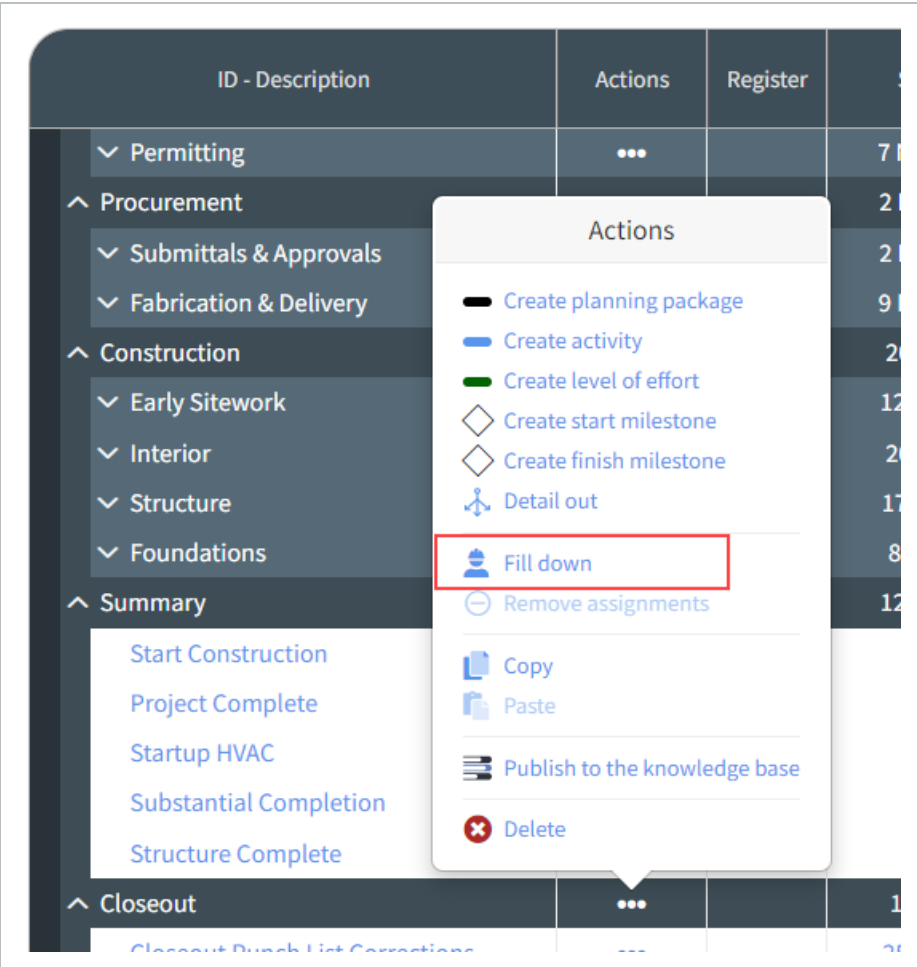

- The Fill down window appears

Fill down

Milestones

SCHED-514.LEV-HOST-002.0

CALENDAR

CODES

RESOURCES

Current calendar

724 Su-Sa 12:00A-1...

Available calendars

Search...

☐

KOS G 5d x 10hr w Holidays

☐

Turtle Season (2015-18)

☐

24x7 w/ Turtle Season

☐

0.Standard 5 Day w/ Hol

☐

Turtle Season (2015-18)

☐

24x7 w/ Turtle Season

☐

510 M-F No Holidays

☐

KOS G 7d x 10hr No Holidays

☐

KOS G 5d x 10hr w Holidays

Selected calendar

Selected codes

Clear all

Selected resources

Clear all

3. Under Calendar, choose a calendar from available calendars

Fill down

Milestones
SCHED-514.LEV-HOST-002.0

CALENDAR

CODES

RESOURCES

Current calendar

724 Su-Sa 12:00A-1...

Available calendars

Search...

☐

510 M-F No Holidays

☒

KOS G 7d x 10hr No Holidays

☐

KOS G 5d x 10hr w Holidays

☐

TIC - 5x10 (w/holidays)

☐

WMB.GLB.GD - 7 x 10 hour

☐

24 hours / 7 days

☐

7d-24h (no holidays continuous)

☐

510 Su-Th 7:00A-5:00P No Hol

☐

724 Su-Sa 12:00A-12:00A No Hol

☐

*508 M-F 8:00A-5:00P US Hol

Selected calendar

KOS G 7d x 10hr No Holidays

Selected codes

Clear all

Selected resources

Clear all

Cancel

Fill down

4. Click on the Codes and select any Activity Code.

Fill down

Milestones
SCHED-514.LEV-HOST-002.0

CALENDAR

Activity codes

Search...

*LEV Monthly R...

*LEV Schedule ...

*MP Ad Hoc Sel...

3 - Sub-Phase

LEV - Area

LEV - Cost Brea...

LEV - Discipline

LEV - Equipment...

LEV - Long Leads

LEV - RFP Numb...

LEV - Schedule I...

LEV - Tech Req...

CODES

LEV - Cost Breakdown Structure values

Search...

☒

540

RESOURCES

Selected calendar

KOS G 7d x 10hr No Holidays

Selected codes

Clear all

LEV - Co...Structure: 540

Selected resources

Clear all

Cancel

Fill down

5. Click on Resources and select any Resource value.

Fill down

Milestones
SCHED-514.LEV-HOST-002.0

CALENDAR CODES **RESOURCES**

Resource category

Search...

- All resources
- Installed Equipment
- Installed Material
- Labor
- Material
- New Category
- Nonlabor
- Ny kategori 1
- Supply
- Supply Non
- Unique

All resources values

Search...

- ☐ *EXPT Export Vessel
- ☐ *FLAY Flowline Vessel
- ☐ *SURV Survey Vessel
- ☐ Nbl Ops & Eng Serv Noble Operations and Engineering Services
- ☒ SPL-1 Subsea Package Lead - Doiron
- ☐ SPL-2 Subsea Package Lead - Pyron
- ☐ SPL-3 Subsea Package Lead - Timte
- ☐ SPL-4 Subsea Package Lead - Gaston
- ☐ SPL-5 Subsea Package Lead - Blockhus
- ☐ SPL-6 Subsea Package Lead - Anderson
- ☐ SPL-8 Subsea Package Lead - Tavassoli
- ☐ SPL-9

Selected calendar

KOS G 7d x 10hr No Holidays

Selected codes [Clear all](#)

LEV - Co...Structure: 540

Selected resources [Clear all](#)

Labor: Subsea Package Lead - Doiron

[Cancel](#) [Fill down](#)

- All assignments made from this window flow down to all subordinate activities.

NOTE

All available resources can be quickly found using the search function in the resource assignment window. If a resource cannot be found or a project specific resource is to be made, see the “Creating Project Resources via Resource Assignment” section for more information.

NOTE


Resources can still be further edited at the activity level even when set up from the summary level. Plan values are not editable when applying a resource at the summary level but can be adjusted at the activity level.

RESOURCE HISTOGRAM

After a schedule has been loaded with resources, Schedule can generate a resource histogram.


GENERATE A RESOURCE HISTOGRAM

1. In the Schedule's Planning View, select **View Options**.
 - A drop-down menu appears where you can switch the Resource Histogram on or off.
2. Switch the histogram from off to *ON*.




A histogram shows below the Gantt Chart. The resource histogram plots resource utilization over time depending on the following:

- **Resource Settings Configuration Options:** When the resource histogram is switched on, more settings become available for configuration.

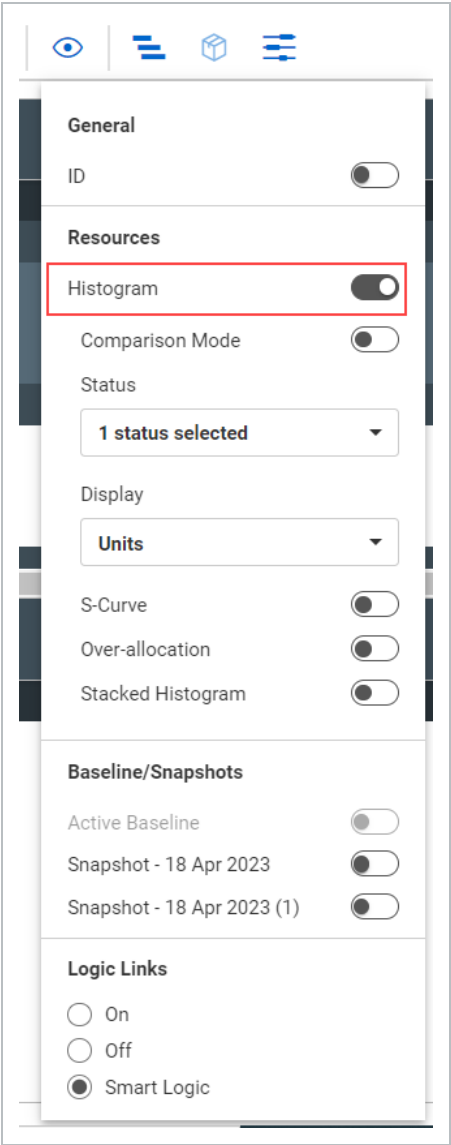


Setting	Function
Resource Histogram	You can switch the Resource Histogram view on or off.
Comparison Mode	Compares Current, Active Baseline, and Snapshots in the Resource Histogram.
Status	Filters histogram to show Planned, Actual resource quantities, Remaining or Remaining

Setting	Function
	Late.
Display	Adjusts the Y-axis of the histogram to show Units, FTE, or Cost.
Unit	The resource’s unit of measure.
S-Curve	Switches on or off the S-Curve on the resource histogram.

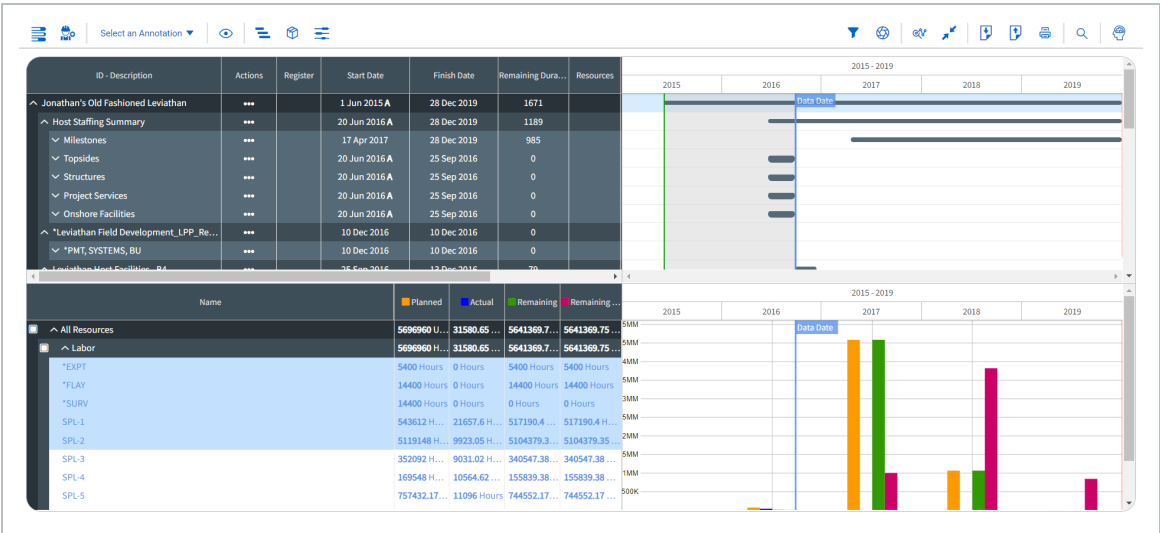

- **The activity or summary level selected in the Gantt Chart:** The resource histogram plots out data based on the activity or planning package selected in the schedule
 - *The zoom level selection:* The zoom level for the Gantt chart controls both the schedule and resource histogram X-axis units of time that is days, weeks, months, quarters, years or decades.



3. Set the Resource Setting Configuration Status to **Planned & Remaining**.

This populates the Resource Histogram with all planned and remaining resources for the activity or planning package selected.

Resource Histogram

Status

2 statuses selected

☒ Planned

☐ Actual

☒ Remaining

☐ Remaining Late

Over-allocation


Stacked Histogram

Name	Planned	Remaining
^ All Resources	5696960 Units	5641369.75 U...
^ Labor	5696960 Hours	5641369.75 H...
*EXPT	5400 Hours	5400 Hours
*FLAY	14400 Hours	14400 Hours
*SURV	14400 Hours	0 Hours
SPL-1	543612 Hours	517190.4 Hours
SPL-2	5119148 Hours	5104379.35 H...
SPL-3	352092 Hours	340547.38 H...
SPL-4	169548 Hours	155839.38 H...


4. Change the Resource Setting Configuration Display from Units to **Cost**.

- FTE stands for Full Time Equivalent, and is the count of people per time period.
- Burn rate is the percent planned per period of time.

- This adjusts the Y-axis values from resource quantities to dollars

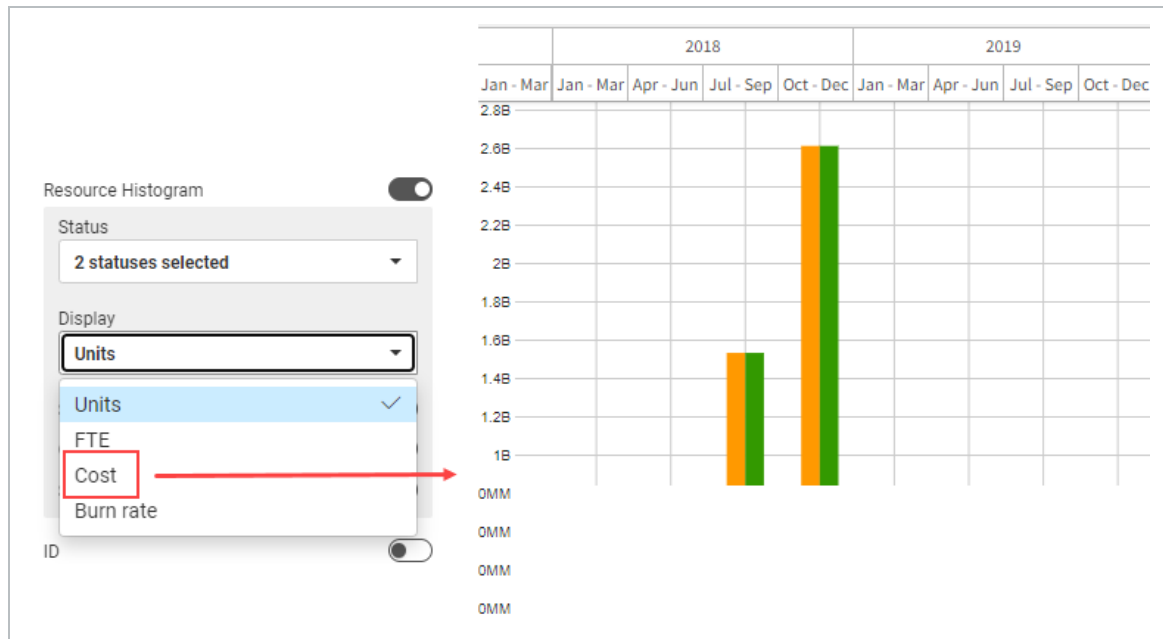

5. Switch on the **S-Curve**. This overlays the S-Curve on the Resource Histogram.

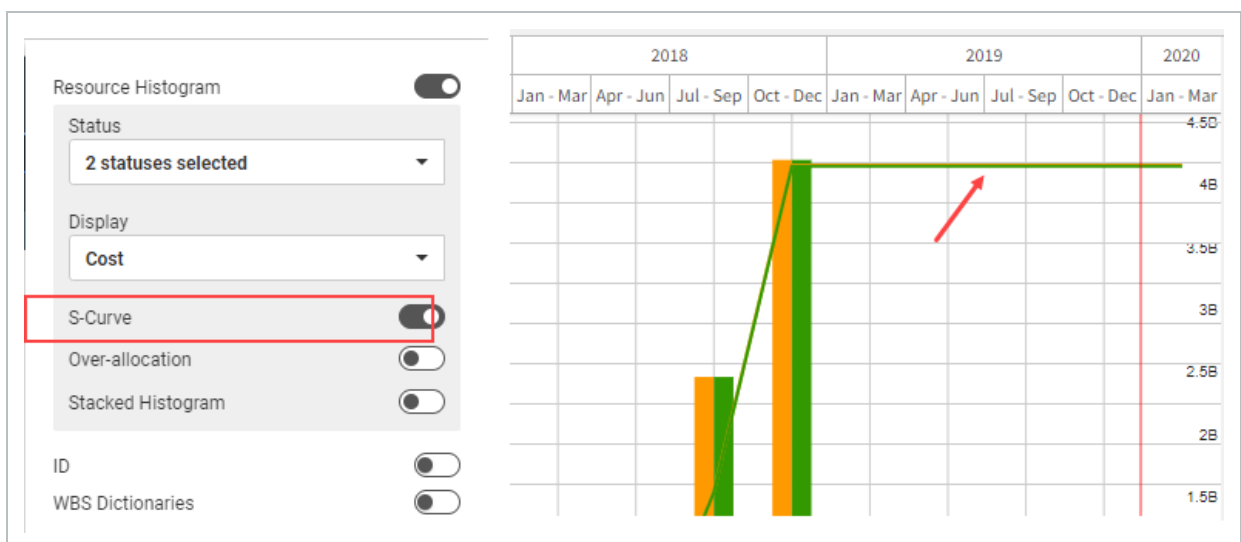
**NOTE**

S-Curves reflect cumulative data. As the values increase over time, this reflects the accumulation of resource units/FTE/cost, depending on settings, over time.

FILTERING BY RESOURCE

Filtering by resource only applies if the stacked resource histogram is turned to *On*. In the filter functionality, the Gantt chart & resource histogram can be filtered to see planning packages and activities assigned specific resources. When the resource histogram is switched on, it can be used as an interactive filter as well. Selecting a Resource Name listed in the histogram or any of the resource bars will filter down the Gantt Chart and Resource Histogram to show only data pertaining to the information selected.


In the image below, the Resource Histogram is filtering based on the selected resource: *Concrete Finisher*.

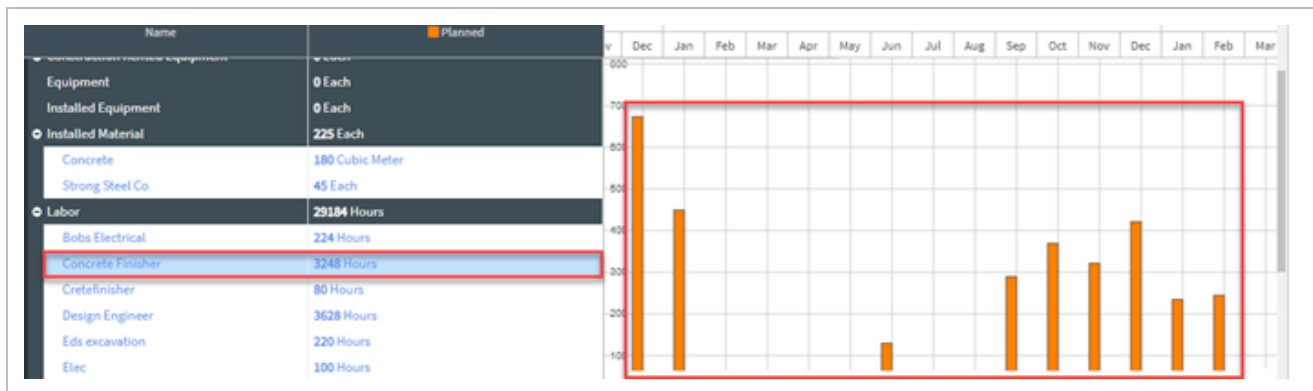

Additionally, to modify or disable the resource filtering, users may click the filter icon to make adjustments to the filter parameters.


HISTOGRAM COMPARISON MODE

In View Options, you can view the histogram in comparison mode, when enabled.

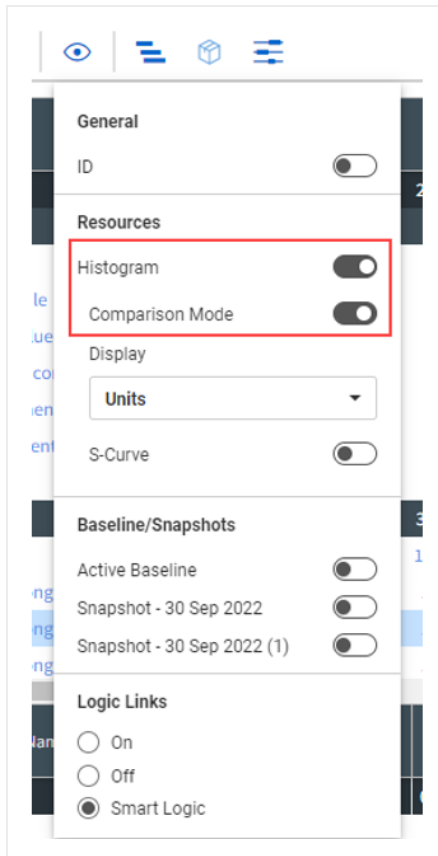


When the Comparison mode toggle is set to On, the baselines and snapshots that exist in the Baseline/Snapshot Management show as a graph with the current baseline. The histogram compares resources rolled up to the category type and shows you resources as they trend.


Each line in the graph represents a baseline, snapshot, and the current estimate.

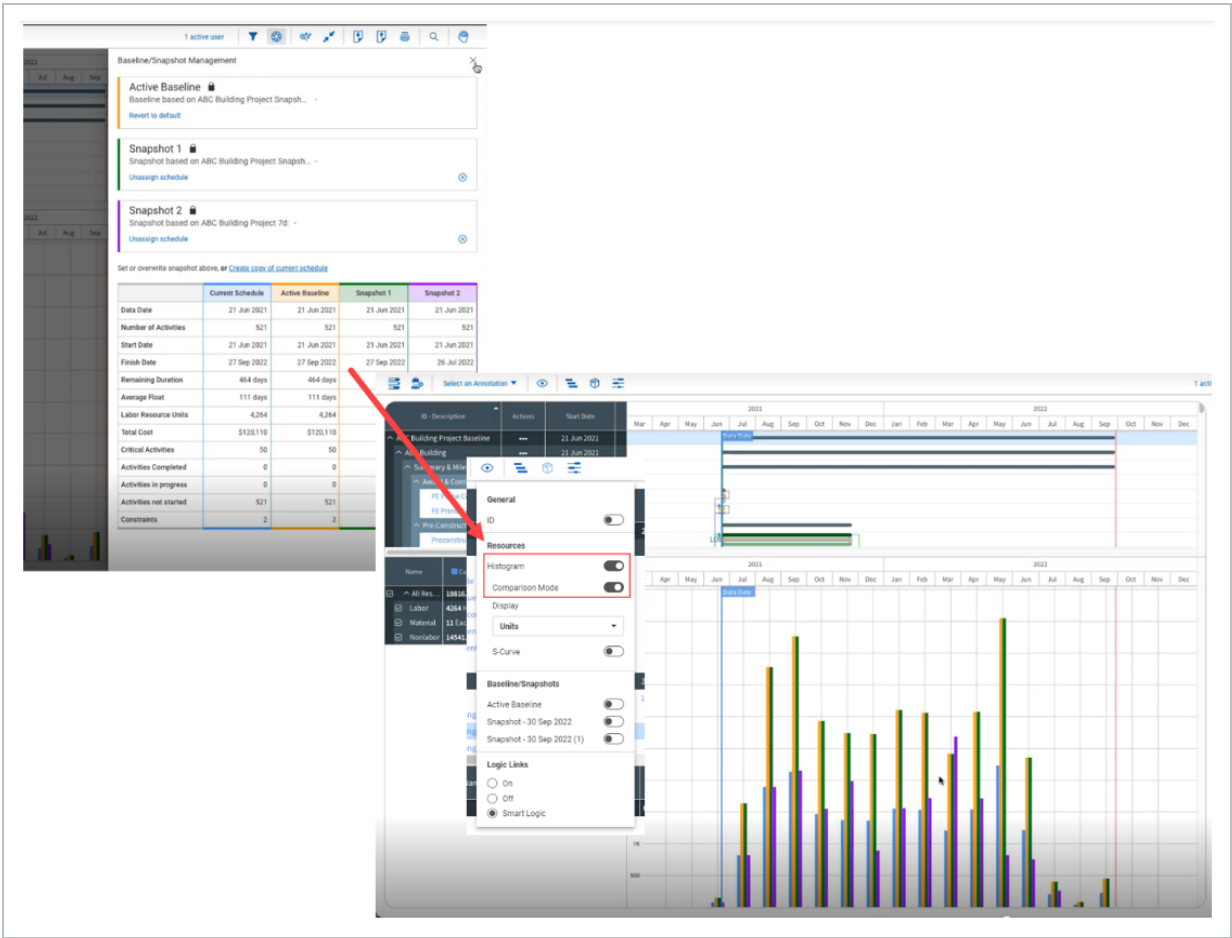

The histogram graph can now also be shown in units and burn rate.

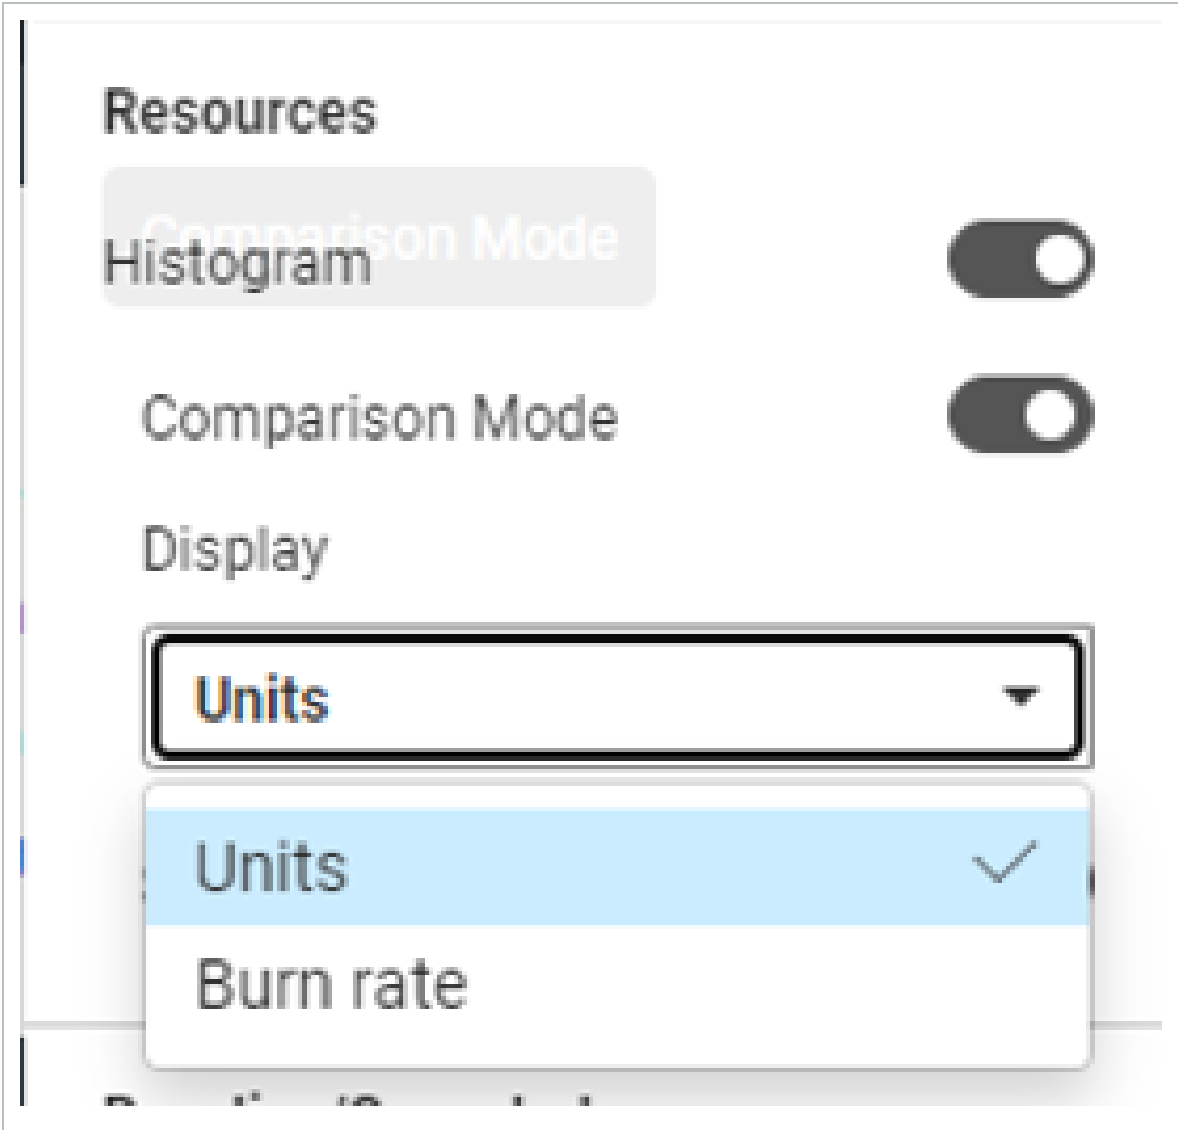


You can also view the histogram with an S-Curve that shows you a cumulative trend line for each baseline, snapshot and current.

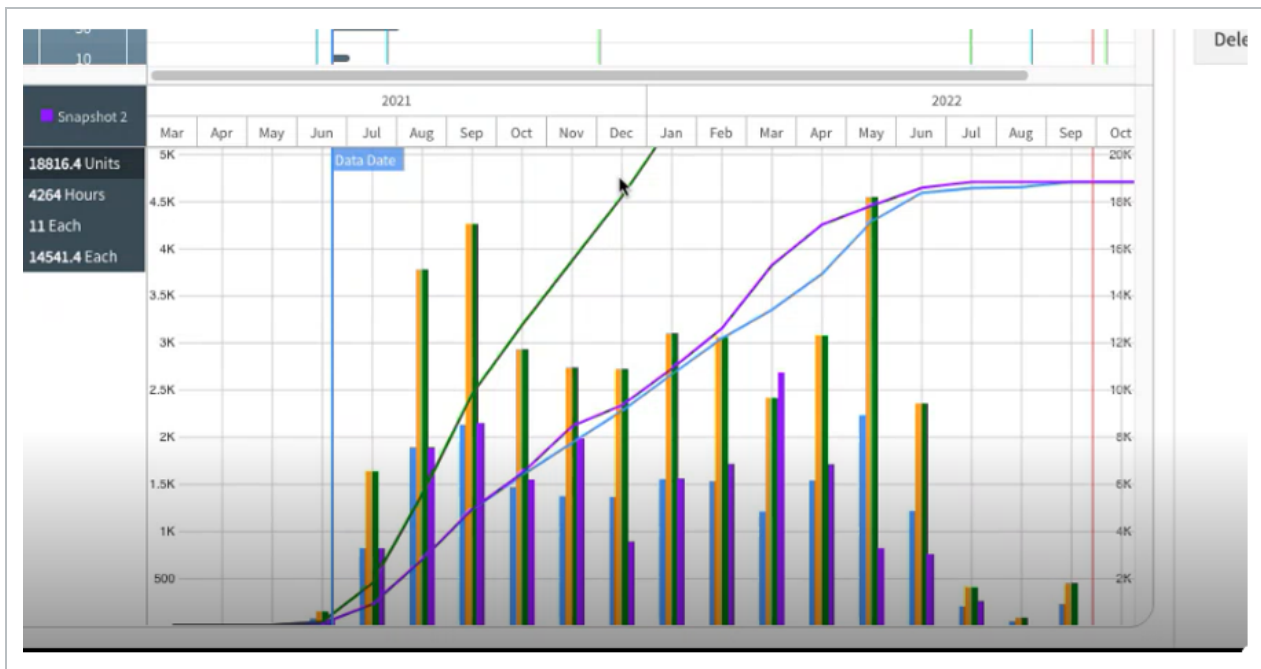

EXPORT ASSIGNMENTS

Schedule export functionality includes the ability to export resource assignments. Select the **Export** icon, then select the **Resource Spread** export type from the drop-down menu.

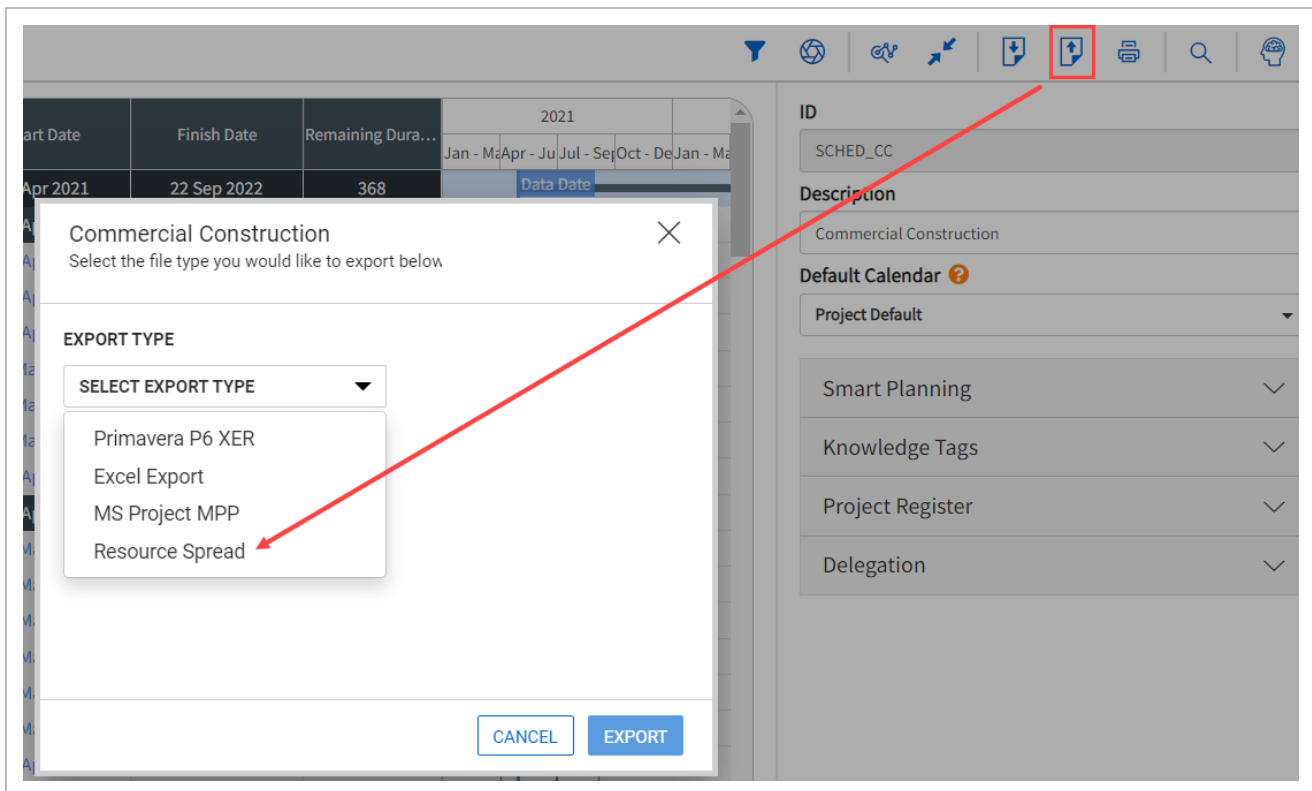


PROJECT SPECIFIC RESOURCES: PROJECT CONFIGURATION SETUP

Resources in a Project are either global resources or project specific resources. Global resources automatically populate a project's resource register from the Knowledge Base. If a resource is not available from the established global resources, project specific resources can be set up.

Project specific resources are useful when the resource utilized is unique to that project and not applicable across the organization.


To establish project specific resources:

1. Select Schedule Configuration from the project drop-down menu.



2. Select the **Resources** tab in the Knowledge Base.

This brings you to the project-level resource register



The Project level resource register functions the same as the Knowledge Base. See Setting up Resources for information about how to add resources and use the Import/Export functionality in the Resources register

Acme Corp - 22.10 Brian Gros... / Commercial Con... / Schedule Configuration

GENERALCONTRIBUTORSKNOWLEDGE TAGSCALENDARSRESOURCESSIP RESOURCESPROJECT SUITE

ID	Name	Category	Color	UoM	Default Units/d	Cost/Unit	Assignments	
FDN	Foundations	Labor		Hours	8.00	100.00	15	
CNC	Concrete	Labor		Hours	8.00	200.00	22	
GRD	Grading	Labor		Hours	8.00	150.00	7	
STL	Steel	Labor		Hours	8.00	350.00	7	
INT	Interiors	Labor		Hours	8.00	225.00	15	

Schedule possesses the concept of global and project specific resources. When you create a schedule, it does not populate the resources in the Schedule Configuration window, but you can import resources from the Knowledge Base to use in your schedule.

TIP


Project specific resources can also be added from the resource assignment window in the planning view. See the Resource Assignment for more information.

CREATE A PROJECT-SPECIFIC RESOURCE VIA THE RESOURCE ASSIGNMENT WINDOW

Project Specific Resources can also be created from the Resource Assignment window in the Planning view.

CREATE A PROJECT SPECIFIC RESOURCE VIA THE RESOURCE ASSIGNMENT WINDOW

1. Without having any resources selected, click the **plus +** icon.

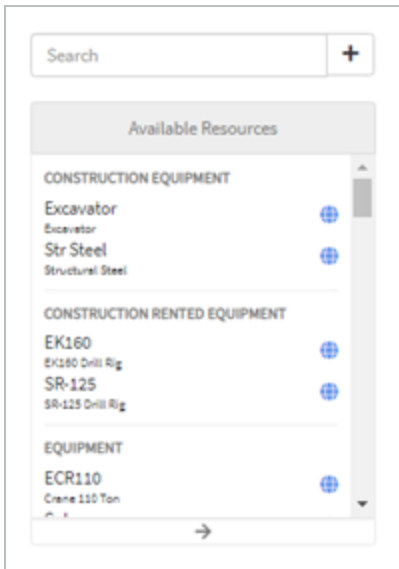

- The Add Resource opens to add a project specific resource

2. Fill out the project resource information and then click **Add**.


RESOURCE HISTOGRAM VIEW

The Resource histogram shows the assigned resources for the project in the histogram window. Assigned resources can be viewed based on Planned, Remaining, Actual, and Remaining Late statuses.

Use the following instructions to enable the Resource histogram view.


ENABLE THE RESOURCE HISTOGRAM VIEW

1. In the toolbar, click the **View options** icon.

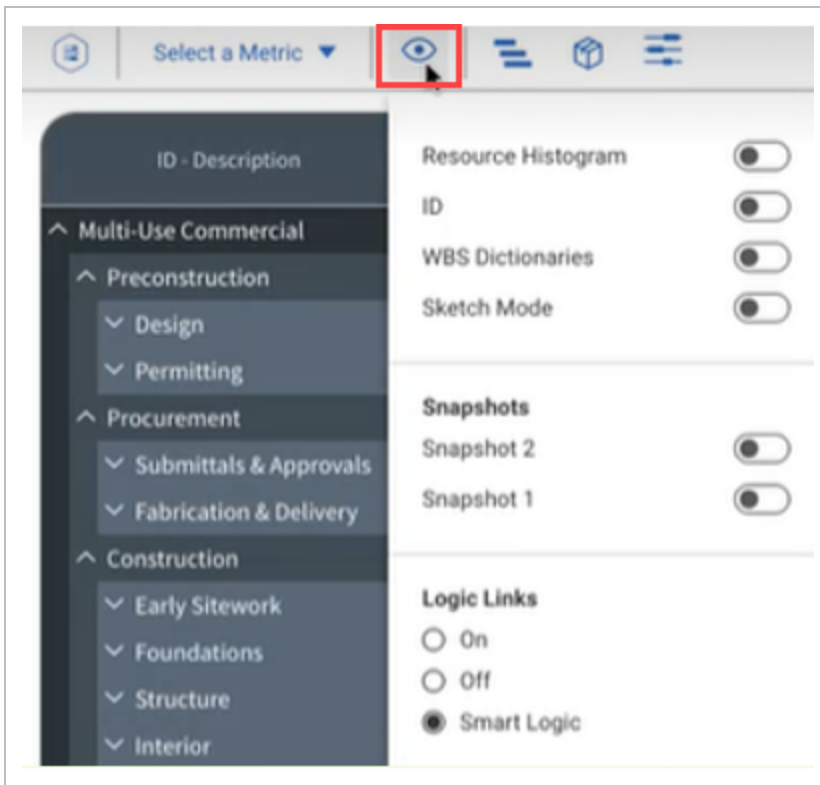


2. Switch the Resource Histogram toggle to enable the Resource histogram.

The view options menu now shows more features in the gray box area. Resources show in the bottom left of the screen. To the right, the histogram window shows.

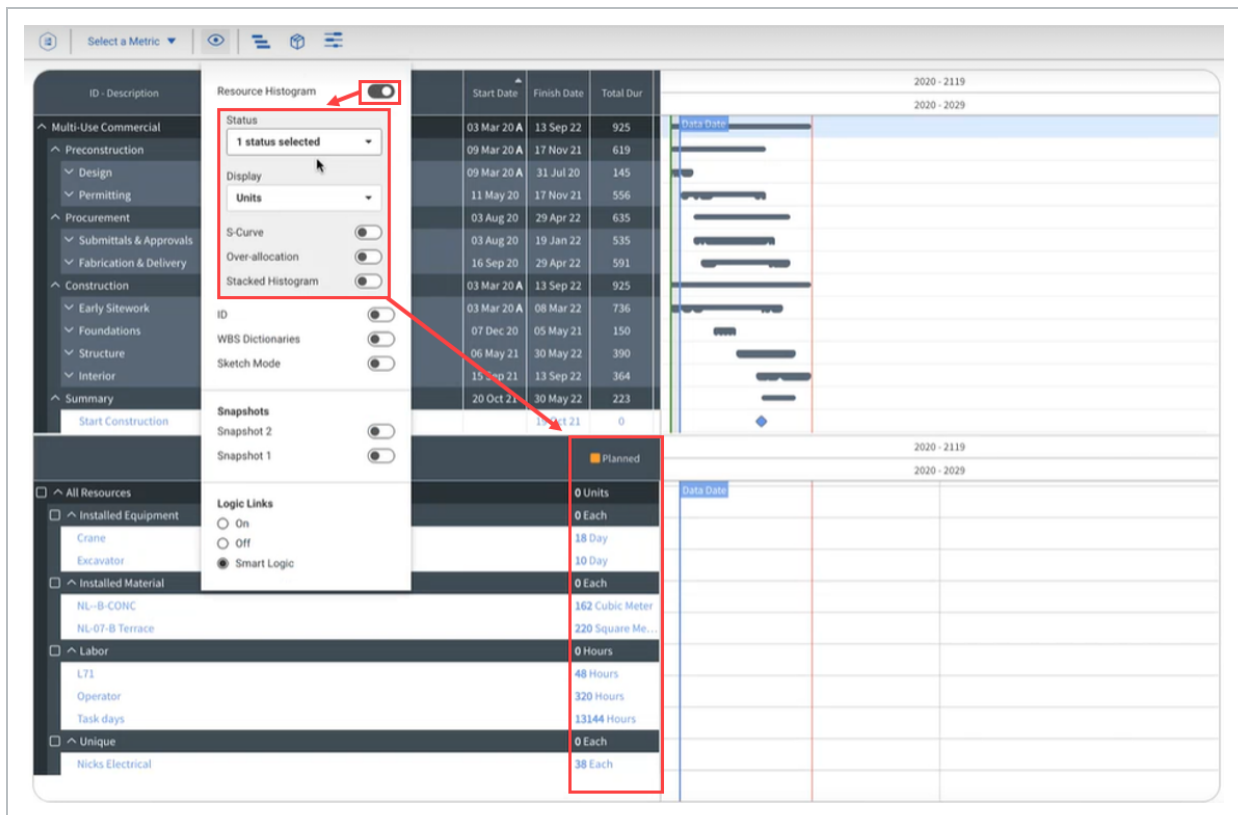


- To view a specific date range for resources, on the right side of the screen, select the **Zoom level** icon.



The Zoom level is set to Month in the following images.


The histogram now shows resources allocated based on the month. By default, only the Planned status is selected.

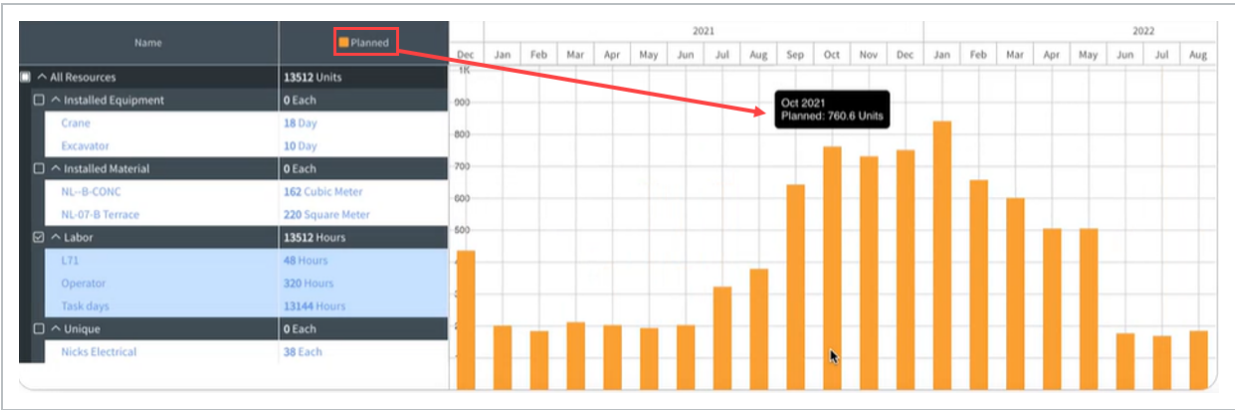


Use the following instructions to add statuses to the histogram.

ADD STATUSES TO THE RESOURCE HISTOGRAM

1. Select the **View options** icon, and then select the **Status** drop-down menu.
The Planned status is selected by default.
2. Select another status to show on the histogram that has not been selected previously.

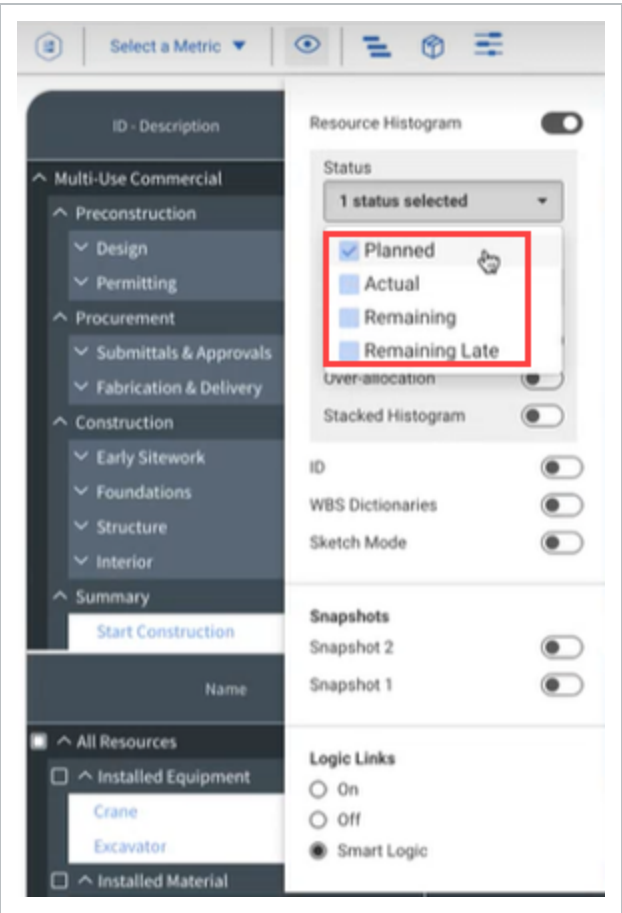

The additional statuses show the resource bar in different colors. You can hover over the bar to view the data or you can review the resource data in the left column. The image below shows that the Planned and Remaining Late statuses currently occupy the histogram.

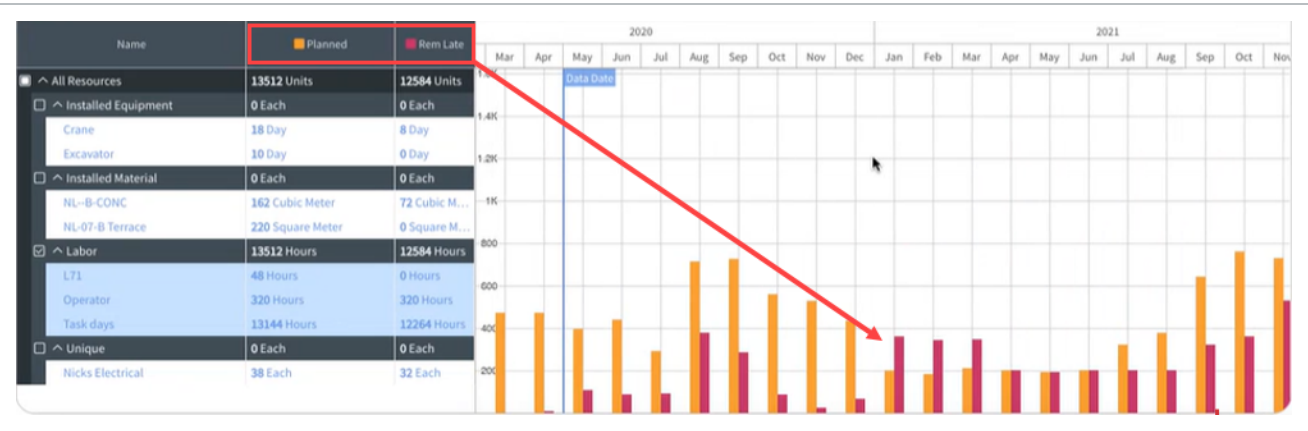

In the columns on the left of the screen, the status selected brings in the units associated to it. In this case, the remaining late units are brought in because the Remaining late status is selected. You can see those units spread incrementally across the project.

NOTE

The data date is also shown on the histogram. You can add the data date and the finish date of the project for reference so that you know the boundaries of your project.


S-CURVE

In addition to the incremental curve, you also have a cumulative curve. This is also known as the S-curve. If you toggle the S-curve *On*, you can see two S-curves are planned on the histogram.


Use the following step by step to enable the S-curve in the Resource histogram.

ENABLE THE S-CURVE

1. In the toolbar, click the **View options** icon.
2. Select the **Status** drop-down menu, and then select **Remaining** and **Remaining Late**.
3. Switch the S-curve toggle to enable the S-curve.

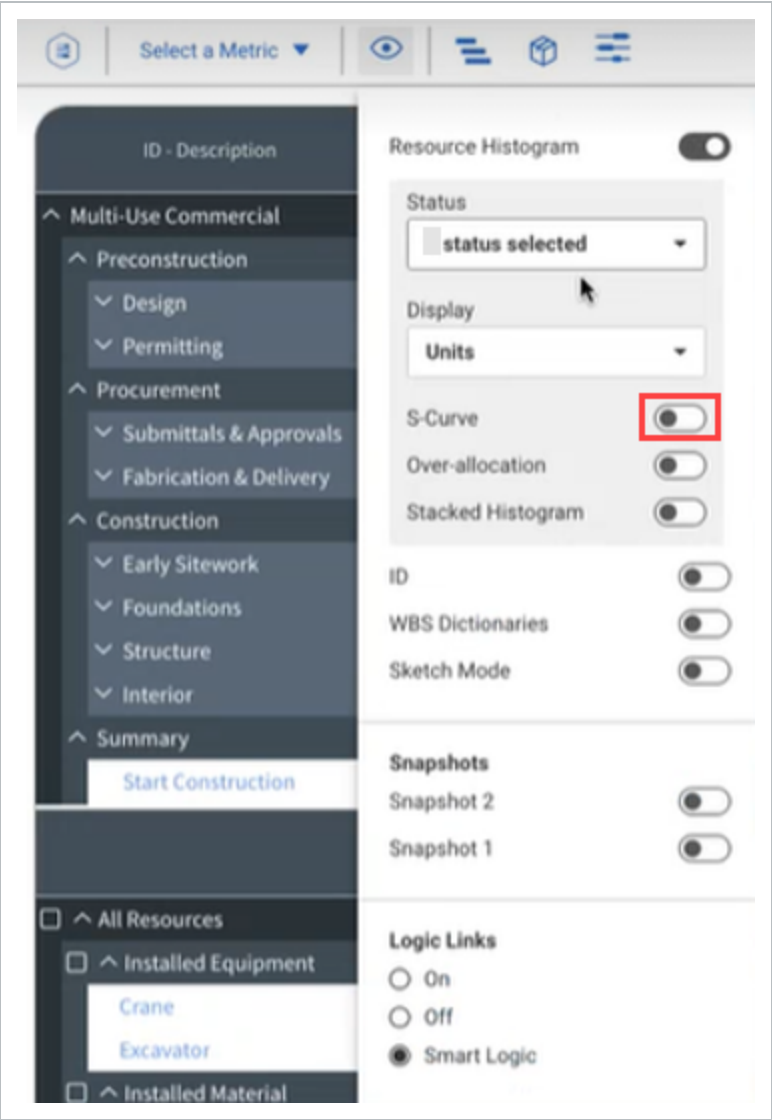


Two S-curves show on the histogram. At the conceptual phase of a project, you are shown these early and late dates. The space between those curves is the float on the project.

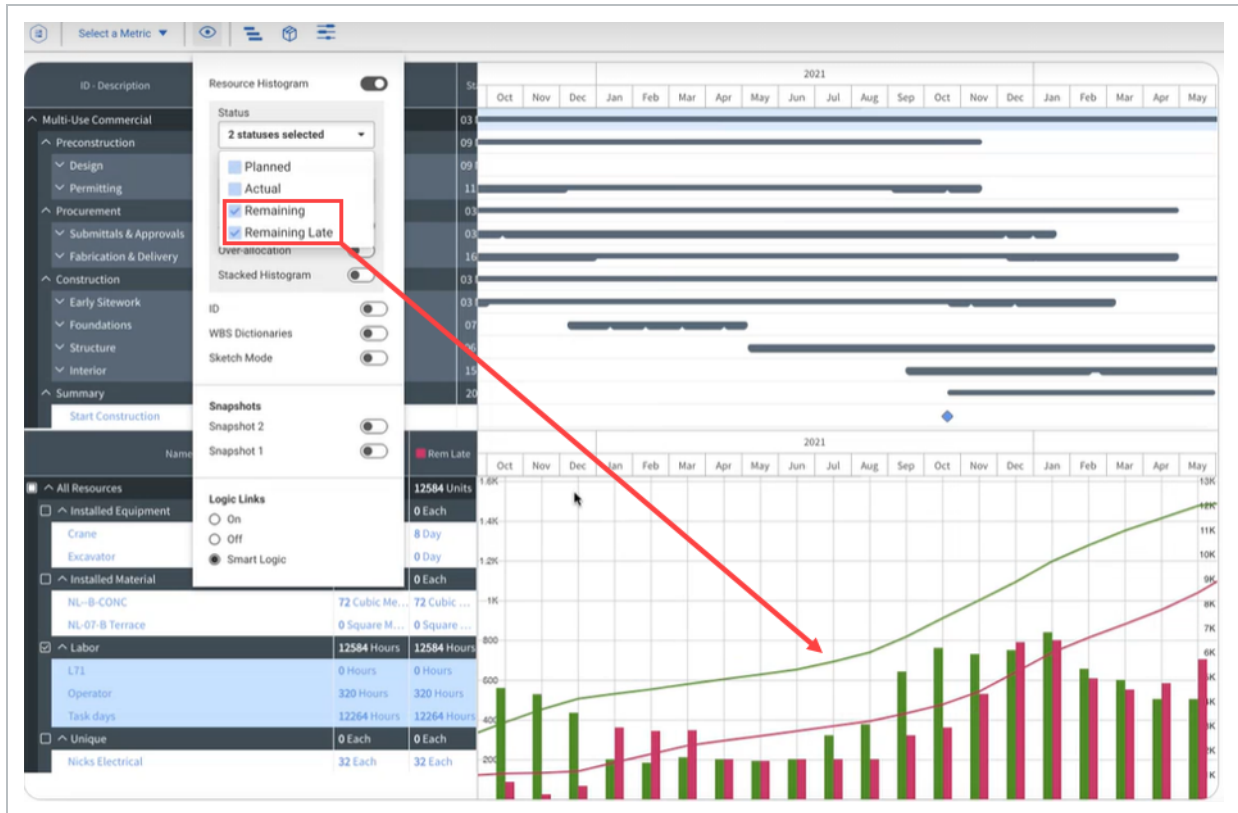


ACTUAL STATUS ENABLED WITH S-CURVE

With the Actual status enabled with the S-curve lines, you can see that the Actual line ends where the Remaining Late and Remaining lines start. This is your job to date running total for the project. For example, you had certain man-hours earned to date and the remaining hours to earn start from what you have earned to date. You started from the Actuals line in blue and then you go forward from there. The Actual line end where remaining units begin. The Remaining and Remaining late lines starts where actuals for the project end.

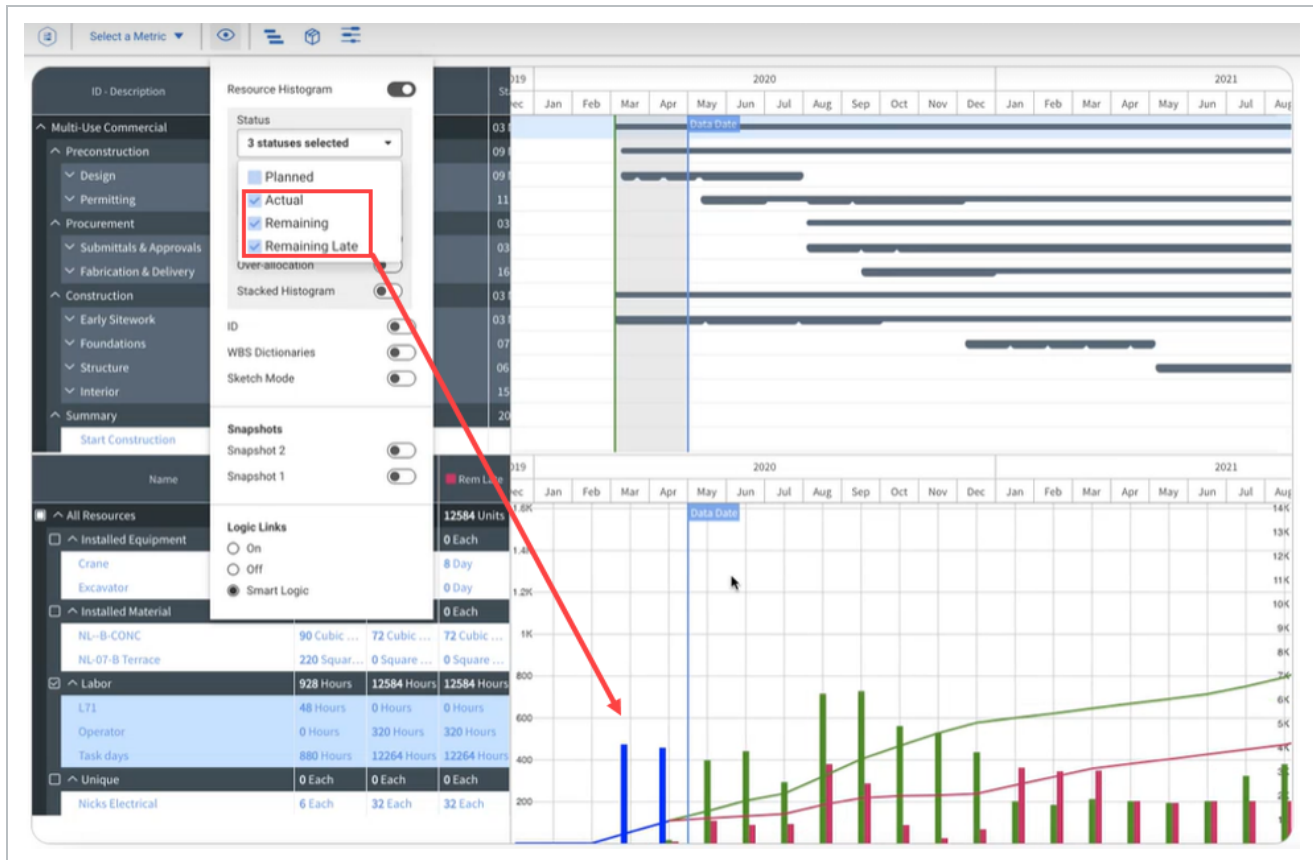

OVER-ALLOCATION

Over-allocation shows you where you are over allocated based on your resource limits. For example, where you planned for more resources needed to complete the work than you currently plan to have on site. This means in the month of August and September, the bars above the line represent a need for more resources. To fix this over-allocation, you can move activities around to flatten that peak, add more resources, or extend the duration of your activities.

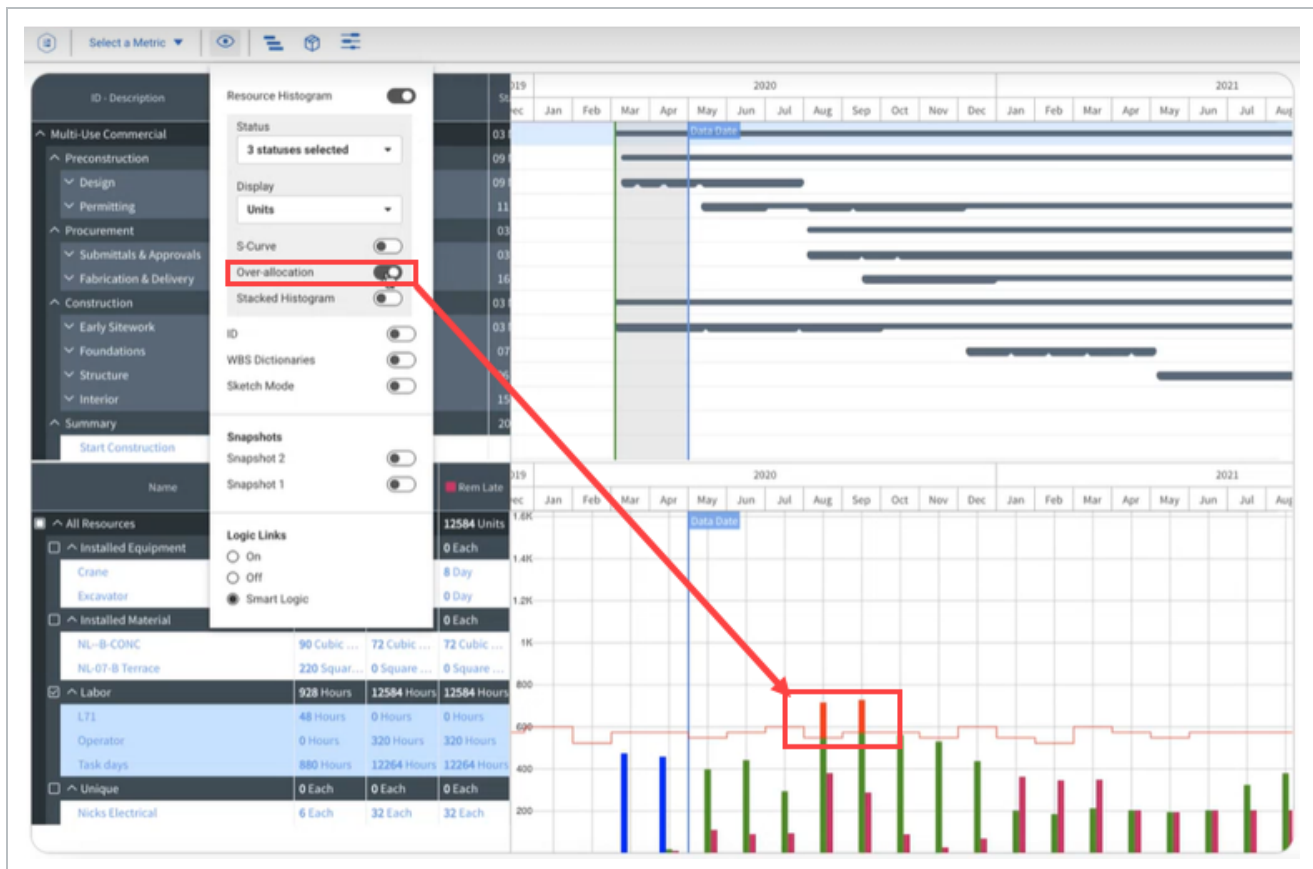

The line across the histogram represents the activity calendars on which these resources are assigned. Weekends, holidays, and exceptions make the line drop because you are working fewer days in that given period. During those periods, you have fewer days to complete the work.

Use the following step by step to enable Over-allocation in the Resource Histogram.


ENABLE THE OVER-ALLOCATION

1. In the toolbar, click the **View options** icon.
2. With Resource Histogram enabled, switch the Over-allocation toggle to enable Over-allocation.

STACKED HISTOGRAM

The Stacked Histogram shows the different resources in the histogram using different colors. Hover over the different colored tool tips to show which resource that color represents. The tool tip also gives you data for the specific resource and period.


The Stacked Histogram contains advanced filtering capabilities, letting you click on a specific colored bars in a specific time period. Schedule then builds a filter to show that resource for that time period in the Gantt chart.

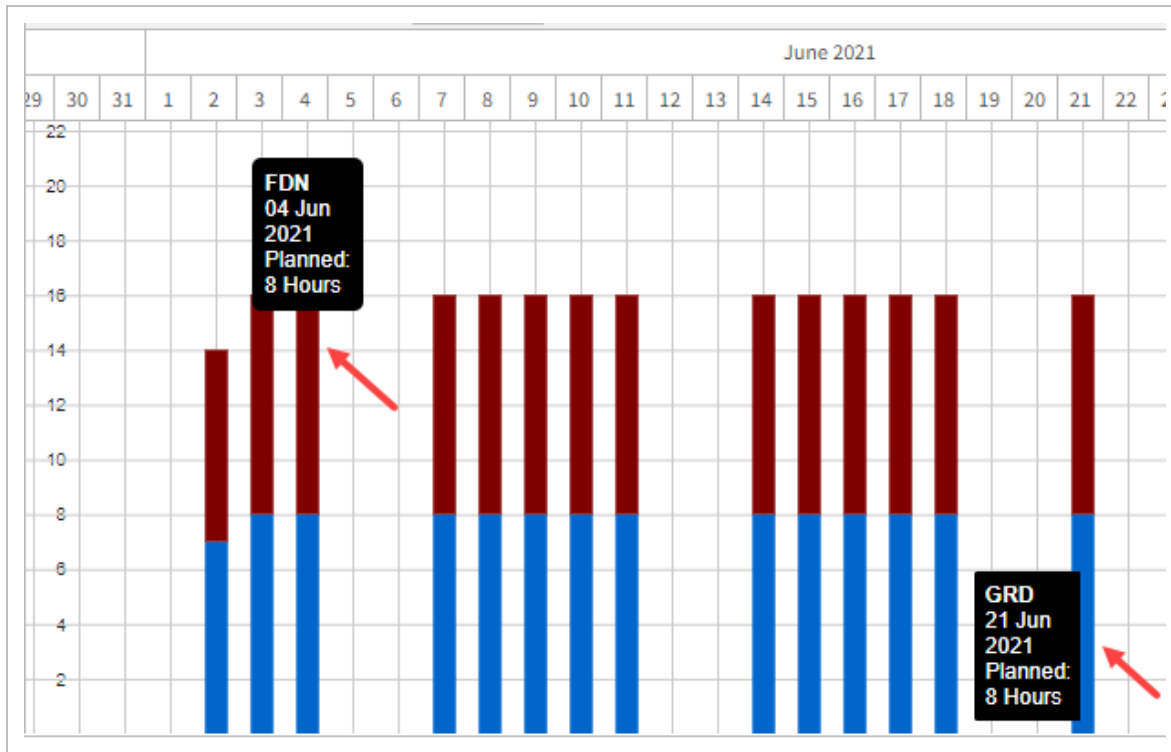

Use the following step by step to enable the Stacked Histogram.


ENABLE THE STACKED HISTOGRAM

1. In the toolbar, click the **View options** icon.
2. With Resource Histogram enabled, switch the **Stacked Histogram** toggle on.

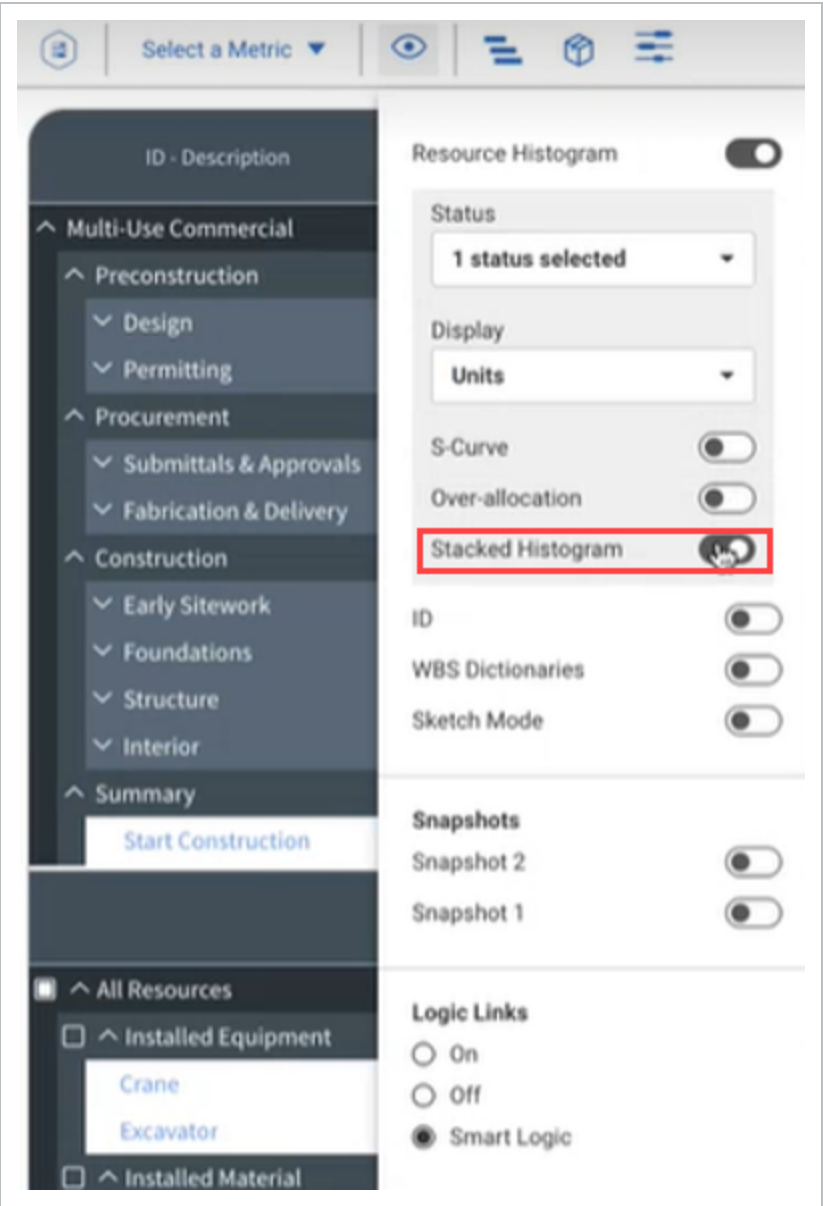

Stacked Histograms are shown on the histogram.

- 3. Hover over the different colored bars to show the tool tip information.

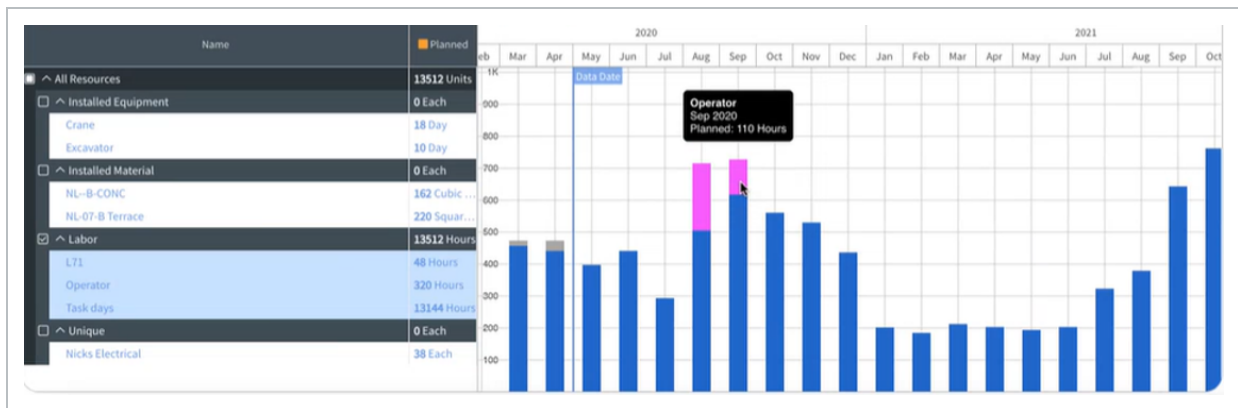


CHANGING THE STACKED HISTOGRAM COLORS

Similar to the color column in the SIP resources, the Stacked Histogram colors are controlled at a project level in the Project Configuration.

Use the following step by step to edit the column colors for the stacked histogram.

EDIT STACKED HISTOGRAM COLORS

















1. Select the navigation drop-down menu.
2. Select **Schedule Configuration**.



3. Select the **Resources** tab.

Resources that have been added to the Resources tab have a column labeled Color.

4. Select the color cell in the row of the resource you want to edit. Then choose a different color for that resource.

<div> <div>GeneralContributorsKnowledge TagsCalendarsResourcesSIP ResourcesProject Suite</div> <div> Add new resource <div> <div></div> <div></div> <div></div> </div> </div> </div>								
ID	Name	Category	Color	Unit	Default Units/d	Cost/Unit	Assignments	
Task days		Labor ▶		Hours	8	100	76	
NL-07-B Terrace	NL-07-B (Mat) Constr ~ Terrac	Installed Material ▶		Square Meter	22	100	1	
NL-B-CONC	NL-07-B (Mat) Constr ~ Concre	Installed Material ▶		Cubic Meter	9	100	2	
Nicks Electrical	Nicks Electrical	Unique ▶		Each	1	100	2	
Operator	Operator	Labor ▶		Hours	10	100	1	
Excavator	Excavator	Installed Equipm... ▶		Day	1	100	1	
Crane	Crane	Installed Equipm... ▶		Day	1	100	2	
L71	Mechanical (Labor)	Labor ▶		Hours	8	100	1	

BURN RATE


When Burn Rate is enabled, it shows as a percentage on the x-axis. The Burn rate is the percent of total man-hours in a period. The equation is the following:

Month total for a resource ÷ project total for resource(s) = Burn rate percentage


Use the following step by step to enable the Burn rate on the Resource Histogram.

ENABLE THE BURN RATE

1. In the toolbar, click the **View options** icon.
2. Select the **Display** drop-down menu.
3. Select **Burn rate**.

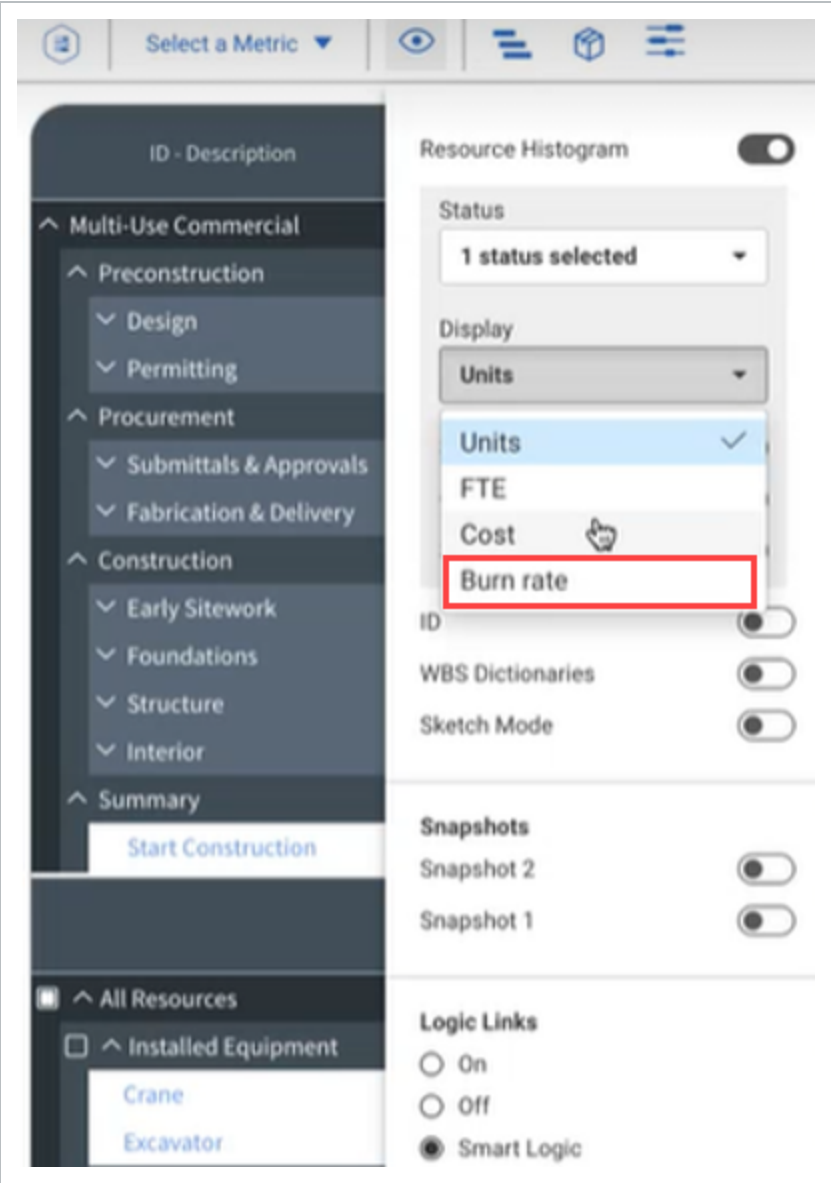

The histogram shows Burn rate data.

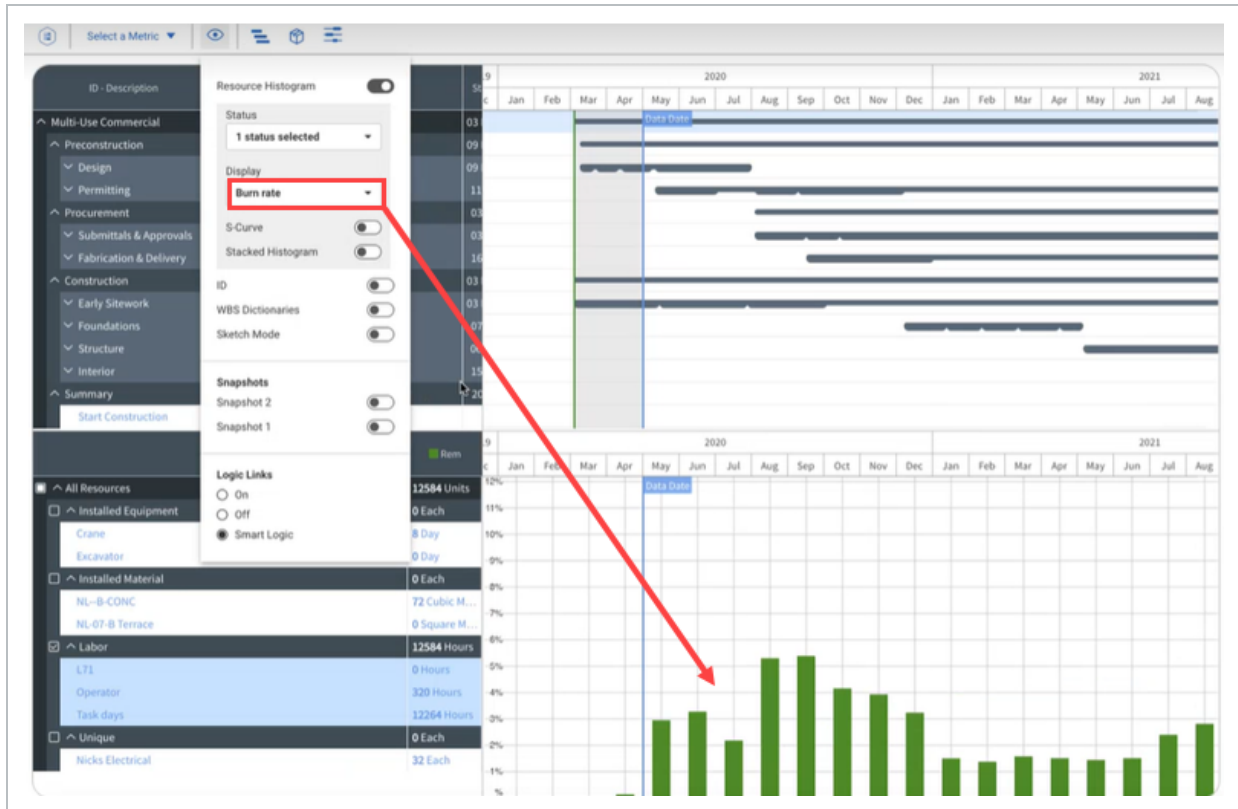

EXCEL EXPORT

The Excel export feature lets you use the exported project file for reporting since it is a flat data source.

When you export from Schedule, the data from the entire project is exported including the following tabs:

- WBS
- Activity
- Logic
- Codes
- Udfs
- Resource Assignments

Each tab provides information that can be built upon each other. This lets you pivot on different data to create slicers for your reports. The Excel export also lets you make bulk edits to a schedule. You can build an entire schedule in Excel and then import it back into Schedule. This includes logic, resource assignments, and the WBS. Each tab contains the following fields:

- Required
- Optional
- Validated
- Ignored


When considering what to import back into a Schedule project, you have the option to delete some tabs and import in only the specific tabs that were changed.

NOTE If there are no changes to the file imported back into a Schedule project, the import shows no changes have been made.

Use the following step by step to export a Schedule project.

EXPORT FROM HISTOGRAM

1. Select the **Export** button on the right of the screen.
 - The Resources Building dialog box is shown

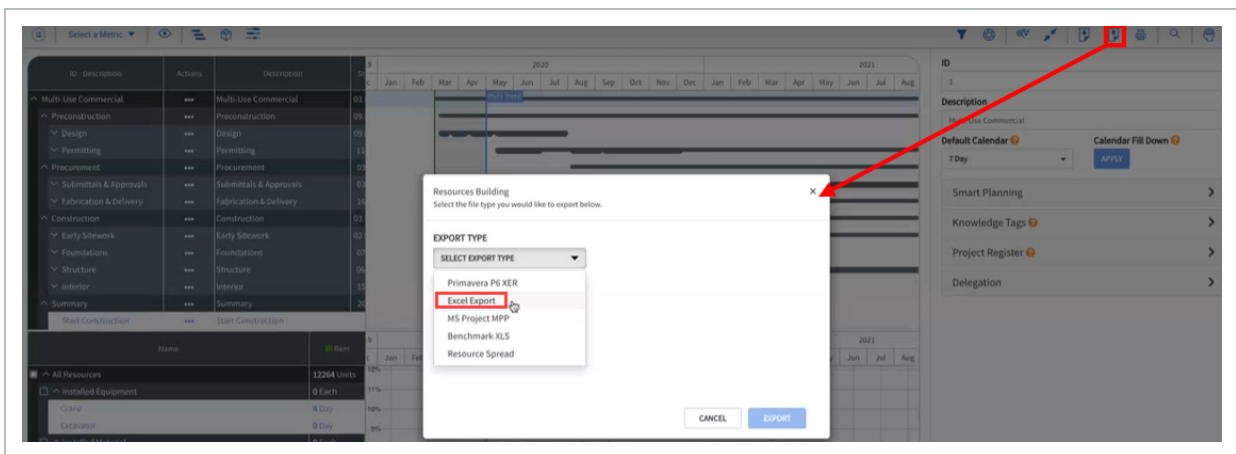

2. Select the **Export Type** drop-down menu.
3. Select **Excel Export**, and then select **Export**
 - An Excel project file opens

A9					
	A	B	C	D	E
1	REQUIRED	Field is required for import			
2	OPTIONAL	Field is optional for import			
3	VALIDATED	Field must match master data available in application			
4	IGNORED	Field not to be populated			
Notes:					
5	1. WBS ID must be unique				
6	2. When a WBS is deleted, all child WBS's will be deleted and activities will be placed in the root of the project				
7	WBS ID	WBS Description	Cost	Deliverable	Deliverable Quantity
8	Test	Text	Numeric	Text	Numeric > 0
9	256	256		128	Text: "Yes"
10	1	Use Commercial	7200		
11	1.1	Construction	6		
12	1.1.1	Design	6		
13	1.1.2	Permitting	6		
14	1.2	Procurement	6		
15	1.2.1	Submittals & Approvals	6		
16	1.2.2	Fabrication & Delivery	6		
17	1.3	Construction	7200		
18	1.3.1	Early Sitework	7200		
19	1.3.1.1	Parking Structure	7200		
20	1.3.1.2	Utilities Structure	6		
21	1.3.1.3	Entry & Access Roads	6		
22	1.3.2	Foundations	6		
23	1.3.3	Structure	6		
24	1.3.3.1	Floor 1	6		
25	1.3.3.2	Floor 2	6		
26	1.3.3.3	Floor 3	6		
27	1.3.5	Interior	6		
28	1.3.5.2	Floor 2	6		
29	1.3.5.1	Floor 1	6		
30	1.5	Summary	6		
31	1.4	Closeout	6		
32					
33					
34					

Use the following step by step to import an Excel file into a Schedule project.

IMPORT INTO THE SCHEDULE

1. From Schedule, select the **Import** button on the right of the screen.
2. Browse to the file you want to import back into Schedule.
3. Select **Import**.

NOTE

An error message can be shown during the Import process. This error message can show where an error occurred in the Excel template and where the fix needs to be made. The import still brings in the data that is correct, but it skips over the data that generated the error. The error is then logged in Schedule.

This page intentionally left blank.


LESSON 7 – SCHEDULING

SCHEDULING OVERVIEW

SCHEDULING


SETTING SCHEDULE PROGRESS ATTRIBUTES

1. Click the **Scheduling** icon in the Smart Planning tab.

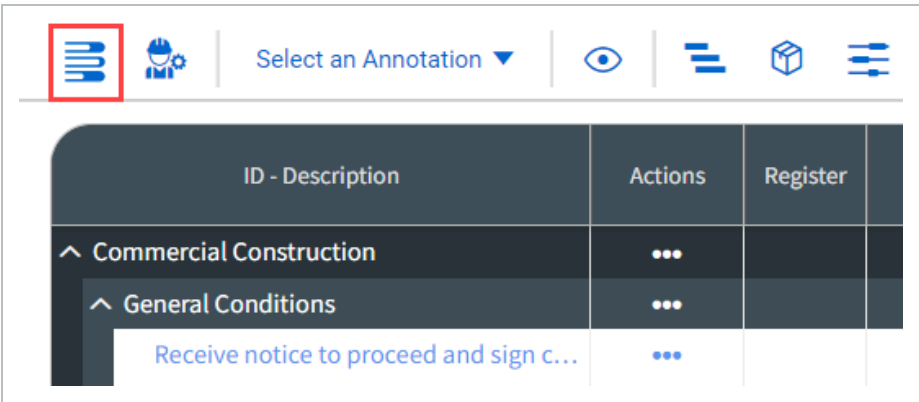

2. Populate the following information on the General tab:
- **Project Start** - This is the project start date.
 - **Data Date** - Sets the “current” or as-of date that you are looking at in the system.
 - **Project Finish** - This is the project finish date.
 - **Auto CPM** - This should generally be set to *On*, so logic is automatically applied to

items in your schedule.

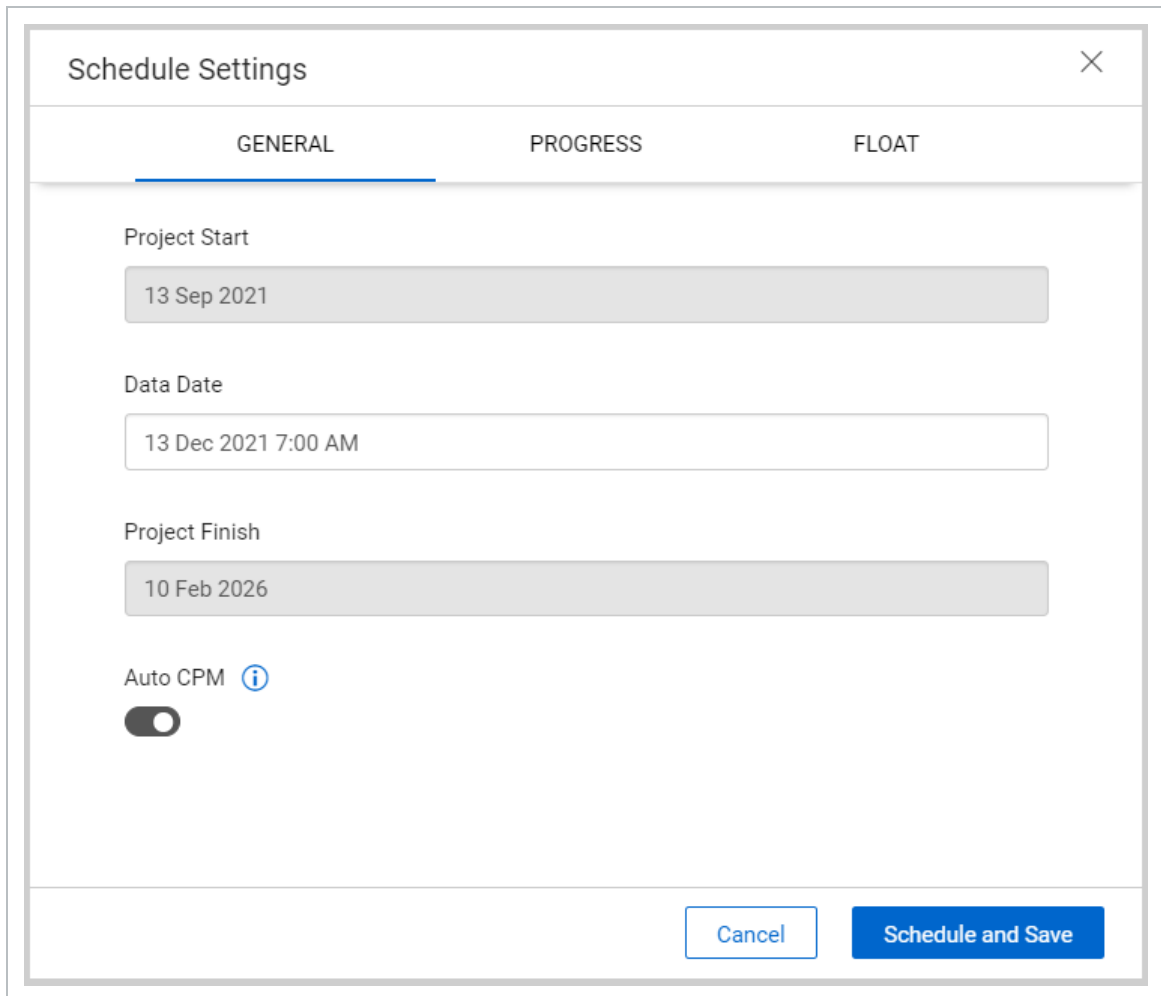

The screenshot shows a 'Schedule Settings' dialog box with three tabs: GENERAL, PROGRESS, and FLOAT. The GENERAL tab is selected. It contains three date pickers: 'Project Start' (13 Sep 2021), 'Data Date' (13 Dec 2021 7:00 AM), and 'Project Finish' (10 Feb 2026). Below these is a toggle for 'Auto CPM' which is currently turned off, accompanied by an information icon. At the bottom right are 'Cancel' and 'Schedule and Save' buttons.

GENERAL	PROGRESS	FLOAT
Project Start 13 Sep 2021		
Data Date 13 Dec 2021 7:00 AM		
Project Finish 10 Feb 2026		
Auto CPM ⓘ <input type="checkbox"/>		
		Cancel Schedule and Save

3. Populate the following information on the Progress tab:

- **Schedule Mode** - The Schedule Mode can either be **Scheduling** or **Planning**. Activities without predecessor logic or constraints will be scheduled against the Data Date.
- **Out of Sequence Progress** - This should remain on retained logic, retains planned dependencies between unworked portions of activities.
- **Auto Progress** - If set to *On*, Schedule assumes that work is proceeding as planned. Activities will be progressed to where they were planned to be on the data date. If set to *Off*, you manually progress activities. This should be done prior to advancing the data date of the project.

- **Recalculate Actual Units When Duration % Complete Changes** - Actual units on assigned resources update per the duration % complete. For example, if a 10-day activity is progressed to 50% duration % complete then a resource assigned to that activity with 100 units planned would update to 50 actual units. Off - Duration % complete and Actual units are unlinked.
- **Relationship Lag Mode** -Dictates which calendar between a predecessor and its successor the lag of a relationship is used when establishing Finish and Start dates in CPM.

The screenshot shows the 'Schedule Settings' dialog box with the 'PROGRESS' tab selected. The dialog has three tabs: 'GENERAL', 'PROGRESS', and 'FLOAT'. The 'PROGRESS' tab contains the following settings:

- Schedule Mode**: A dropdown menu set to 'Scheduling'.
- Out of Sequence Progress**: A dropdown menu set to 'Retained Logic'.
- Auto Progress**: A toggle switch that is currently turned off.
- Recalculate Actual Units When Duration % Complete Changes**: A toggle switch that is currently turned off.
- Relationship Lag Mode**: A dropdown menu set to 'Predecessor'.

At the bottom right of the dialog are two buttons: 'Cancel' and 'Schedule and Save'.

4. Populate the following information on the Float tab:

- **Identify Critical Activities by** - Identify critical activities by either the **Total Float** or the **Longest Path**. If the Total Float value is less than or equal to the defined number of hours (default 0) then it is an indication that an activity is critical. The Longest Path is the path

through a project network from start to finish where the Total Duration is longer than any other path.

- **Total Float** - Set the Total float to less than or equal to **8 hours**. The Total Float represents the amount of time a task can be delayed without affecting the completion date of the project.
- **Manually Configure Settings** - Set the Manually Configure Settings to **On**.
- **Define Critical Activities Using** - You can define critical activities using either **Total Float** or **Free Float**. Free Float represents the amount of time a task can be delayed without affecting the start date of its subsequent tasks.
- **Number of Paths to Calculate** - You can calculate up to 10 sub-critical paths. This helps you to better envision the activities that have a potential of being delayed, which gives you additional time and consideration to push out the schedule. You can choose to execute certain actions such as defining the critical activities by using either free float or total float, select an activity to stop showing multiple float paths, and determine the number of float paths to calculate.

Schedule Settings

GENERAL

PROGRESS

FLOAT

Identity Critical Activities by

Total Float

Total Float

≤ Old

Hours

Float Paths

Manually Configure Settings

On

Define Critical Activities Using

Total Float

Select Activity to Stop Displaying Multiple Float Paths at

Number of Paths to Calculate

9

Cancel

Schedule and Save


To see the float paths in Plan view, you can group by float path in the Group By Builder to see which activities are critical and sub-critical, and the float path where they reside.

ID - Description	Actions	Start	Finish	At Complet...	Total Fl...	Free Float
▼ No Float Path	...	23 May 2014 A	9 May 2017	748		
▼ 9	...	28 Jul 2015 A	20 Apr 2017	402		
▼ 8	...	8 Sep 2014 A	21 Apr 2017	663		
▼ 4	...	6 Jul 2016 A	13 Apr 2017	179		
^ 3	...	22 Sep 2014 A	17 May 2017	619		
Install Civil U/G Aggregates	3 Oct 2016 A	20 Apr 2017	125	124	0
Install Civil U/G Aggregates	3 Nov 2016 A	20 Apr 2017	103	124	0
Install Civil U/G Aggregates	1 Sep 2015 A	20 Apr 2017	378	124	0
Install Civil U/G Load at Sto...	...	3 Mar 2015 A	20 Apr 2017	499	124	0
Paving	...	19 Oct 2016 A	20 Apr 2017	114	124	0
Stockpile / Waste Knockdo...	...	22 Sep 2014 A	20 Apr 2017	601	124	0
Structural Backfill - Water T...	...	16 Apr 2015 A	20 Apr 2017	470	124	0
SUB.Final Site Seeding & La...	...	21 Apr 2017	17 May 2017	18	124	124
^ 2	...	18 Dec 2015 A	19 Jun 2017	348		
Install Misc Metals NE Mezz	18 Dec 2015 A	20 Apr 2017	309	103	0
Install Misc Metals North O...	...	18 Mar 2016 A	13 Apr 2017	252	103	0
Site Finish / Paving	...	3 Oct 2016 A	19 Jun 2017	164	103	0
SUB.Project Painting Plant	28 Sep 2016 A	19 Jun 2017	167	103	103
▼ 10	...	4 Dec 2015 A	14 Apr 2017	313		
▼ 5	...	10 Dec 2015 A	21 Apr 2017	315		
▼ 6	...	27 Mar 2017	1 May 2017	25		
^ 1	...	23 May 2014	27 Nov 2017	885		
Contract Final Acceptance 1...	...		27 Nov 2017*	0		
PP: Contract Administratio...	...	23 May 2014	23 May 2014	0	0	885
PP: Contract Administratio...	...	23 May 2014	23 May 2014	0	0	885
^ 7	...	27 Aug 2015 A	31 Mar 2017	368		
Install Civil U/G Subgrade Fi...	...	27 Aug 2015 A	31 Mar 2017	368	137	13

5. Clicking **Schedule** updates the data date and logic based on the settings selected.

CRITICAL PATH - DRIVING INDICATOR

The driving indicator (steering wheel) appears in the Logic section of the IRIS panel. The driving indicator indicates that a predecessor or successor is on the critical path.

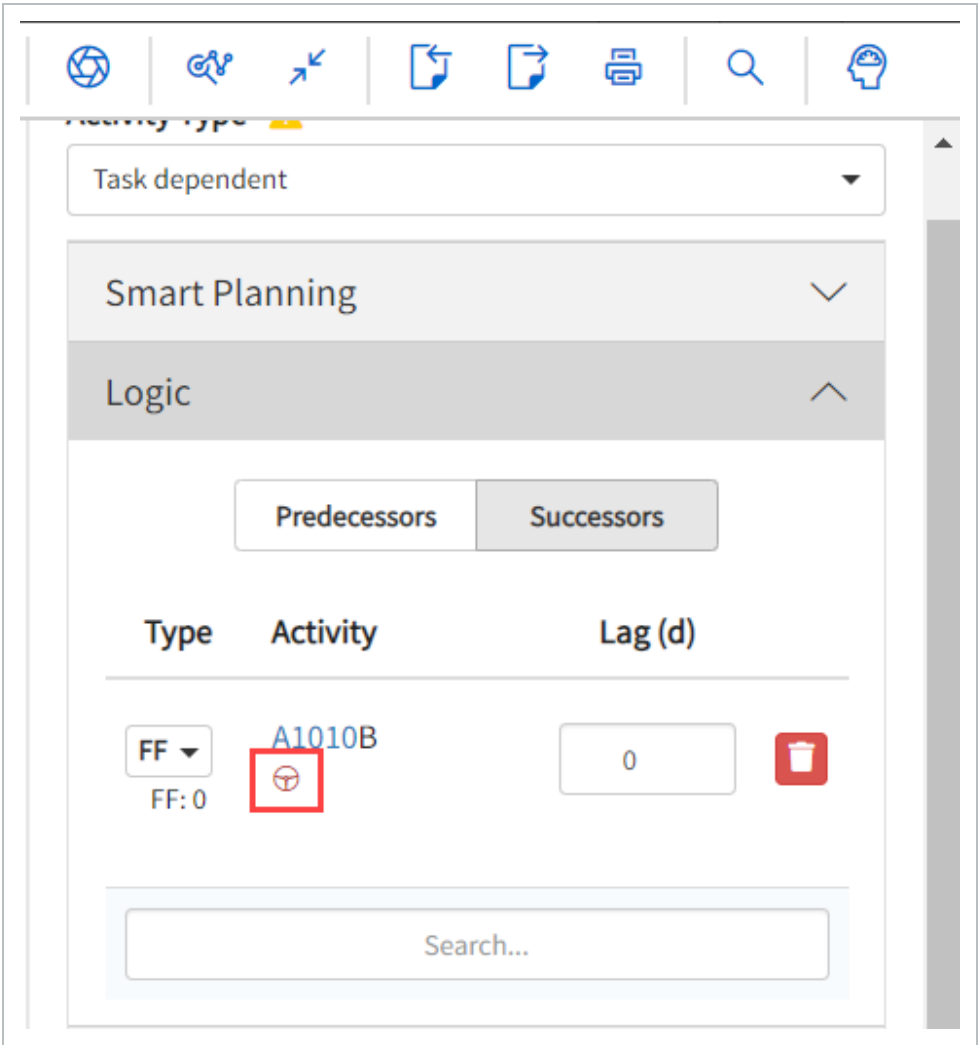

PROGRESSING

To begin Progressing, select the activity that you want to progress, and reference the smart planning panel.

ID

1.1. A3320

Description

Activity A3320

Calendar

test.7 day.1874

Constraint

None

Smart Planning

Planned (d)

120

Cost (\$)

7515000

Remaining (d)

0

R

Start

09 Oct 2017

Actual (d)

167

Finish

24 Mar 2018

At Complete (d)

167

Percent Complete

Phys

100

Early Start

None

Late Start

None

Planned Start

09 Oct 2017

Early Finish

None

Late Finish

None

Planned Finish

05 Feb 2018

Total Float

0

Free Float

.


Logic

Knowledge Tags

Project Register

Delegation

Activities can be marked as started by clicking the **Start** toggle. As activities progress, they can be updated by changing the remaining duration, the finish date, or the Percent Complete fields. When a task is finished, the Finish flag can be switched to *On* to indicate this in the system.

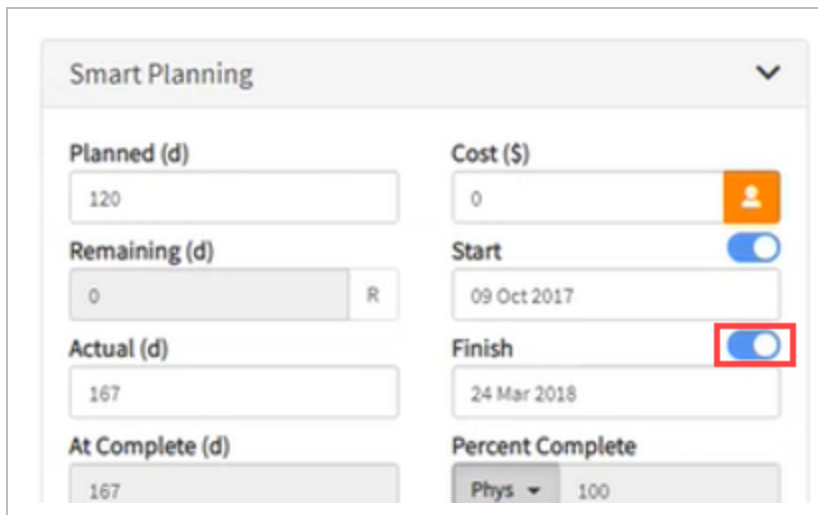


The image shows a 'Smart Planning' form with two columns of input fields. The left column contains duration-related fields: 'Planned (d)' with value 120, 'Remaining (d)' with value 0 and a small 'R' icon, 'Actual (d)' with value 167, and 'At Complete (d)' with value 167. The right column contains cost and date fields: 'Cost (\$)' with value 0 and an orange user icon, 'Start' with value 09 Oct 2017 and a toggle switch, 'Finish' with value 24 Mar 2018 and a toggle switch highlighted by a red box, and 'Percent Complete' with a dropdown menu set to 'Phys' and a value of 100.

Smart Planning	
Planned (d)	Cost (\$)
120	0
Remaining (d)	Start
0 R	09 Oct 2017
Actual (d)	Finish
167	24 Mar 2018
At Complete (d)	Percent Complete
167	Phys 100

PERCENT COMPLETE

Percent complete can be calculated in three different ways:

- Duration
- Units
- Physical

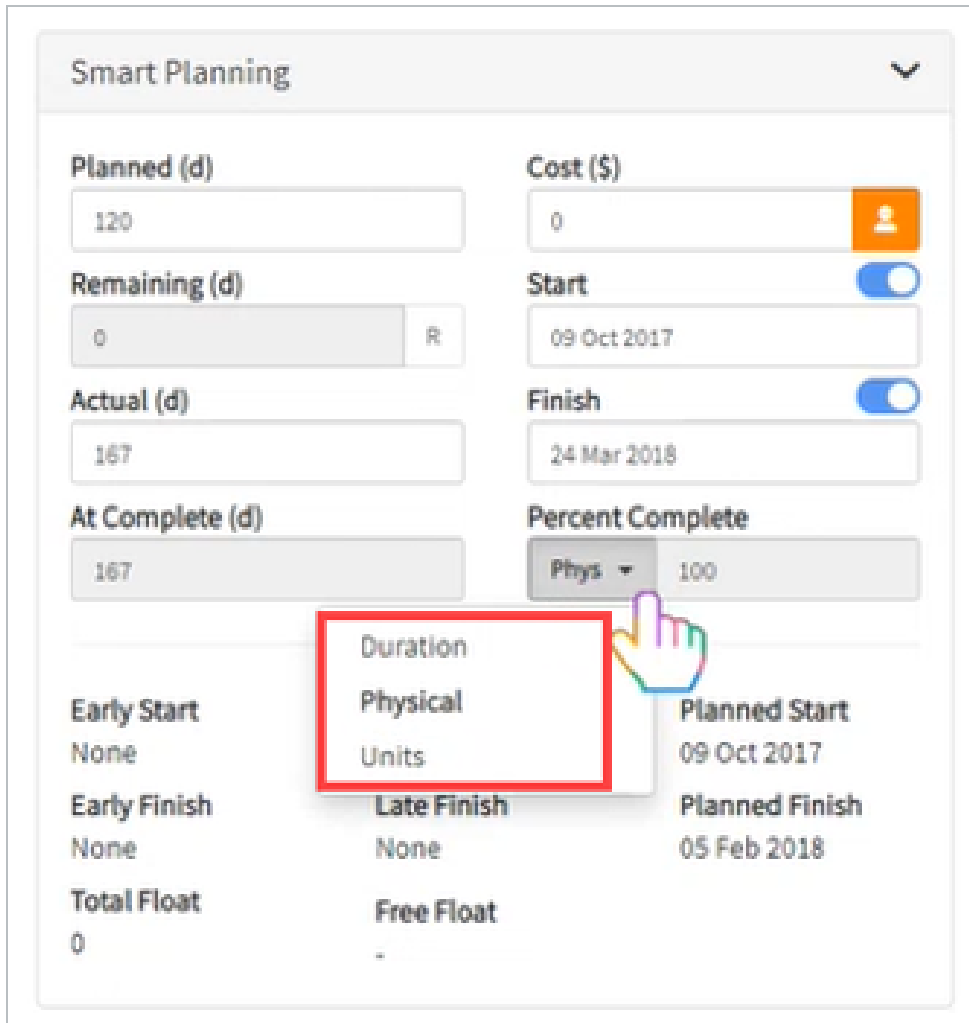

Smart Planning

Planned (d) 120	Cost (\$) 0
Remaining (d) 0 R	Start 09 Oct 2017
Actual (d) 167	Finish 24 Mar 2018
At Complete (d) 167	Percent Complete Phys 100


Duration
 Physical
 Units
 Late Finish
 Free Float

Early Start None	Planned Start 09 Oct 2017
Early Finish None	Planned Finish 05 Feb 2018
Total Float 0	Free Float -

Duration percent complete uses the duration that was originally loaded onto the activity. For example, if the duration was set to ten days for completion and only five days have been completed, the system automatically sets duration to 50 percent complete.

Units percent complete uses the resource budgeted units. Schedule uses any units that have been budgeted to that activity to automatically calculate the percent complete. For example, if there are 100 man hours someone needs to work and they only worked 50 hours, the system would calculate it to 50% complete.

You can also update the Units Percent Complete at the activity level. When the Recalculate Actual Units When Duration % Complete Changes toggle in Schedule Settings is set to Off, you can manually edit the Unit Percent Complete field in Smart Planning.

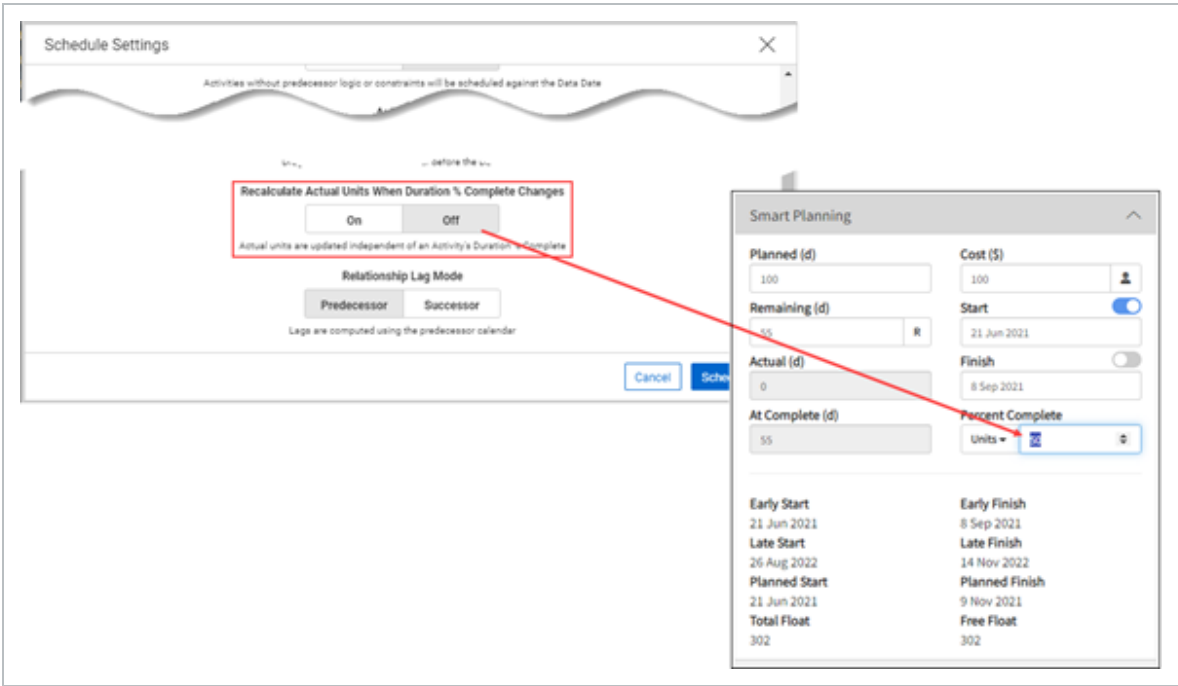

Updating the Units Percent Complete at the activity level in Smart Planning also updates the actual and remaining for the associated resource assignments.

Smart Planning

Planned (d)

100

Cost (\$)

100

Remaining (d)

55

R

Start

21 Jun 2021

Actual (d)

0

Finish

8 Sep 2021

At Complete (d)

55

Percent Complete

Dur

44.88

Resource Assignments

ID	Category	Curve	Plan	Remaining	Actual
	Labor	Linear	40	20	20
	Labor	Linear	40	20	20

Modify

You can modify the resource assignment, which automatically recalculates and updates the Duration Percent Complete in Smart Planning.

Smart Planning

Planned (d)
100

Cost (\$)
100

Remaining (d)
55 R

Start
21 Jun 2021

Actual (d)
0

Finish
8 Sep 2021

At Complete (d)
55

Percent Complete
Units ▾ 37.5

A1000: Activity A1000
(21 Jun 2021 - 8 Sep 2021) - 55.125d

+ Add new resource

Available Resources

- > SCE-CRE
SCE CRE Resources
- Srini
- Chris

FTE/Qty	Plan	Rem	Act	
0.09	40	30	10	⊗
0.09	40	20	20	⊗


Physical percent complete uses the Phys % Complete column as a text field to type in the percent complete. This only applies to an activity that has started and is not completed. Physical percent complete interacts with earned value management. For example, if you have 20% physical complete and 5% duration complete, there are three ways of updating this. You can change the remaining duration, you can change the finish date, or you can change the duration percent complete. The system automatically adjusts the math.

ADDING % COMPLETE COLUMNS TO THE GANTT CHART

1. From the Gantt Chart, select the **Select View Template** icon.



2. In the Available Columns column, scroll to the Duration section. Then select the following columns for percent complete:
 - % Complete
 - % Complete Type
 - Dur % Complete
 - Phys % Complete
 - Unit % Complete
3. Use the arrows to move the columns to the Selected Columns column.

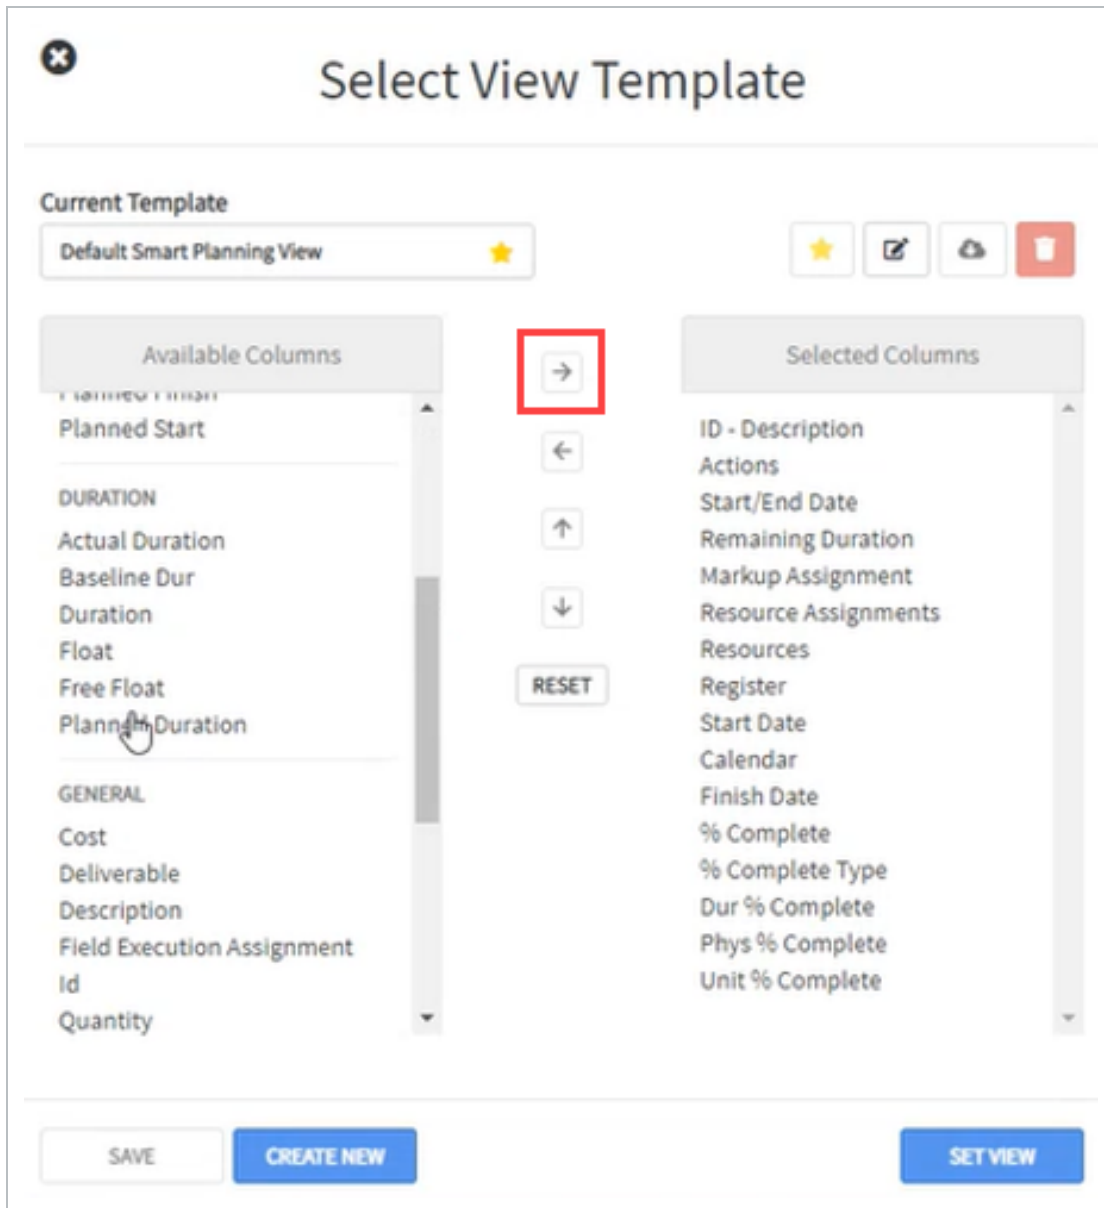

4. Select **Set View** to add the percent complete columns to the Gantt chart.

SNAPSHOT AND SCHEDULE SETTINGS

SET SNAPSHOT

Setting the snapshot lets you compare any future changes that we make to the plan to our current plan.

It is important to set the snapshot before applying any progress to the schedule. This lets you compare the current progress against the snapshot plan.


NOTE

Before setting the snapshot, the SN1 Start and SN1 End dates columns show no values.

ID - Description	Rem Dur	Progress	Start Date	Finish Date	Baseline Start	Baseline End	New
North Tower Commercial Building			01 Aug 19	31 Mar 22			
Multi-level			01 Aug 19	31 Mar 22			
Preconstruction			01 Aug 19	07 May 20			
Design			01 Aug 19	31 Dec 19			
Proposal Submissions	9	0%	01 Aug 19	13 Aug 19			
Proposal Reviews & Approvals from Bo	23	0%	14 Aug 19	13 Sep 19			
Establish Permitting Documents	32	0%	16 Sep 19	29 Oct 19			
Create Early Stage Construction Docs	45	0%	30 Oct 19	31 Dec 19			
Permitting			30 Oct 19	07 May 20			
Fire Permit	25	0%	30 Oct 19	03 Dec 19			
Sitework Permit	17	0%	01 Jan 20	23 Jan 20			
Building Permit	41	0%	24 Jan 20	20 Mar 20			
Foundation Permit	21	0%	23 Mar 20	20 Apr 20			

SET THE SNAPSHOT

1. Click **Snapshot icon > Set Snapshot..**



- After the snapshot is set, you can view the SN1 Start and SN1 End dates shown in the column. The snapshot dates are now populated in Schedule.

ID - Description	Rem Dur	Progress	Start Date	Finish Date	Baseline Start	Baseline End	New
North Tower Commercial Building			01 Aug 19	31 Mar 22			— — ◆
Multi-level			01 Aug 19	31 Mar 22			— — ◆
Preconstruction			01 Aug 19	07 May 20			— — ◆
Design			01 Aug 19	31 Dec 19			— — ◆
Proposal Submissions	9	0%	01 Aug 19	13 Aug 19	01 Aug 19	14 Aug 19	
Proposal Reviews & Approvals from Bo	23	0%	14 Aug 19	13 Sep 19	14 Aug 19	14 Sep 19	
Establish Permitting Documents	32	0%	16 Sep 19	29 Oct 19	16 Sep 19	30 Oct 19	
Create Early Stage Construction Docs	45	0%	30 Oct 19	31 Dec 19	30 Oct 19	01 Jan 20	
Permitting			30 Oct 19	07 May 20			— — ◆
Fire Permit	25	0%	30 Oct 19	03 Dec 19	30 Oct 19	04 Dec 19	
Sitework Permit	17	0%	01 Jan 20	23 Jan 20	01 Jan 20	24 Jan 20	
Building Permit	41	0%	24 Jan 20	20 Mar 20	24 Jan 20	21 Mar 20	
Foundation Permit	21	0%	23 Mar 20	20 Apr 20	23 Mar 20	21 Apr 20	
Water Permit	13	0%	21 Apr 20	07 May 20	21 Apr 20	08 May 20	
Permit Completion Milestone			08 May 20	07 May 20	08 May 20	08 May 20	

NOTE

If the snapshot has not been set when a Markup Cycle is started, Schedule requests confirmation to establish the snapshot so any markups or changes to the schedule can be compared before and after review.

NOTE

Gantt bars of up to 2 snapshots can be visualized against the current schedule Gantt bars for comparison. Gantt grid columns show variances between the current schedule and the snapshot columns.

SCHEDULING

Schedule uses CPM for scheduling a set of activities. This method calculates the activity dates based on the durations and logic.

To schedule the project or review schedule options, click **Schedule**.

Select an Annotation ▼

ID - Description	Actions	Register	
^ Commercial Construction	...		
^ General Conditions	...		
Receive notice to proceed and sign c...	...		

Schedule Settings

Project Start

26 Apr 2021

Data Date

26 Apr 2021 12:00 AM

Project Finish

21 Sep 2022

Schedule Mode

Planning

Scheduling

Activities without predecessor logic or constraints will be scheduled against the Data Date

Auto CPM

On

Off

Automatically perform CPM on any changes to the schedule

Critical Activities Contain Total Float Less Than or Equal To...

0

hours

Out of Sequence Progress

Retained Logic

Progress Override

Actual Dates

Relationships are maintained between the predecessor and successor for unworked portions of activities and continued after the predecessor has finished (recommended)

Auto Progress

On

Off

Drag activities forward that occur before the Data Date

Recalculate Actual Units When Duration % Complete Changes

On

Off

Actual units are updated independent of an Activity's Duration % Complete

Relationship Lag Mode

Predecessor

Successor

Lags are computed using the predecessor calendar

Cancel


Schedule

DATA DATE

Data Date


20 Nov 2020

Set the Data Date to the day and hour you want to update the schedule to. The Data Date is used as the starting point to calculate the dates of all remaining activities. The Data Date is represented by the blue vertical line on the Gantt chart

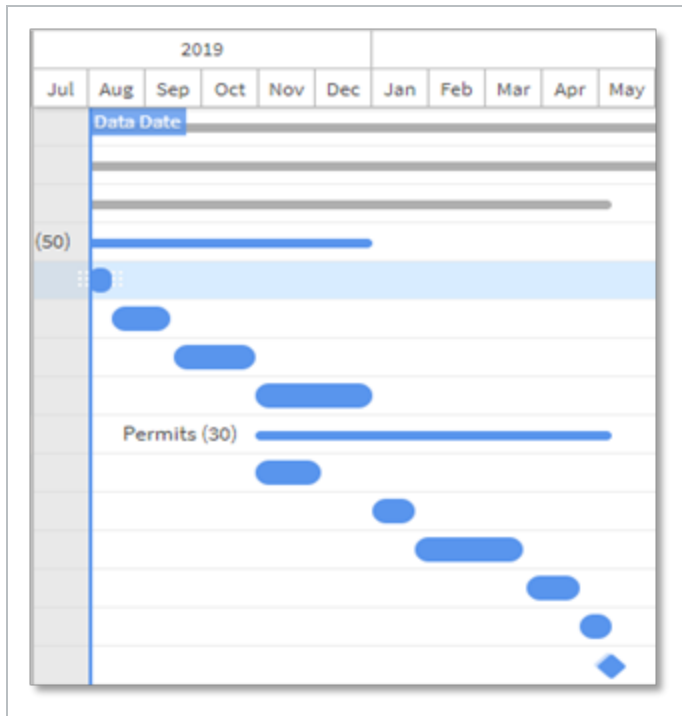

SCHEDULE MODE (PLANNING VS. SCHEDULING MODE)


The Schedule Mode determines how activities without predecessor logic or constraints will respond to the updates being made to the schedule.




- In **Planning Mode**: Activities without predecessor logic or constraints do not snap back to the Data Date. This allows activities without predecessors to be scheduled throughout the project's timeline.
- In **Scheduling Mode**: Activities without predecessor logic or constraints are scheduled against the Data Date.

AUTO CPM

Selecting the Auto CPM option *On* updates activity duration and sequence as actual progress is entered into Schedule. Switching this to *Off* prevents the schedule from automatically adjusting when activity is updated, and it must be adjusted manually. This is particularly useful if schedulers plan to update multiple activities in bulk, and then determine the CPM.



Out of Sequence Progress



- **Retained Logic:** Relationships are maintained between the predecessor and successor for unworked portions of activities and continued after the predecessor has finished.
- **Progress Override:** Relationships between the predecessor and successor are disregarded, and unworked portions of activities continue before the predecessor has finished.
- **Actual Dates:** When actual dates in the future occur, the remaining duration of in-progress activities are calculated after the conclusion of the future activity.

AUTO PROGRESS

Auto Progress determines if activities automatically start and progress when the Data Date has passed.

- If Auto Progress is *On*, activities that occur before the Data Date will automatically start progressing.
- If Auto Progress is *Off*, activities that occur before the Data Date will be pushed forward to the current Data Date without having started.

BASELINE/SNAPSHOT

Snapshots take all information from your current project file and saves it to the Snapshot Management menu. After a snapshot is saved, you can set another snapshot, overwrite a snapshot, delete a

snapshot, save as a new schedule, or promote to a schedule.

NOTE

There are only two snapshot slots available per project. The information on the snapshot cannot be edited after it has been created. Only the name of the snapshot can be changed.

The active baseline and any available snapshots are in a grid format, in addition to a color-coded metric table. This lets you see a comparison between the current schedule, active baseline, and available snapshots.

1 active user

Baseline/Snapshot Management

Active Baseline

Baseline based on Copy 1221 Gemini Solar - Co... Gopala Penmesta - 2 Feb 2023

[Assign schedule](#)

Snapshot 1

Snapshot - 18 Apr 2023: Paul - 18 Apr 2023

[Overwrite snapshot](#) [Promote to project list](#)

Snapshot 2

Snapshot - 18 Apr 2023 (1): Paul - 18 Apr 2023


[Overwrite snapshot](#) [Promote to project list](#)

Set or overwrite snapshot above, or [Create copy of current schedule](#)


Snapshot 3 has been saved to your schedule list [View in schedule list](#)

	Current Schedule	Active Baseline	Snapshot 1	Snapshot 2
Data Date	30 Jun 2022	20 May 2022	30 Jun 2022	30 Jun 2022
Number of Activities	9	9	9	9
Start Date	30 Jun 2022	20 May 2022	30 Jun 2022	30 Jun 2022
Finish Date	13 Dec 2022	2 Nov 2022	13 Dec 2022	13 Dec 2022
Remaining Duration	167 days	167 days	167 days	167 days
Average Float	35 days	10 days	35 days	35 days
Labor Resource Units	0	0	0	0
Total Cost	\$0	\$0	\$0	\$0
Critical Activities	4	4	4	4
Activities Completed	1	0	1	1
Activities in progress	1	0	1	1
Activities not started	7	9	7	7
Constraints	3	3	3	3

You can also assign other schedules that are part of the same project workspace as the current schedule to your active baseline and snapshots using the assign schedule function.

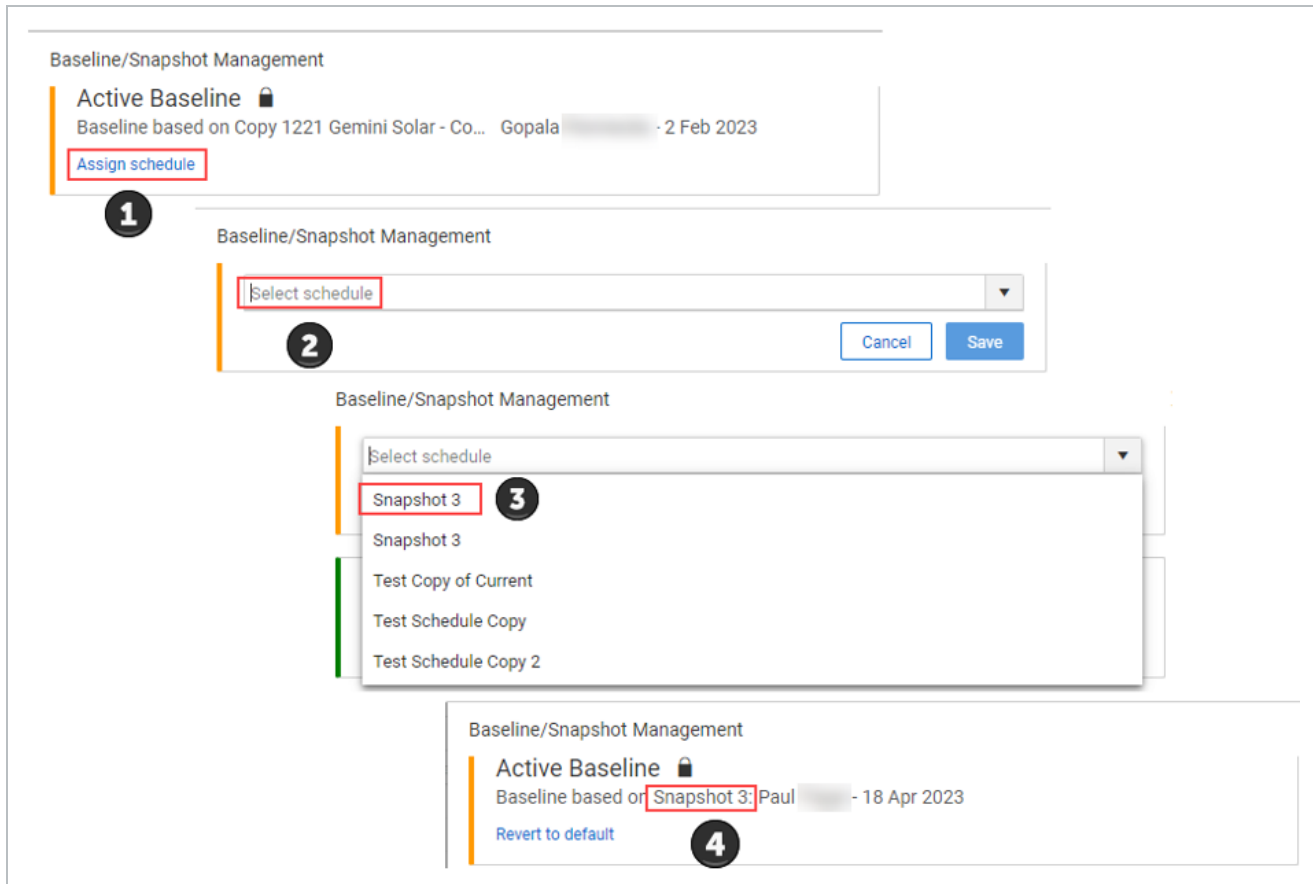


Select *Revert to default* to return to the previously assigned defaulted schedule.

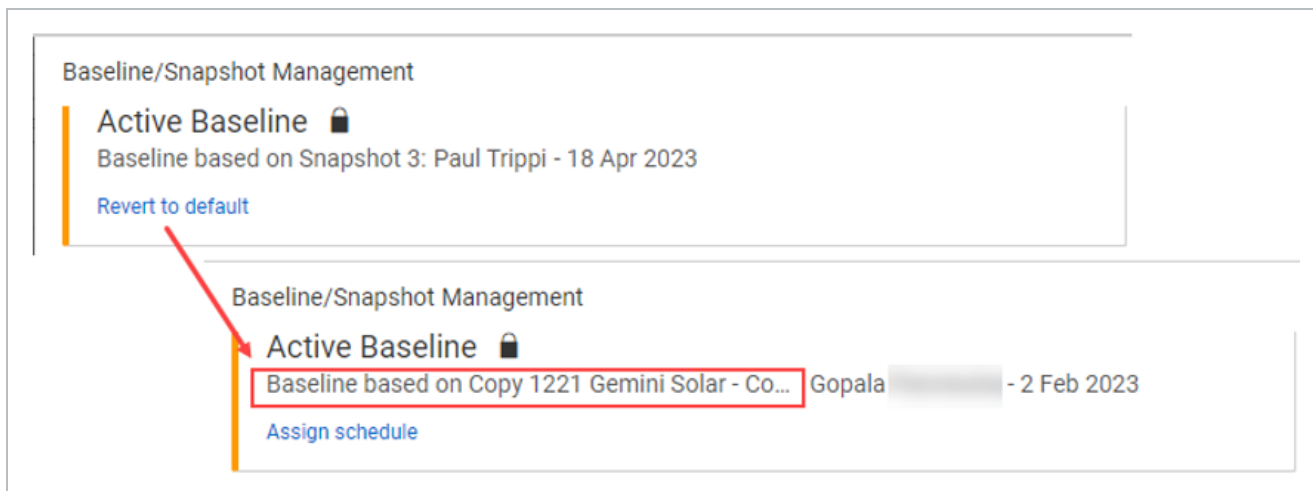

ACTIVE BASELINE

The images below show what the Gantt chart illustrates when the active baseline is turned off and then on.

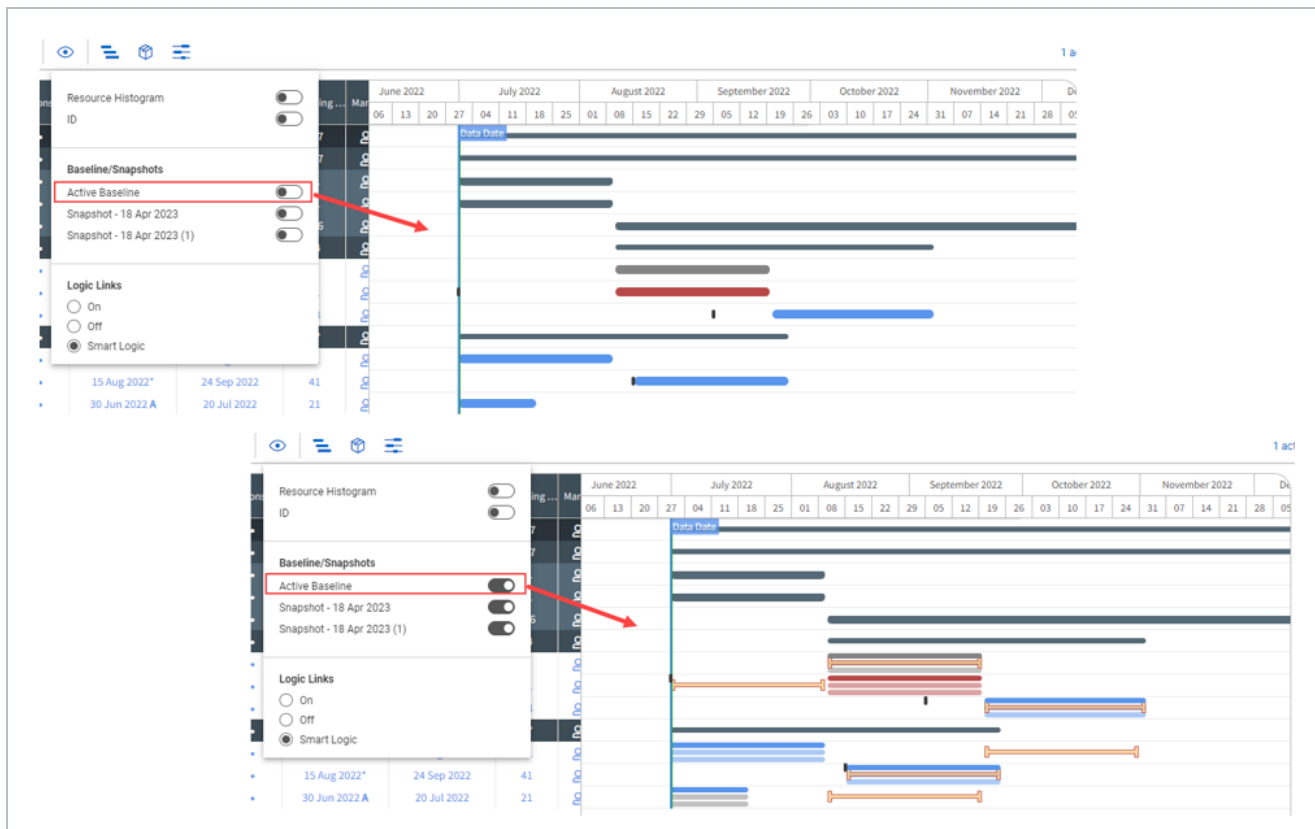


CREATE A SNAPSHOT

The following step-by-step walks you through how to create a snapshot.


NOTE You can only create snapshots from the Plan view.

CREATE A SNAPSHOT

1. From the Plan view, select the **Snapshot** button in the toolbar. The Snapshot Management menu opens.

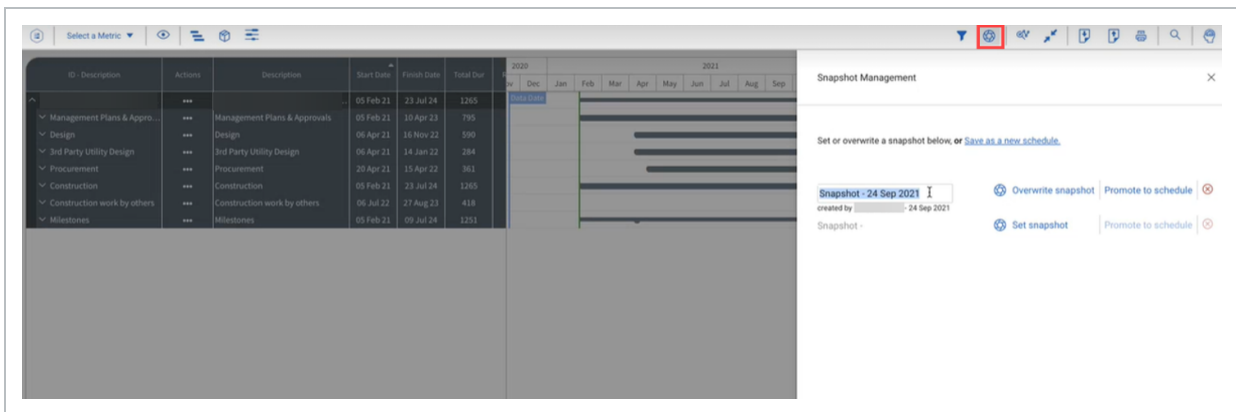

2. In the Snapshot Management menu, select **Set snapshot**. The snapshot automatically saves as Snapshot – [date].
3. Click the **Edit** icon next to the snapshot name to change the dialog box into an editable text box. You can now rename the snapshot to a name of your preference.



OVERWRITE A SNAPSHOT


You can overwrite a previous snapshot if the information saved in the first snapshot does not have the most up-to-date information.

NOTE If another user saved the snapshot you want to overwrite, confirm with that user that the information in the snapshot to be overwritten is no longer needed.

The following step-by-step walks you through how to overwrite an existing snapshot.

OVERWRITE A SNAPSHOT

1. From the snapshot Management menu, find the snapshot you want to overwrite.
2. Select **Overwrite snapshot**.

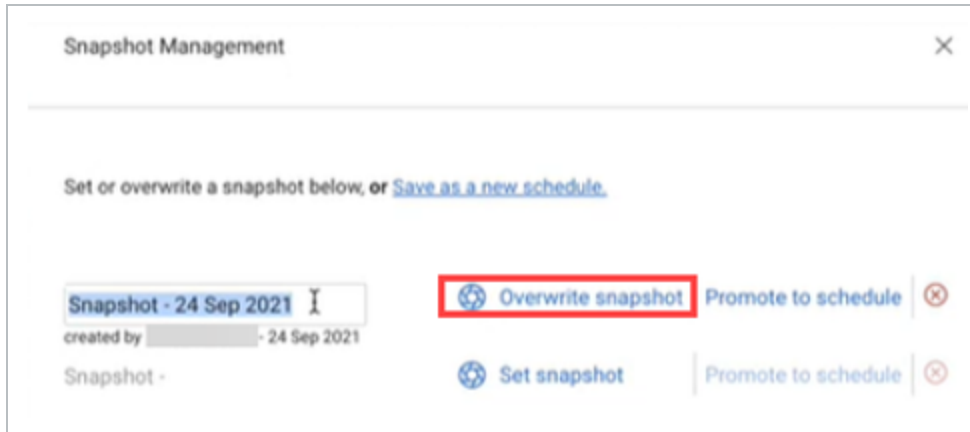

The old snapshot is overwritten and a new snapshot is saved in that snapshot slot.


ANALYSIS VIEW TEMPLATE

The Analysis View template works alongside the snapshots. This view lets you bring in new columns from SN1 Actual Finish to the additional variance columns. These columns are used in snapshots to compare information between snapshots and the current project. This template includes anything with a snapshot or a variance.


The following step-by-step walks you through how to select the Analysis View template.

ANALYSIS VIEW TEMPLATE

1. In the toolbar, select the **Select View Template** icon.




2. In the Current Template field, select the blue icon on the right. A drop-down menu opens.

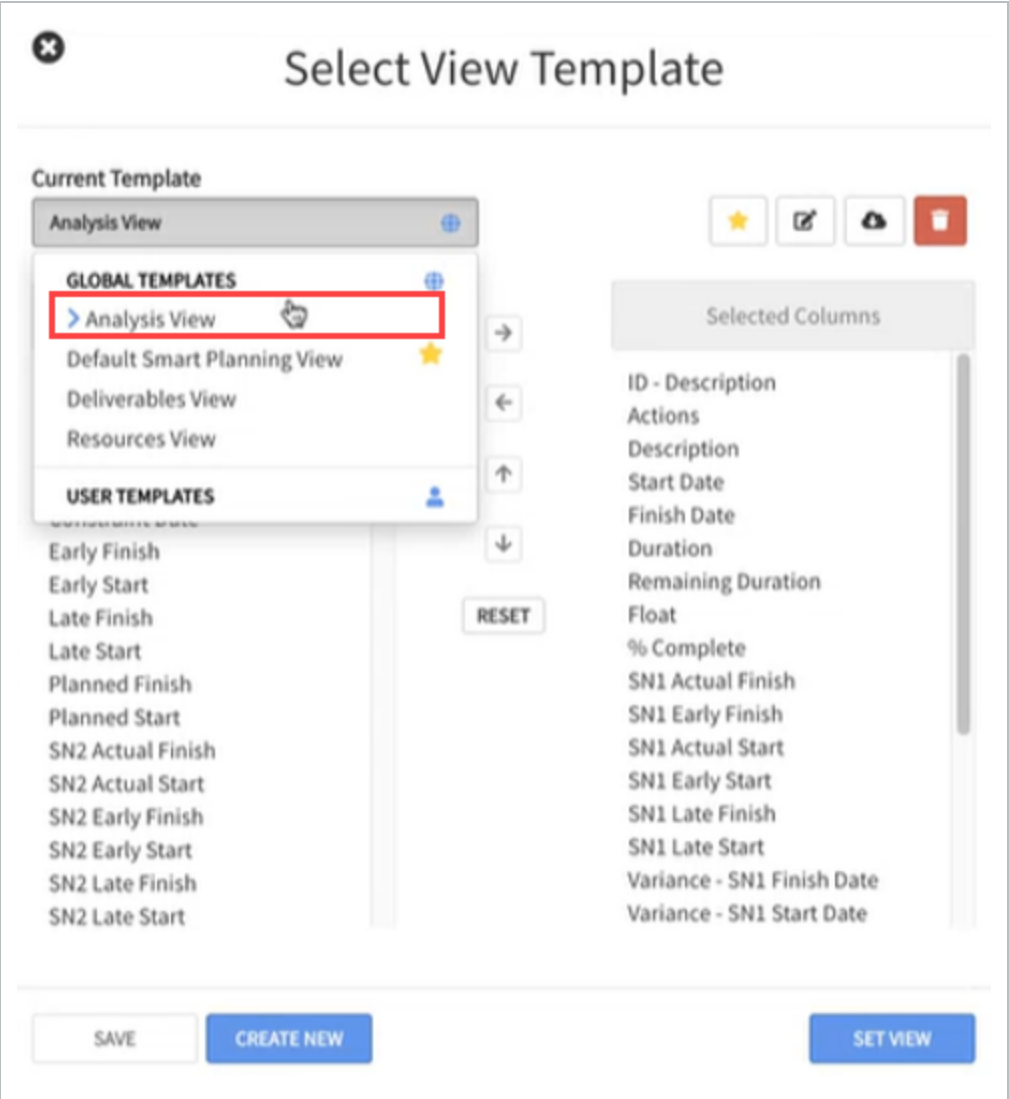

3. Under Global Templates, select **Analysis View**.

Columns that are available for viewing snapshot changes are available in this template. You can also add any available columns to the template as needed.

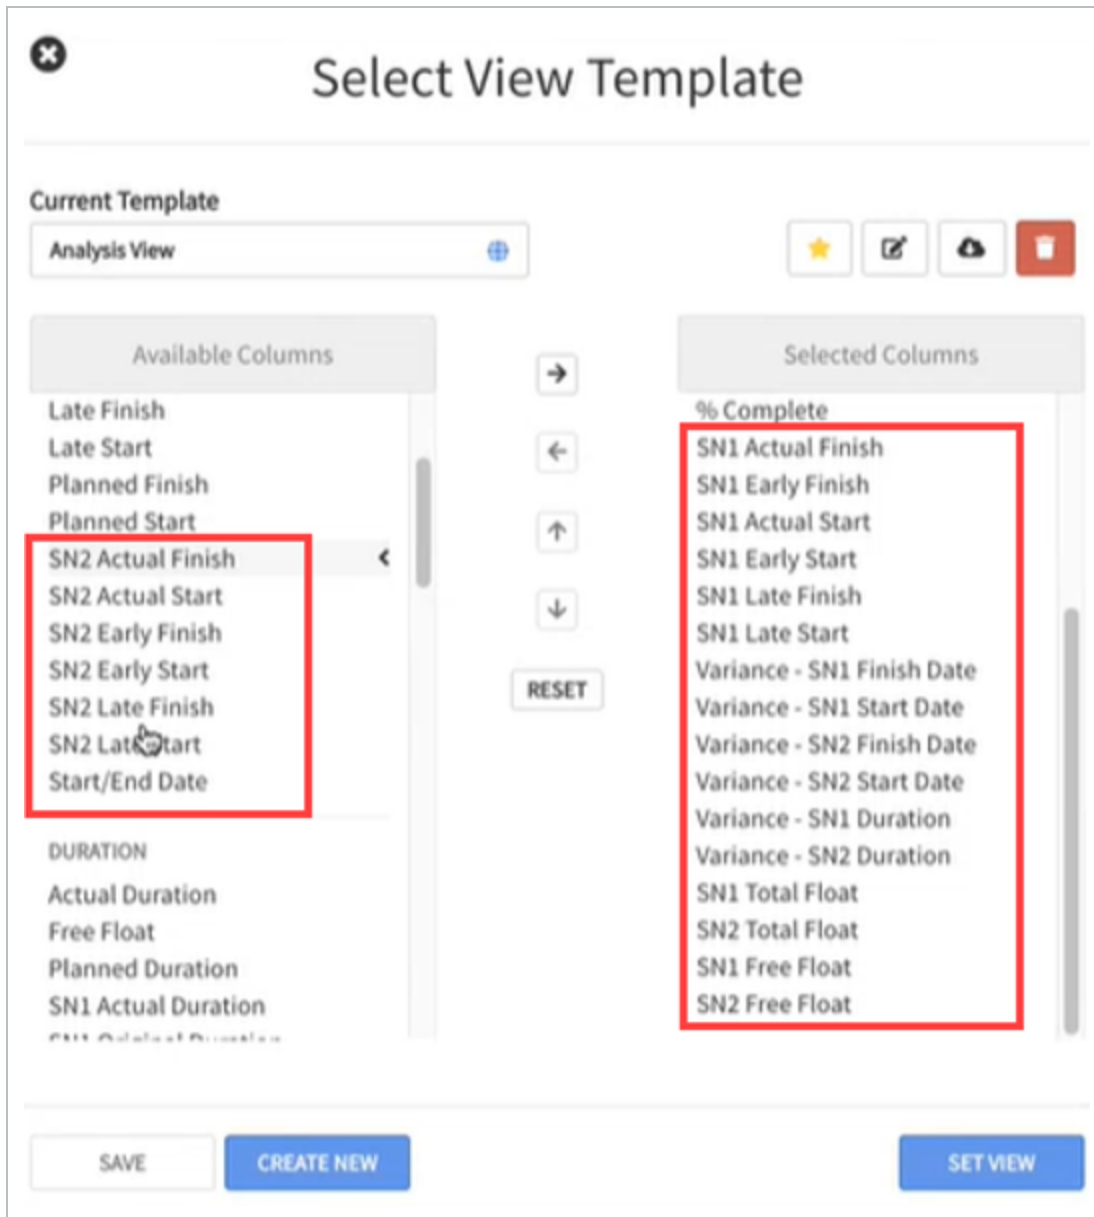


4. Use the arrows to move the columns over to the Selected Columns column as needed.
5. After the Analysis View template has been edited, select **Set View** to add the columns to the Gantt chart.

VIEW SNAPSHOTS IN THE GANTT CHART

After the snapshot has been created, your Gantt chart is updated with bars for the information that relates to the current schedule status and the snapshot status. The darker bars can be moved to


change the schedule on the Gantt Chart. The lighter bars represent the snapshot. The bars are blue when the schedule is not critical and red if they are critical.

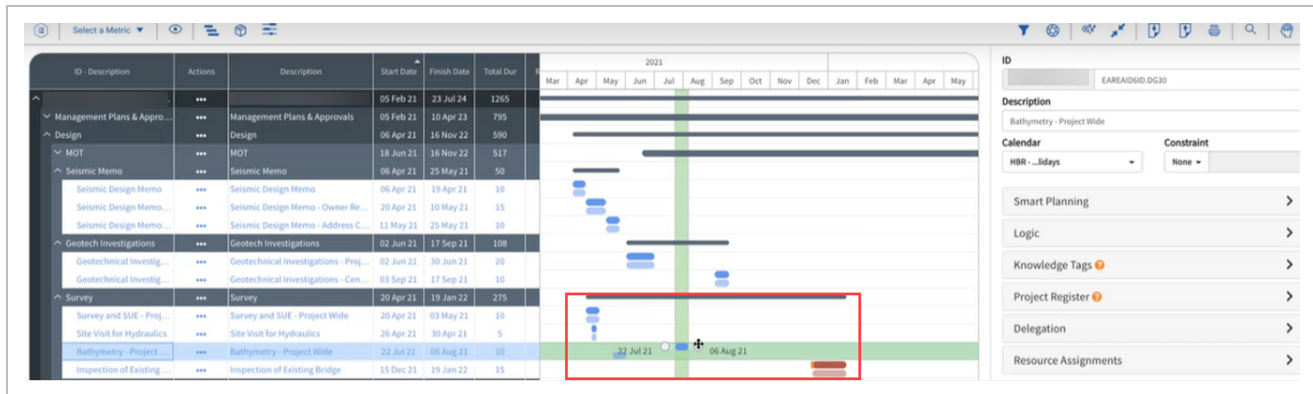

The following step-by-step walks you through how to view existing snapshots on the Gantt Chart.

VIEW SNAPSHOTS

1. In the toolbar, select the **View options** icon.
2. Under the Snapshots section, select the slider for the snapshot you prefer to see in the Gantt chart. A drop-down menu opens.

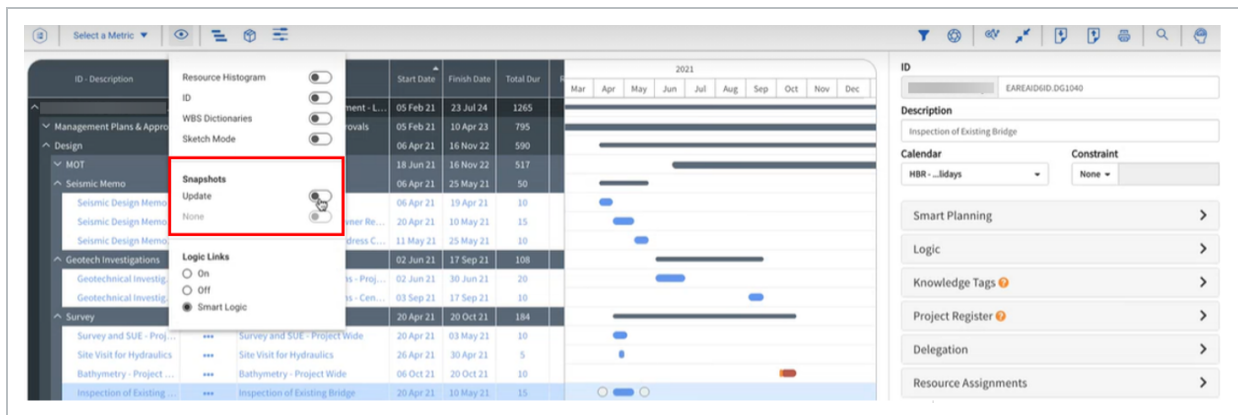


Two bars now show for items in the Gantt chart. You can move around the darker blue or darker red bars. The lighter bars represent the information saved in the snapshot and cannot be moved.

VARIANCE COLUMNS

Each variance column compares the snapshot to the current project.

The columns show a badge depending on how the information changed. If there is a net zero change, then no badge appears. For example, the variance columns might show a green badge number if there is a decrease in duration between the snapshot and the current project. The badge numbers could also show in red if the duration increased between the snapshot and the current project. If there is no change between the snapshot and project, the number shows as 0.

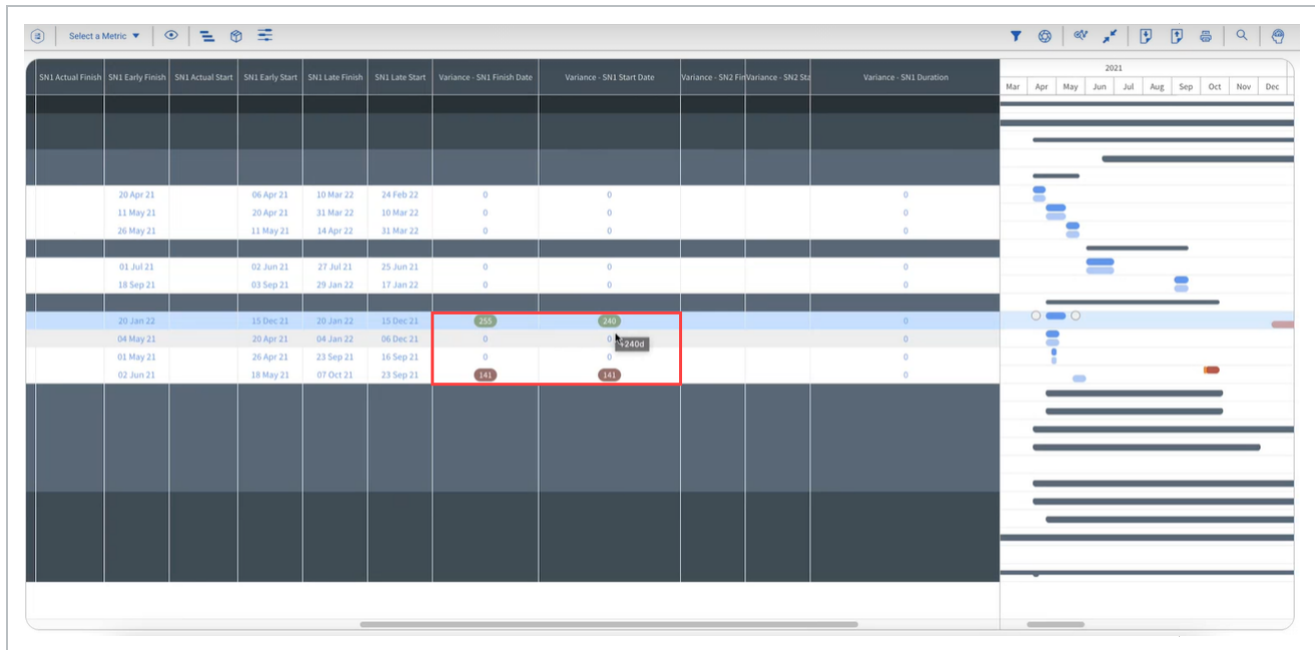

PROMOTE TO SCHEDULE


When you choose to promote a snapshot to schedule or to save a snapshot as a new schedule, the snapshot selected is then saved to the project list.

Promote to Schedule saves a snapshot to the project list. If you select **Save as a new schedule**, this option saves the current project as a copy onto the project list view as a new schedule.


The following step-by-step walks you through how to save a snapshot to the project list.

PROMOTE TO SCHEDULE

1. In the Snapshot Management menu, click the **Promote to Schedule** button.

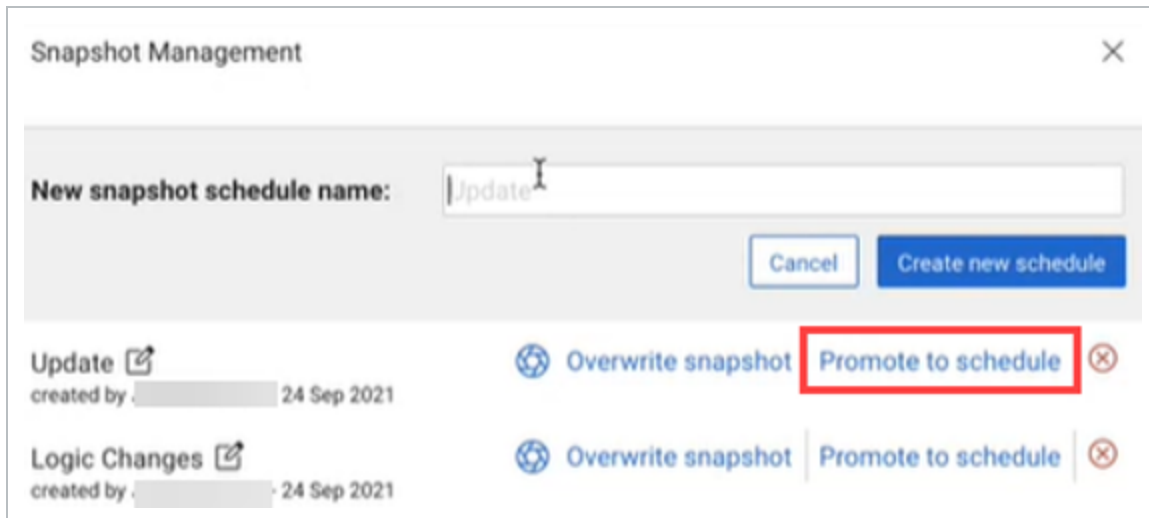

2. If preferred, enter a new name for the snapshot in the New snapshot schedule name field.
3. Click **Create new schedule**. The new schedule has been saved to the project list.
4. Click **View in Project List** to view the new schedule.




PROJECT LIST VIEW

You can organize your schedules in project folders. Project folders can be created in the project list to better organize schedules into a project hierarchy. You can list as many schedules as needed under

each project workspace.


The projects can be organized alphabetically using the column header sort function. Use the options from the Action menu on folders to perform the following:

- Edit Project Workspace Name
- Move schedules
- Delete

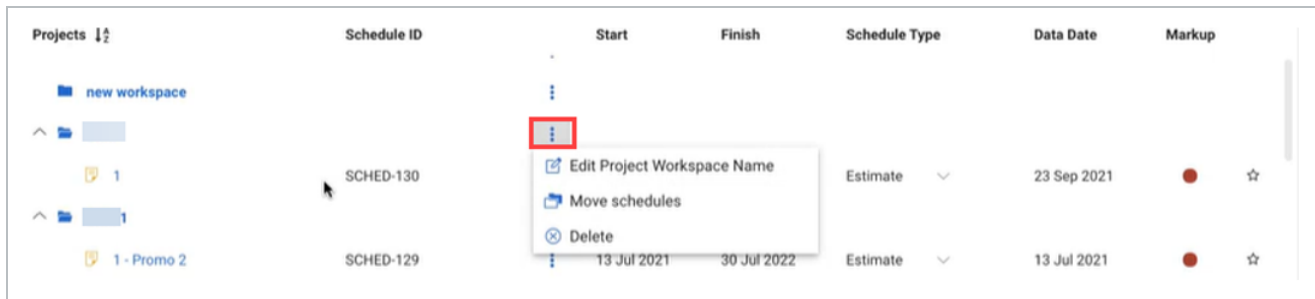

Use the options from the Action menu on individual schedules to perform the following:

- Edit Schedule Name
- Edit Schedule ID
- Move schedule
- Copy
- Delete

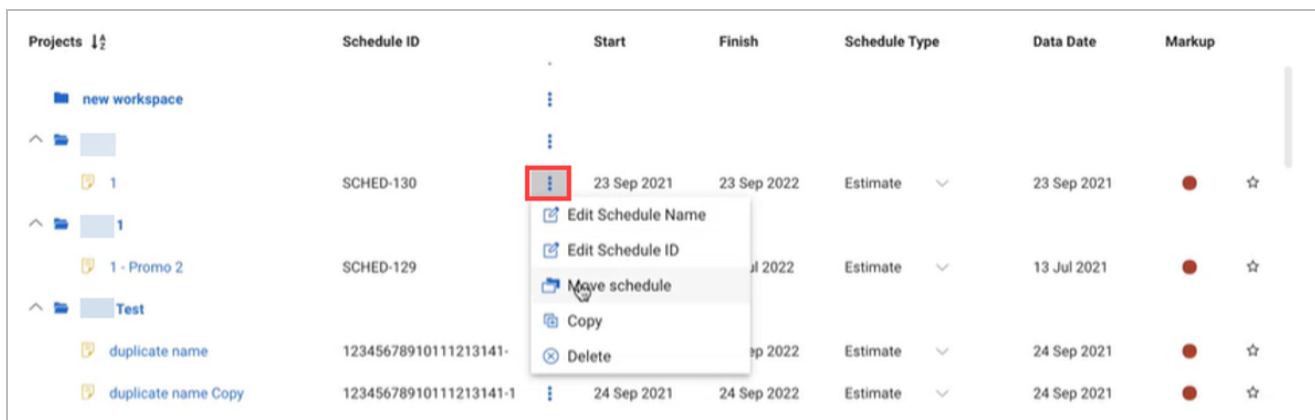

You can also edit the Schedule Type for each schedule. By default, the Schedule Type field is set to **Estimate**.


NOTE

If you do not organize your schedules into specific project folders, then the schedule is placed under the None folder by default.

If you import a project file into Schedule, you must include the Schedule ID, Schedule Name, and a Project Workspace.

INTEGRATIONS

The Integrations and Update buttons show in the Plan view toolbar. Click **Integrations** to see the InEight products currently integrated with Schedule, which currently only includes InEight Estimate. The green circle icon on the button indicates there is an active integration in Schedule. The Update button is used to pull the data changes made to the InEight product (Estimate) in to Schedule.

**NOTE**

After you click **Update**, changes cannot be made to the schedule until the update is completed.


To integrate Estimate job data with Schedule workspaces, see Integrated Solutions [InEight Integration Estimate-Schedule](#) for more information.

LESSON 8 – SCHEDULE MARKUP PROCESS

MARKUP PROCESS OVERVIEW

ASSIGNING MARKUP


Markup is assigned in the plan project view from the first level drop-down menu in a project. Select a project WBS summary level, then expand the delegation panel and click the **Modify Assignments** icon, where users can be assigned at various levels within the schedule to provide markup.

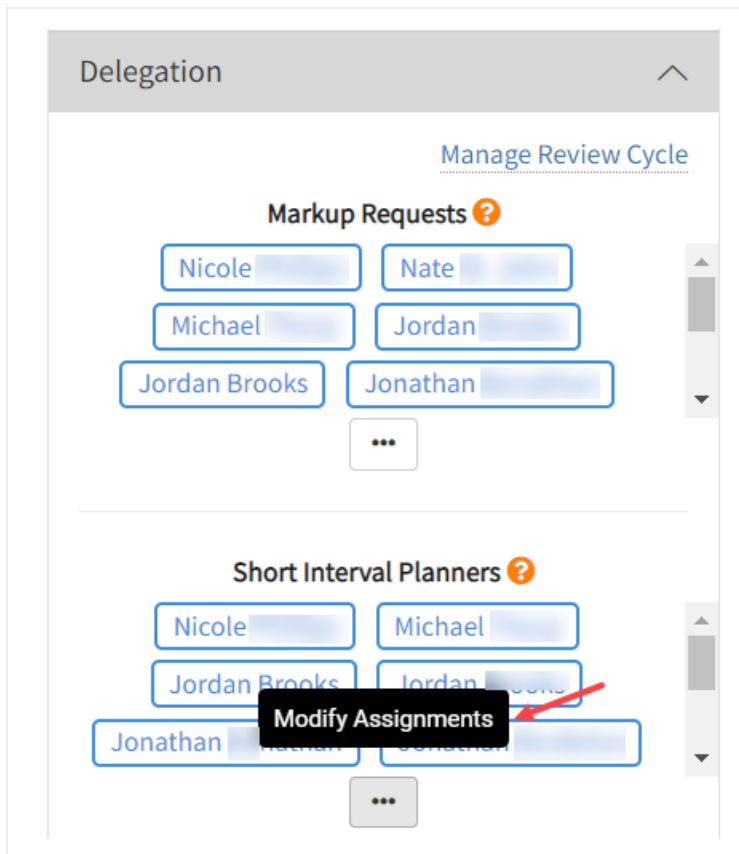

Click the **blue ellipse** icon and select users to assign to WBS elements.

INITIATING THE REVIEW CYCLE

Once contributors are assigned, the review cycle can be initiated by clicking on the Manage Review Cycle link in the top right of the delegation panel or go to the project settings view from the 1st level drop-down menu within a project and select Manage Review Cycle.

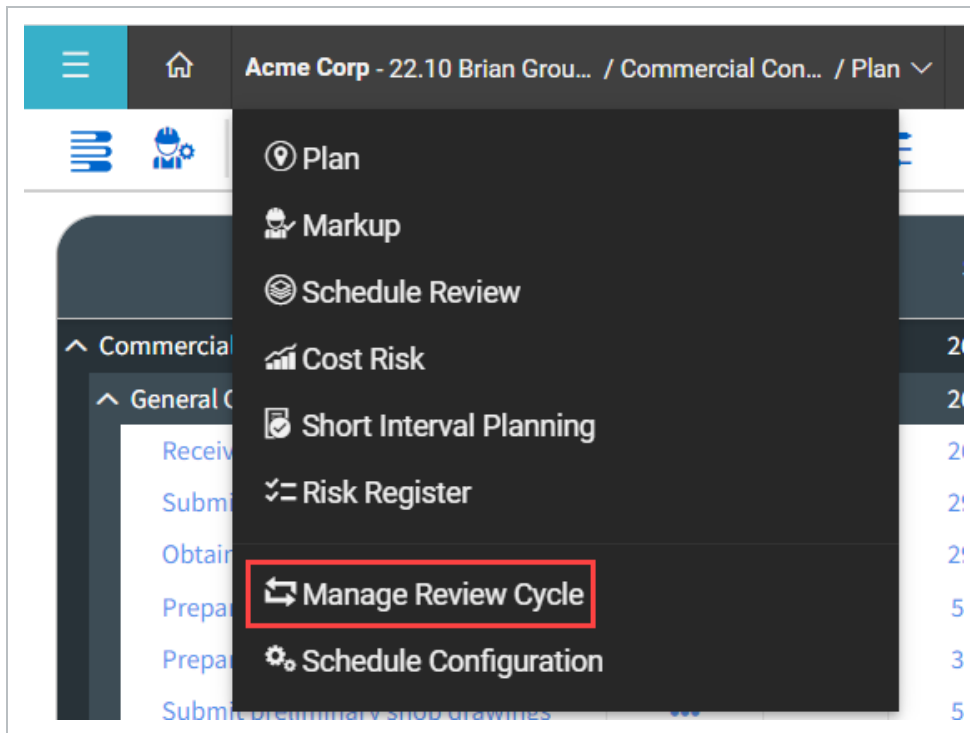

Assigned contributors and a review message can be validated here. After the Start Review Cycle button is clicked, an invitation email is sent to contributors.

Start Review Cycle

Start Review Cycle to solicit expert feedback from project team members

START REVIEW CYCLE

Message

Explain to your team members the purpose of the review cycle as well as what to focus on. This message will appear in popup at the start of Markup

Please review before end of week

Register Threshold

Difference in BASIS Duration and Team Member Markup that requires a Register entry

+/- 50%

Team Member Markup

Assignee	Team Contribution	Last Accessed	Ready For Review?	Show Whole Project	Show Cost	Clear Markup
Ben Heights	<div><div>38% (3)</div><div>50% (4)</div><div>13%</div></div>	4 months ago	<div></div>	<div></div>	<div></div>	<div></div>
Allen Paddock	<div><div>38% (3)</div><div>13%</div><div>50% (4)</div></div>	1 week ago	<div></div>	<div></div>	<div></div>	<div></div>
Paul Self	<div><div>13%</div><div>50% (4)</div><div>38% (3)</div></div>	4 months ago	<div></div>	<div></div>	<div></div>	<div></div>
Christy Tuppence	<div><div>100% (8)</div></div>	4 months ago	<div></div>	<div></div>	<div></div>	<div></div>
Overall	<div><div>22% (7)</div><div>53% (17)</div><div>25% (8)</div></div>					<div>REMOVE ALL</div>

EXPORT USER MARKUP


Uncertainty

Export project uncertainty ranges generated from team member markup to a risk analysis tools - Oracle PRA (Pertmaster) or Deltek Acumen Risk

EXPORT FORMAT

MARKING UP THE SCHEDULE

After the review cycle is in process, assigned contributors should log into the project, confirm they are in the Markup project view from the first level drop-down menu in a project, and provide feedback to sections of the schedule assigned to them.



REVIEWING MARKUP

After Markup is complete, group consensus and individual responses can be assessed from the Review project view from the first level drop-down menu in a project. Consensus is indicated by the signal bars in the tabular WBS view, and individual responses can be viewed by selecting a WBS element and looking in the Duration Uncertainty slide-out panel to the left.


After a review is complete, the cycle can be ended by returning to the Manage Review Cycle page, and clicking **End Review Cycle**.

INITIATING THE REVIEW CYCLE

Now that users have been assigned to various sections of the schedule, you can initiate a review cycle. This will send a notice (email) to contributors assigned to provide markup, notifying them that they may start their review.

OPENING THE VIEW CYCLE

1. To access the Review Cycle settings, open the **Delegation** tab from Iris and select **Manage Review Cycle**.

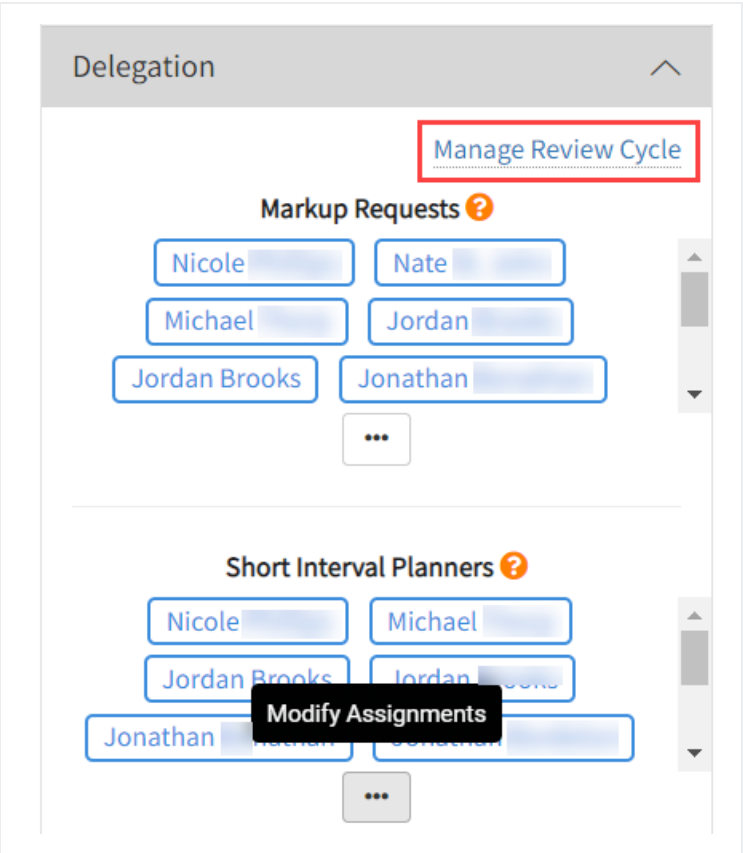

TIP

In the Manage Review Cycle screen, settings can be adjusted prior to initiating the cycle.

The Manage Review Cycle window opens.

Start Review Cycle
 Start Review Cycle to solicit expert feedback from project team members

START REVIEW CYCLE

Message
 Explain to your team members the purpose of the review cycle as well as what to focus on. This message will appear in popup at the start of Markup

22.10 Markup Group Testing! Let's Markup!

Register Threshold
 Difference in Schedule Duration and Team Member Markup that requires a Register entry

None ▾

Team Member Markup

Assignee	Team Contribution	Last Accessed	Ready For Rev...	Show Whole P...	Show Cost	Clear Markup
Brian Mikinski	66% (85) 17% (22) 12%	9/30/22		<input type="checkbox"/>	<input type="checkbox"/>	
Nicole Phillips	51% (66) 16% (21) 27% (35)	10/12/22		<input type="checkbox"/>	<input type="checkbox"/>	
Jonathan Bordelon	29% (38) 50% (64) 16% (20)	10/12/22		<input type="checkbox"/>	<input type="checkbox"/>	
Brian Basis Planning Mikinski	36% (47) 11% 39% (50)	10/27/22		<input type="checkbox"/>	<input type="checkbox"/>	
Nate St. John	15% (19)	10/19/22		<input type="checkbox"/>	<input type="checkbox"/>	
Jonathan Bonathan	Not started			<input type="checkbox"/>	<input type="checkbox"/>	
Jonathan Bordelon	Not started			<input type="checkbox"/>	<input type="checkbox"/>	
Jordan Brooks	Not started	11/9/22		<input type="checkbox"/>	<input type="checkbox"/>	

REGISTER THRESHOLD

If a markup is provided with a schedule duration adjustment more higher than the value defined, a Project Register Event is required with the markup.

Start Review Cycle
 Start Review Cycle to solicit expert feedback from project team members

START REVIEW CYCLE

Message
 Explain to your team members the purpose of the review cycle as well as what to focus on. This message will appear in popup at the start of Markup

22.10 Markup Group Testing! Let's Markup!

Register Threshold
 Difference in Schedule Duration and Team Member Markup that requires a Register entry

None ▾
 None
 +/- 10%
 +/- 25%
 +/- 50%

Team Member Markup

Assignee	Team Contribution	Last Accessed	Ready For Rev...	Show Whole P...	Show Cost	Clear
Brian	66% (85) 17% (22) 12%	9/30/22		<input type="checkbox"/>	<input type="checkbox"/>	

TEAM MEMBER MARKUP

The Team Member Markup, shows a list of users who have permissions to provide feedback.

NOTE

To remove reviewers, go back to Plan view and use the Iris to unassign them as Markup Contributors.

Team Member Markup						
Assignee	Team Contribution			Last Accessed	Ready For Rev...	Clear Markup
Brian	66% (85)	17% (22)	12%	9/30/22	<input type="checkbox"/>	<input type="checkbox"/>
Nicole	51% (66)	16% (21)	27% (35)	10/12/22	<input type="checkbox"/>	<input type="checkbox"/>
Jonathan	29% (38)	50% (64)	16% (20)	10/12/22	<input type="checkbox"/>	<input type="checkbox"/>
Brian	36% (47)	11%	39% (50)	10/27/22	<input checked="" type="checkbox"/>	<input type="checkbox"/>

Column	Description
Assignee	First and Last name of contributor.
Team Contribution	Visual percent complete of items reviewed vs assigned.
Last Accessed	Last instance the contributor was in the Schedule system.
Ready for Review?	Confirmation the contributor has finished their markups.
Show Whole Project	Toggle if contributors see the whole project or only items they are assigned to.
Show Cost	Toggles if cost is shown when providing markups.
Clear Markup	Clear/delete markups made.

EXPORT OPTIONS

The Export User Markup function lets you export the markup data to excel after the review has been completed. This creates an archive of the data for reference.


NOTE

Markups can only be exported per cycle. Once a new cycle is initiated, the previous cycle is over written. Exporting after a cycle saves the data before it is overwritten.

START/STOP A REVIEW CYCLE

Once all the Review Cycle settings have been set, select the Start Review Cycle button at the top of the page in . This will begin the review cycle for Project Contributors to provide feedback and markup the schedule.

Start Review Cycle

Start Review Cycle to solicit expert feedback from project team members

START REVIEW CYCLE

Message

Explain to your team members the purpose of the review cycle as well as what to focus on. This message will appear in popup at the start of Markup

22.10 Markup Group Testing! Let's Markup!

GENERATE A REVIEW CYCLE

1. Select **Manage Review Cycle**. The team members that you added are listed but they have not taken any action yet

Team Member Markup							
Assignee	Team Contribution			Last Accessed	Ready For Rev...	Show Whole P...	Show Cost
Brian Mikinski	66% (85)	17% (22)	12%	9/30/22		<input type="checkbox"/>	<input type="checkbox"/>
Nicole Phillips	51% (66)	16% (21)	27% (35)	10/12/22		<input type="checkbox"/>	<input type="checkbox"/>
Jonathan Bordelon	29% (38)	50% (64)	16% (20)	10/12/22		<input type="checkbox"/>	<input type="checkbox"/>
Brian Basis Planning Mikinski	36% (47)	11%	39% (50)	10/27/22	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

- 2. Switch the Show Whole Project to **ON** for the persons you want to be able to view the entire project schedule. By default the markup users only see the section of the project that you have assigned them to

Team Member Markup							
Assignee	Team Contribution			Last Accessed	Ready For Rev...	Show Whole P...	Clear Markup
Brian Mikinski	<div><div></div><div></div><div></div></div> <div>66% (85)17% (22)12%</div>			9/30/22		<input checked="" type="checkbox"/>	<input type="checkbox"/>
Nicole Phillips	<div><div></div><div></div><div></div></div> <div>51% (66)16% (21)27% (35)</div>			10/12/22		<input type="checkbox"/>	<input type="checkbox"/>
Jonathan Bordelon	<div><div></div><div></div><div></div></div> <div>29% (38)50% (64)16% (20)</div>			10/12/22		<input checked="" type="checkbox"/>	<input type="checkbox"/>
Brian Basis Planning Mikinski	<div><div></div><div></div><div></div></div> <div>36% (47)11%39% (50)</div>			10/27/22	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

- 3. Enter your message to provide guidance to the team members.

Message

Explain to your team members the purpose of the review cycle as well as what to focus on. This message will appear in popup at the start of Markup

Please review.

- 4. Click **Start Review Cycle**.
- 5. Click **Yes** to updating the project baseline.

Do you want to update the Project Baseline before beginning this Review Cycle?

Project Baselines allow you to visualize the impact of the Markup Review process.

YES

NO

As markups are being made, you can refresh the Manage Review Cycle page to see what percent complete contributors are with their markups

Team Member Markup

Assignee	Team Contribution	Last Accessed	Ready For Review?	Show Whole Project	Show Cost	Clear Markup
Allen Paddock	<div><div>25%</div><div>15%</div><div>58% (28)</div></div>	2 years ago		<input type="checkbox"/>	<input type="checkbox"/>	
Ben Heights	<div><div>17%</div><div>29% (14)</div><div>52% (25)</div></div>	2 years ago		<input type="checkbox"/>	<input type="checkbox"/>	
Christy Tuppance	<div><div>31% (15)</div><div>10%</div><div>40% (19)</div></div>	2 years ago		<input type="checkbox"/>	<input type="checkbox"/>	
Bridgette Quintero	<div><div>10%</div><div>10%</div><div>24%</div></div>	5 months ago		<input type="checkbox"/>	<input type="checkbox"/>	
Susan Cappelloni	<div><div>20%</div></div>	2 years ago		<input type="checkbox"/>	<input type="checkbox"/>	
Overall	<div><div>22%</div><div>16%</div><div>46% (78)</div></div>					<div>REMOVE ALL</div>

EXPORT USER MARKUP

NOTE The color coding of the Team Contribution visualizes the summaries:

- Green:** Percent of items marked up reducing duration
- Orange:** Percent of items marked up increasing duration
- Yellow:** Percent of items marked as planned duration is OK
- White:** Percent of items pending review

6. Click **End Review Cycle** after markups have been submitted.

End Review Cycle


End Review Cycle to review Markup from team members

END REVIEW CYCLE


MARKING UP THE SCHEDULE

UNCERTAINTY

User assigned sections for markup and review can begin to provide feedback in the Markup view.

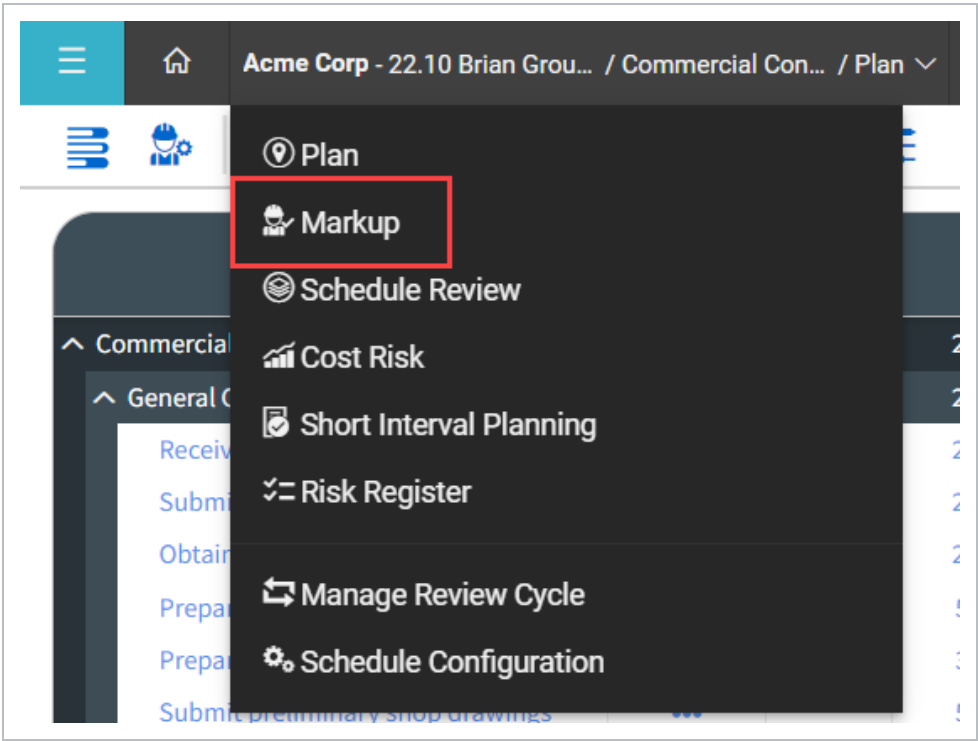


The My Markup Status confirmation box opens to show markup status information.

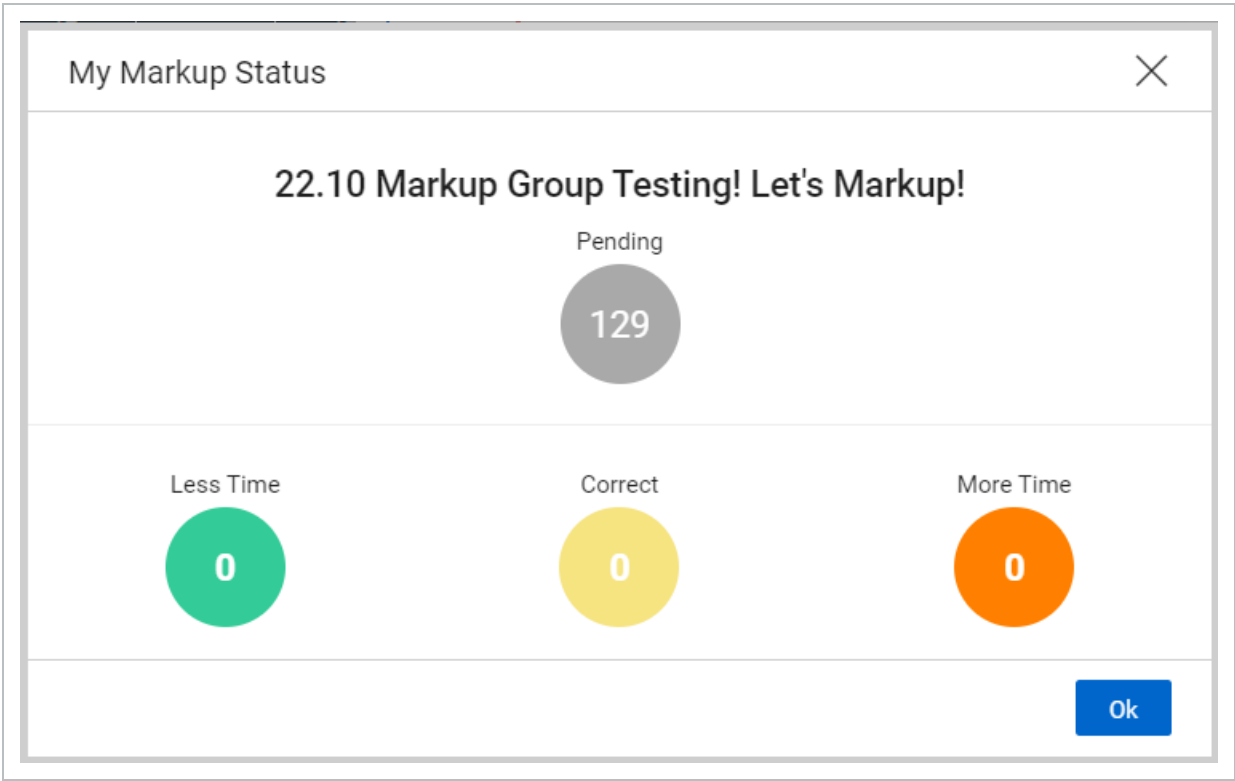

After the schedule is in the Markup view, contributors can begin to give feedback on the schedule. Markups made to increase or decrease durations on the schedule in turn generate uncertainty.

Uncertainty is an internal factor, such as quantity growth or productivity loss or gain. It evaluates duration or cost realism and plan confidence.

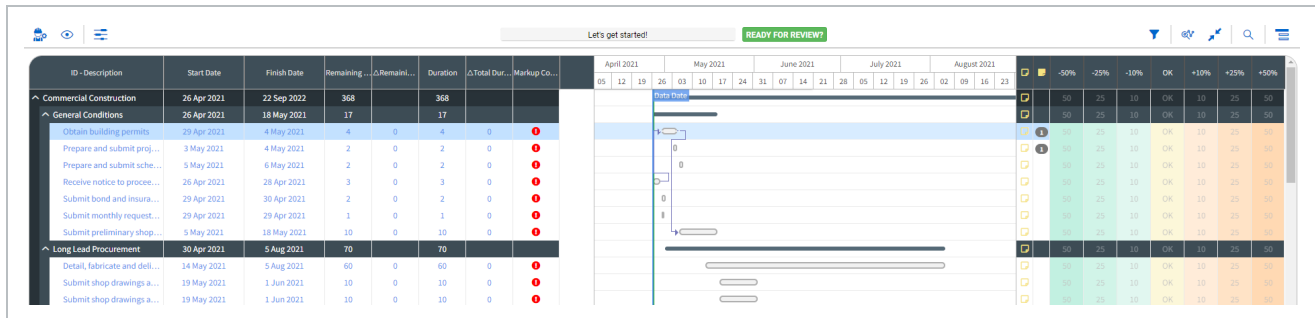

SCORECARD VALUES

The scorecard provides a quick and easy way to give an estimate of whether the planned durations need to be increased or decreased. Selecting a percentage increases or decreases the duration by that amount.

		-50%	-25%	-10%	OK	+10%	+25%	+50%
		50	25	10	OK	10	25	50
		50	25	10	OK	10	25	50
	1	50	25	10	OK	10	25	50
	1	50	25	10	OK	10	25	50
		50	25	10	OK	10	25	50
		50	25	10	OK	10	25	50
		50	25	10	OK	10	25	50
		50	25	10	OK	10	25	50
		50	25	10	OK	10	25	50

As markups are made on the scorecard, the bars on the Gantt chart adjust accordingly. This gives project contributors a live view of how the schedule is impacted by their markups.

MARKING UP THE SCHEDULE VIA THE SCORECARD

- ## My Markup Status

Please complete all markups by EOD mm/dd/yy at 00:00

Pending

52


Less Time Correct More Time

0 0 0


OK

Category	Count
Pending	52
Less Time	0
Correct	0
More Time	0


- Page 221 of 291

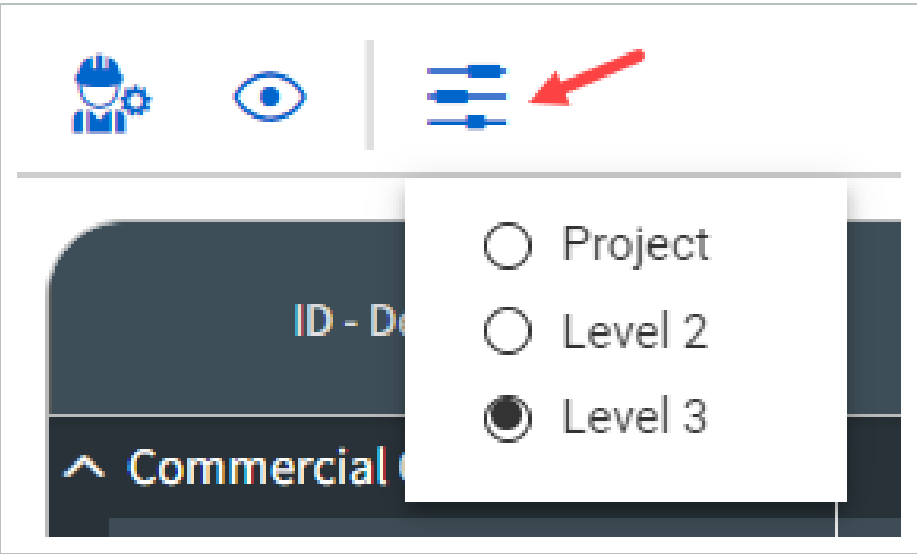

5. Go to the scorecard and adjust activities by selecting a markup score. Activities should show a Lock icon once selected, confirming the markup made.

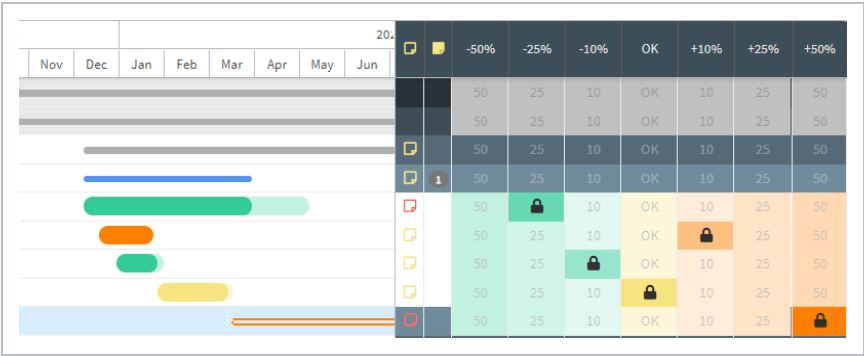



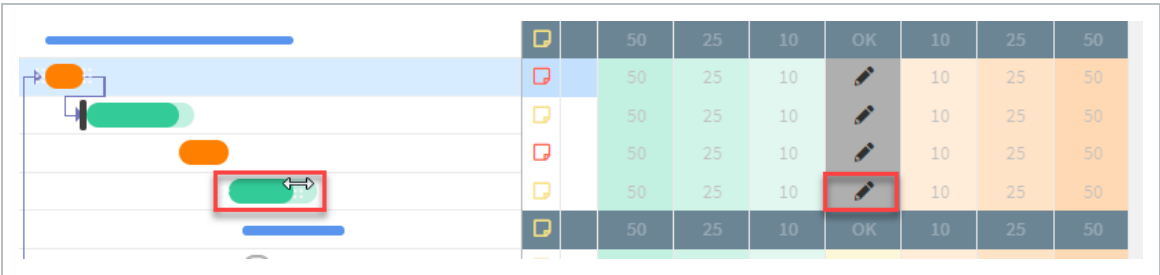







6. Go to the Gantt chart and slide the start or end bars around to adjust duration.
- The scorecard will changes the icons to a pencil, signifying a custom duration adjustment was made.



NOTE

Markups meeting or exceeding the threshold, established in the Manage Review Cycle settings, will change the Event Register icon to red, signifying the user is to add an event to the Events Register.

		50		10	OK	10	25	50
		50	25	10	OK		25	50
		50	25		OK	10	25	50
		50	25	10		10	25	50
		50	25	10	OK	10	25	

This page intentionally left blank.

LESSON 9 – SCHEDULE REVIEW PROCESS - RISK OVERVIEW

REVIEW AND RISK PROCESS OVERVIEW

The Review process is where you can review feedback from markup, and apply a variety of intelligence rankings in order to run a risk assessment on your project.

Uncertainty is an internal factor, such as quantity growth or productivity loss or gain. It evaluates duration or cost realism and plan confidence.

A **Risk Event** is an external factor where events are discrete and measurable, such as third-party delays or unexpected labor shortages. It evaluates the probability of the event occurring, the schedule impact should the event occur, and any impact in associated costs.

NOTE

Projects often tend to mix uncertainty and risks events together resulting in less accurate mapping of risk characteristics to projects. It is important to evaluate risk items and place each in their appropriate categories, Uncertainty or Risk Event.

Uncertainty Category



- Quantity growth
- Productivity loss/gain
- Evaluates duration/cost realism & plan confidence

Risk Event Category




- External factors such as:
 - 3rd party delays
 - Labor shortages
- Evaluates probability of occurring event plus schedule impact & associated impact costs


This feedback can come from the Markup process outlined in other topics. From here, the following review process steps can help you conduct a risk assessment utilizing a confidence level, called a **P-value**.

The below steps explain how to generate a Risk Adjust project:


- 1. From the Project View drop-down, select **Review**.

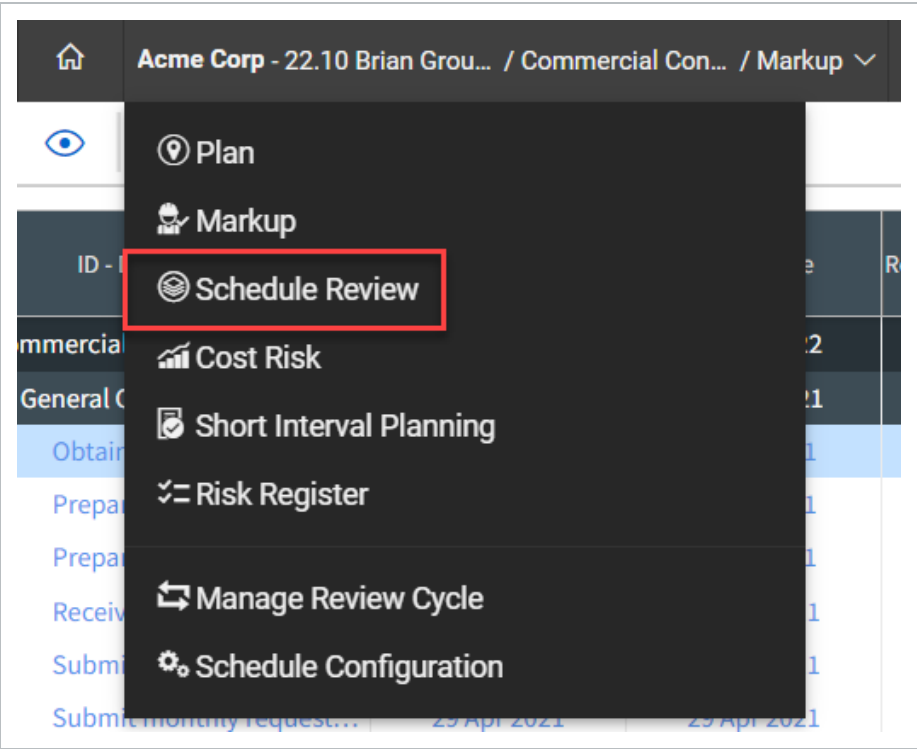


- 2. Select a P-value for instant insight during the review process by first selecting the **P-value** icon .

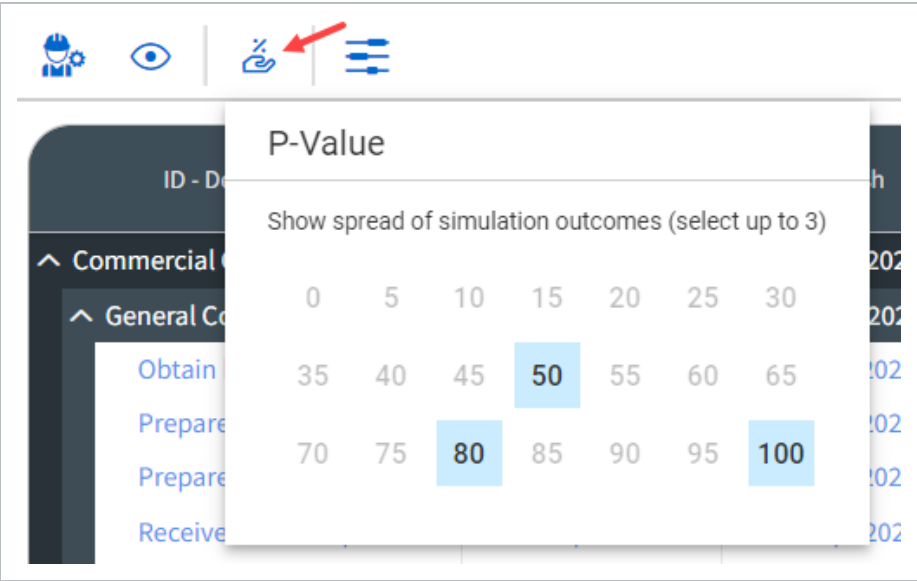

- A P-value of 100 represents a worst case scenario, while a value zero represents a best case scenario
 - You are assigning a confidence level against a target goal
3. Switch the **Uncert** and **Events On/Off** to be applied to the corresponding work package or terminal level.
- This feature includes or excludes that detail in the risk model. It is recommended to begin analysis with both options switched to the *On* position.

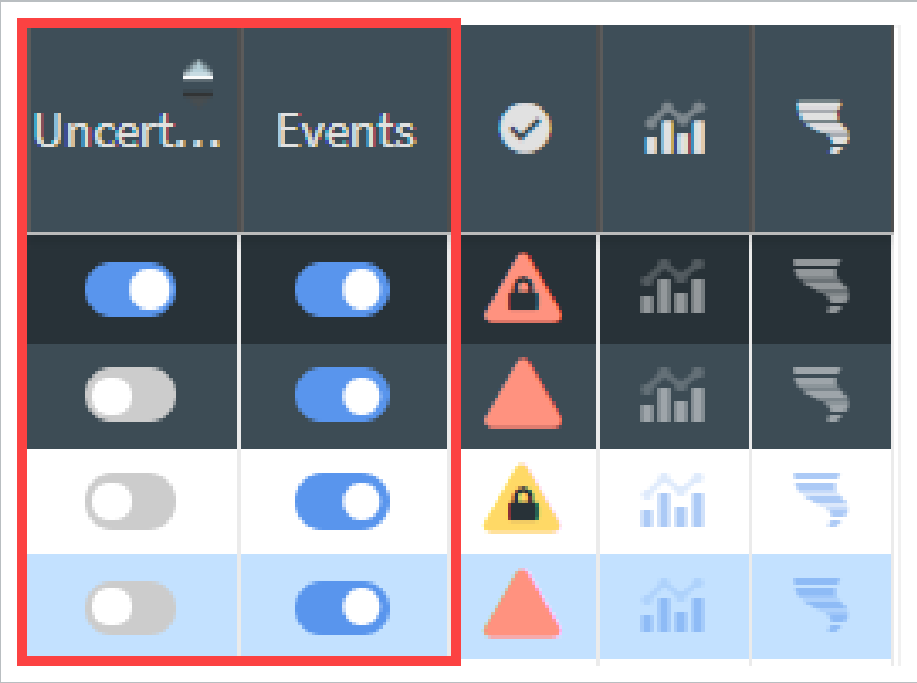


4. Move down the project and review contributor's Uncertainty rankings for each line item.
- When reviewing Uncertainty, there are three main options for generating adjustments to the project: Artificial Intelligence (AI), Human Intelligence (HI), and Risk Intelligence (RI)



5. As needed, assign **Register Events** to project items.


- Any item in a project may be assigned a Register Event
- The default categories are shown below:

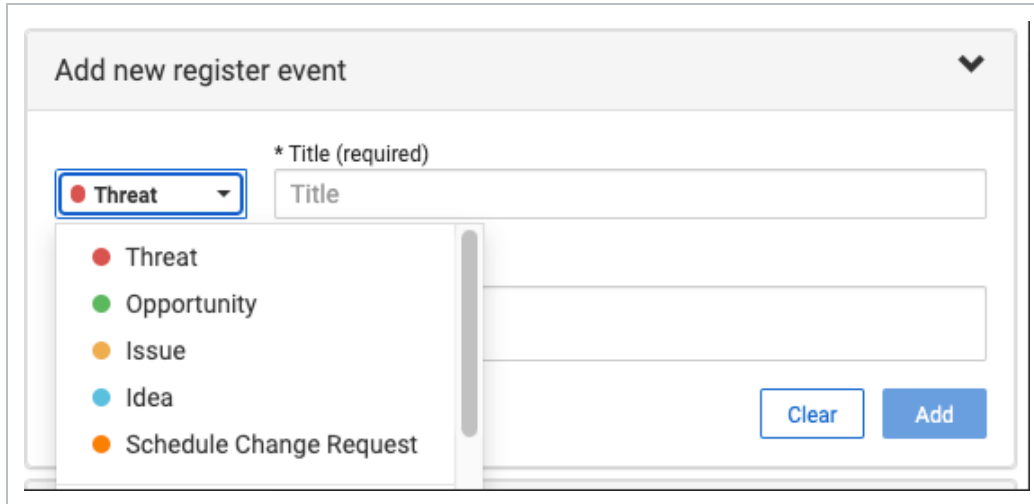


The screenshot shows a dialog box titled "Add new register event" with a dropdown arrow in the top right corner. Inside the dialog, there is a dropdown menu on the left with a red circle icon and the text "Threat". Below this menu is a list of options: "Threat" (red circle), "Opportunity" (green circle), "Issue" (orange circle), "Idea" (blue circle), and "Schedule Change Request" (orange circle). To the right of the dropdown menu is a text input field labeled "* Title (required)" with the placeholder text "Title". Below the text input field is a large empty text area. At the bottom right of the dialog are two buttons: "Clear" and "Add".


- After all uncertainty and events have been agreed to, you can access two main reports that provide insight into the project's risk:

- Risk histogram 

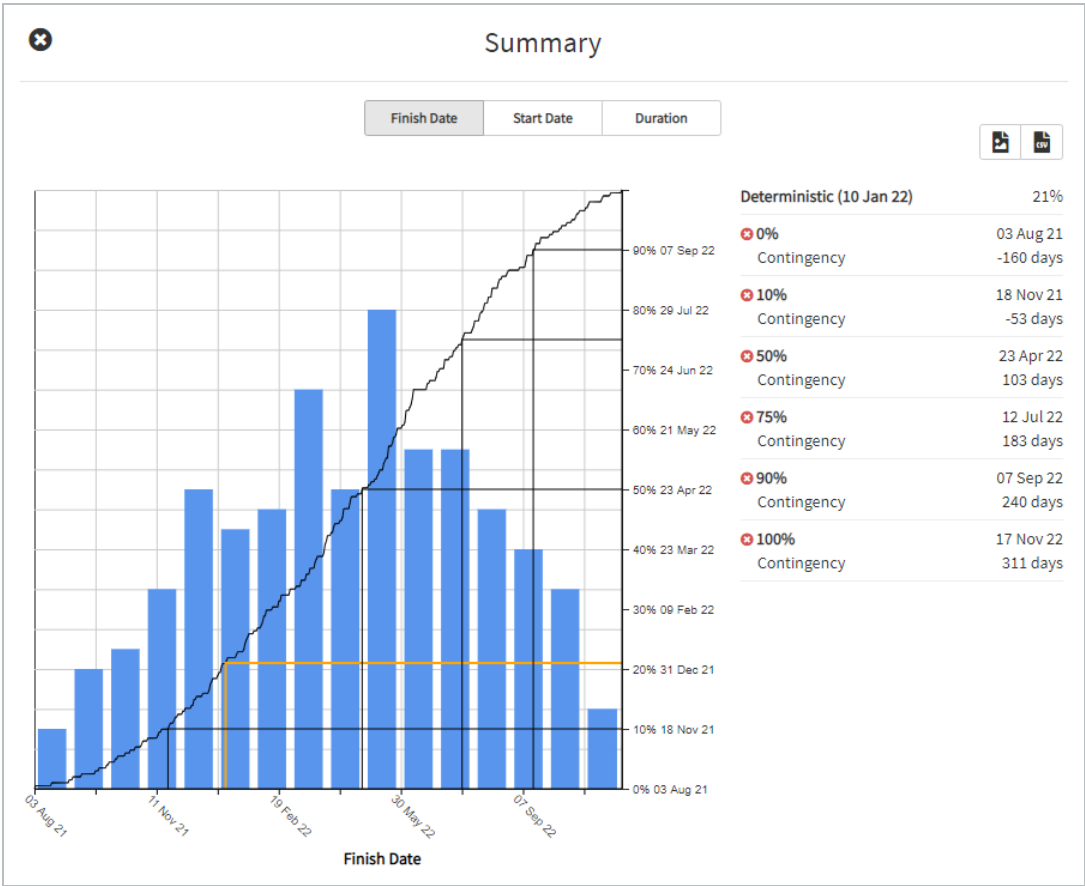


- Tornado analysis 

You can identify how often activities fall upon the critical path during Monte Carlo simulation runs. The image below shows the Criticality % view active.

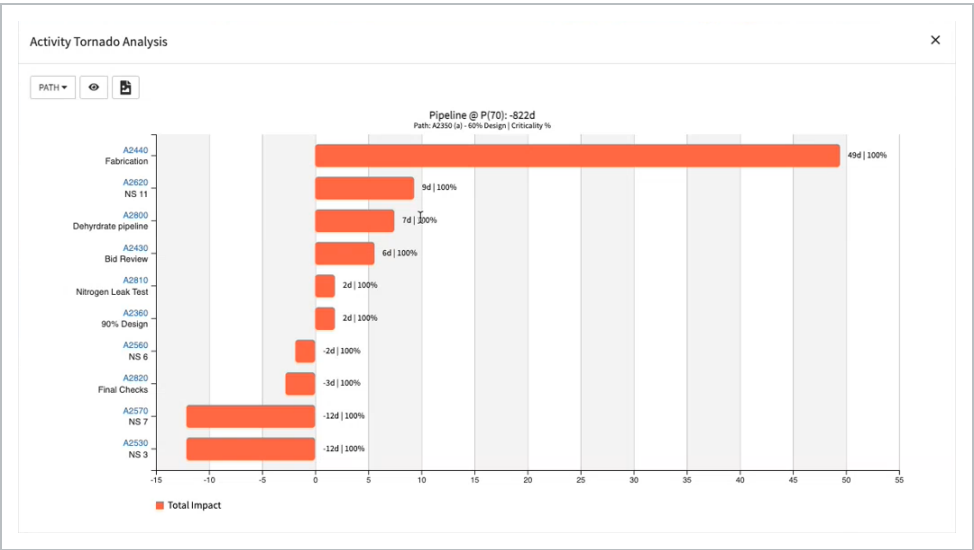


Using Float Consumption, you can visualize hidden risk assignments due to float consumption and compare activity risk tolerance versus net impacts. The image below shows the Float Consumed and the Criticality % views active.

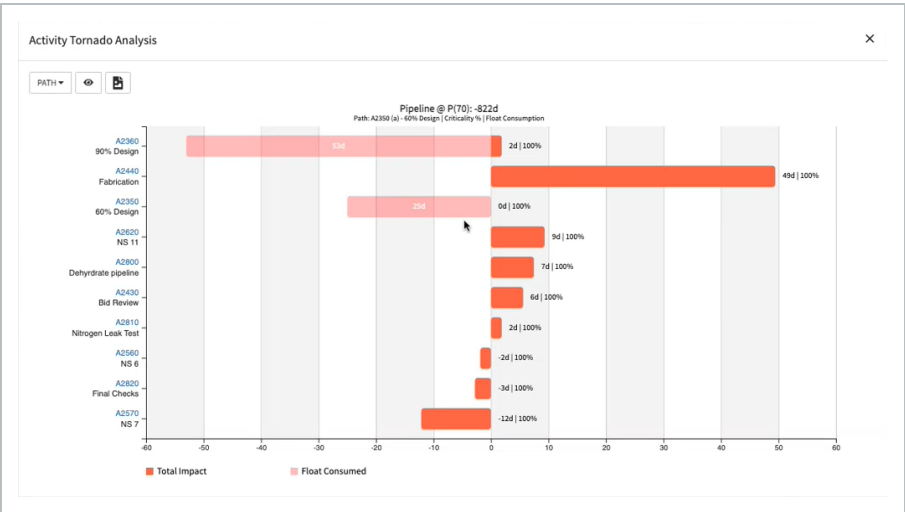

6. Adopt any part of the risk model by selecting **Adopt Markup** or **Apply Uncertainty adjustments to deterministic schedule**. Both options will run a Critical Path Method schedule calculation and generate a new risk adjusted project schedule.


IMPORT/EXPORT

You can Import and Export risks in the project register. There are options for Oracle PRA – Pertmaster and Deltek Acumen. These are simple Excel formats that can also be generated outside of any tool and used for importing into Schedule.

A screenshot of the 'Import/Export' dialog box. The dialog has a close button (X) in the top left corner and a document icon with a right-pointing arrow in the top center. Below these is a section titled 'Action' with two buttons: 'Import' (selected) and 'Export'. Underneath is the text 'Import new or updated register events and their associations to activities within this project'. The next section is titled 'File Format' and has two buttons: 'Oracle PRA - Pertmaster' (selected) and 'Deltek Acumen'. Below that is a section titled 'File (.xlsx)' with a 'Choose File' button and the text 'No file chosen'. At the bottom of the dialog is a large green button labeled 'IMPORT'.

ADD REGISTER EVENT

You can manually add a register event to the project register. Select **Add Register Event** and then define the event type and description.



Risk

of

Event

Cause

Effect

Risk of _____ due to _____ resulting in _____

ADD

CANCEL

FILTER

Select the **filter** icon to enable filtering for the register view.



MATRIX DEFINITION

The default matrix in the Knowledge Library is adopted when the project is created. The matrix can be tailored by project to create a probability and severity range that is appropriate for the project.

Events RegisterRegister TypesMatrix Definition

ATTRIBUTES

EDIT

Description	Probability	Schedule Impact	Cost Impact	Color
Very Low	5%	7 days	\$100	<div></div>
Low	25%	30 days	\$1,000	<div></div>
Medium	50%	60 days	\$10,000	<div></div>
High	75%	90 days	\$100,000	<div></div>
Very High	95%	180 days	\$1,000,000	<div></div>

RELEVANT LINKS

- Manage Markup Review Cycle Quick Guide
- Markup Process Quick Guide
- Video - Manage Review Cycle
- Course - Schedule Feedback and Updates

P-VALUE OVERVIEW

Probability Values or **P-values** are the lens with which you can view instant feedback related to the affects risk or opportunity items have on the planned schedule and/or cost structure.

You can interact with P-Value to manipulate your visibility into a risk-adjusted project.



Select a P-value by clicking on the P-value icon to show a drop-down displaying the options for selecting a value.

P-Value

Expected Value

0

5

10

15

20

25

30

35

40

45

50

55

60

65

70

75

80

85

90

95

100


A P-value of 75 can be interpreted as “we are 75% confident in hitting or beating a target goal”.

The selected P-value shows adjustments to items such as dates and durations. When a risk assignment has an effect to the project, the P-value lens shows in red, how it affects the project. In this example, the duration for “Create Early Stage Construction Docs” increases from a planned duration of 63 to a P-value 75 adjusted duration of 91.

ID - Description	Start Date	Finish Date	Dur	Float	Uncert	Events
Multi-Use Commercial	18 Feb 19 A 18 Feb 19 A	07 Jan 22 17 Jan 23	1055 1430		<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>
Preconstruction	18 Feb 19 A 18 Feb 19 A	21 Feb 20 11 Dec 20	369 663		<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>
Design	18 Feb 19 A 18 Feb 19 A	17 Sep 19 26 Jun 20	212 495		<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>
Create Early Stage Construction Docs	21 Jun 19 21 Feb 20	17 Sep 19 26 Jun 20	63 91	0 0	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>

MARKUP FEEDBACK AND CONSENSUS

Once a markup cycle has been completed, it is ready for review. When selecting a line item for review, options appear in IRIS located on the right of the panel.

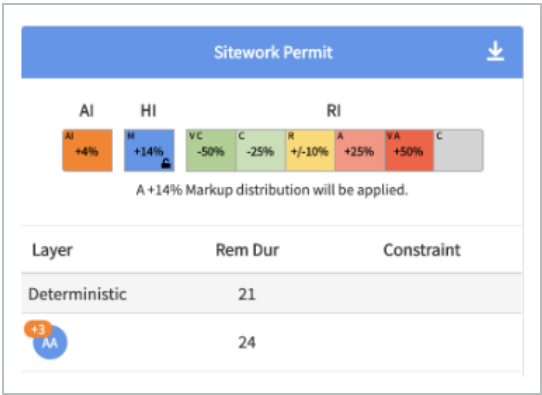


The reviewer has three options for providing markup feedback:

- **Inference Engine (AI)** suggested distribution
- **Human Intelligence (HI)** to leverage the feedback given during the Markup phase
- **Risk Intelligence (RI)** allows you to assign designated uncertainty ranges to any line item


INFERENCE ENGINE (AI)

In this example, if you use the Inference Engine (AI), it applies the suggested distribution of 4%.

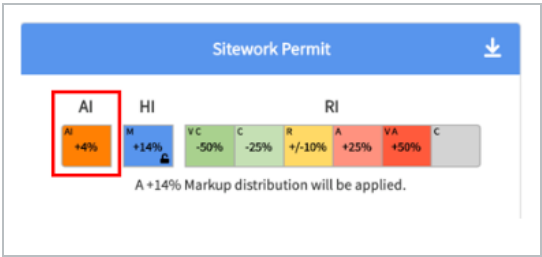


HUMAN INTELLIGENCE (HI)

If you use the **Human Intelligence (HI)** of +14%, using AA’s (delegate’s initials) feedback, that Remaining Duration will take +3 days longer (24d v 21d).

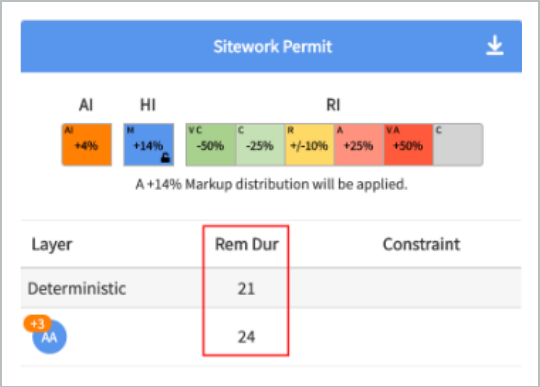

RISK INTELLIGENCE (RI)

By selecting RI, you have chosen to not use HI or AI for that line item.

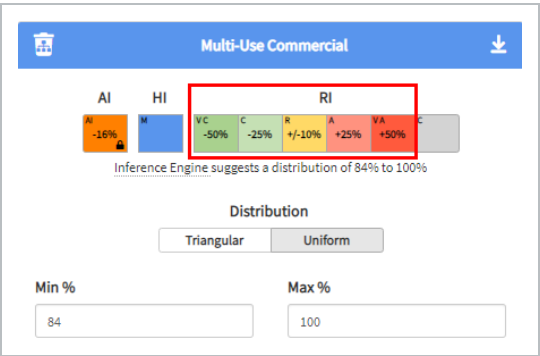

Uncertainty ranges are based on one of five categories the following categories:


Classification	Range	Guidance
Very Conservative	50% - 100%	Could take as little as 50% less
Conservative	75% - 105%	Most likely less
Realistic	90% - 110%	Within +/- 10%
Aggressive	95% - 125%	Most likely more
Very Aggressive	100% - 150%	Could take up to 50% more

NOTE

You may only use one type of intelligence source per line. By selecting RI, you have chosen to not use HI or AI for that line item.

CUSTOM


Using the Custom Intelligence lets you use a user defined level of risk.

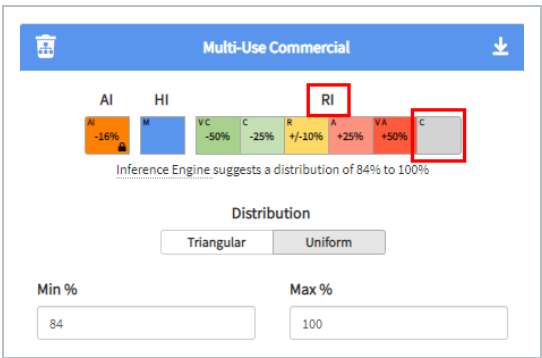

Any changes that impact the project, either positive or negative, are shown in red.

MULTIPLE USER FEEDBACK

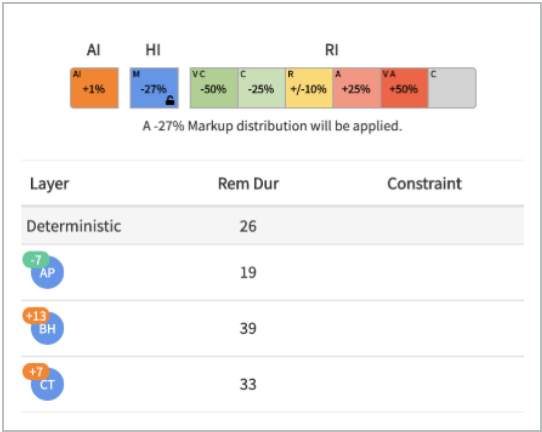


In the event an item contains more than one member’s feedback, you can still decide between the different intelligence types. The Layer column shows all the members that contributed to that item.






Notice here where three members contributed their feedback:

- AP (-7)
- BH (+13)
- CT (+7)

These values are added to the deterministic value to generate corresponding values.

Layer	Rem Dur	Constraint
Deterministic	26	
 AP	19	
 BH	39	
 CT	33	

If you decide to consider all the HI feedback, then a distribution triangle is automatically applied for the risk simulation distribution.

Deterministic	26
 AP	19
 BH	39
 CT	33


Distribution

☒ Triangular ☐ Uniform

Min

Likely

Max




In some scenarios you have the option of setting a distribution to a triangular or uniform curve. A triangle uses the three points (min, likely, max) to generate a weighted distribution. A uniform distribution will use two points (min,max) as limits to a range and set the probability to an equal state for within the parameters.

If you want to discount or ignore a particular feedback, click on the contributor to remove them from the feedback. The distribution triangle adjusts automatically.



DISTRIBUTION OPTIONS

When applying RI to a project item, you have the options to either set distribution to triangular or uniform distribution. A triangle uses three points of information, Min, Likely, and Max, to form a weighted distribution.

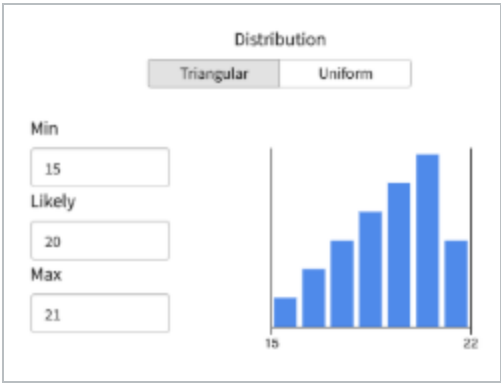

A uniform distribution uses two points, Min and Max to set limits on the range and models an even likelihood of hitting any points along the distribution.



UNCERTAINTY STATUS



The Uncertainty Status column indicates what type of markup feedback is applied to each line item, using one of the following symbols:

Symbol	Markup Feedback Assigned
	Inference Engine (AI)
	Human Intelligence (HI) with no markup values
	Human Intelligence (HI) with strong consensus, with little variations
	Human Intelligence (HI) with a large variation
	Risk Intelligence (RI) Very Conservative (-50%)
	Risk Intelligence (RI) Conservative (-25%)
	Risk Intelligence (RI) Realistic (+/-10%)
	Risk Intelligence (RI) Aggressive (+25%)
	Risk Intelligence (RI) Very Aggressive (+50%)
	Risk Intelligence (RI) Custom

NOTE

For Human Intelligence (HI) feedback, you can hover over the symbol to find the variation percentage.

For Inference Engine (AI) and Risk Intelligence (RI) feedback, the Uncertainty Status

Symbol will be a  if using Triangular distribution and a square  if using Uniform distribution.


TIP

The lock symbol represents that an uncertainty value has been applied to that line item and locks that value in place. For example, if a user assigns an uncertainty value to a parent line item, that value will be assigned to all its' children lines, expect for those that are locked in with a value previously assigned.


Once feedback on uncertainty and events are reviewed, you are ready to generate outcomes via Risk Histograms and Tornado Analysis.

RISK HISTOGRAM

The Risk Histogram visualizes results from numerous iterations made using the distributions assigned to line items. Click on the **Risk histogram** icon next to any line item to report against that point in the project.

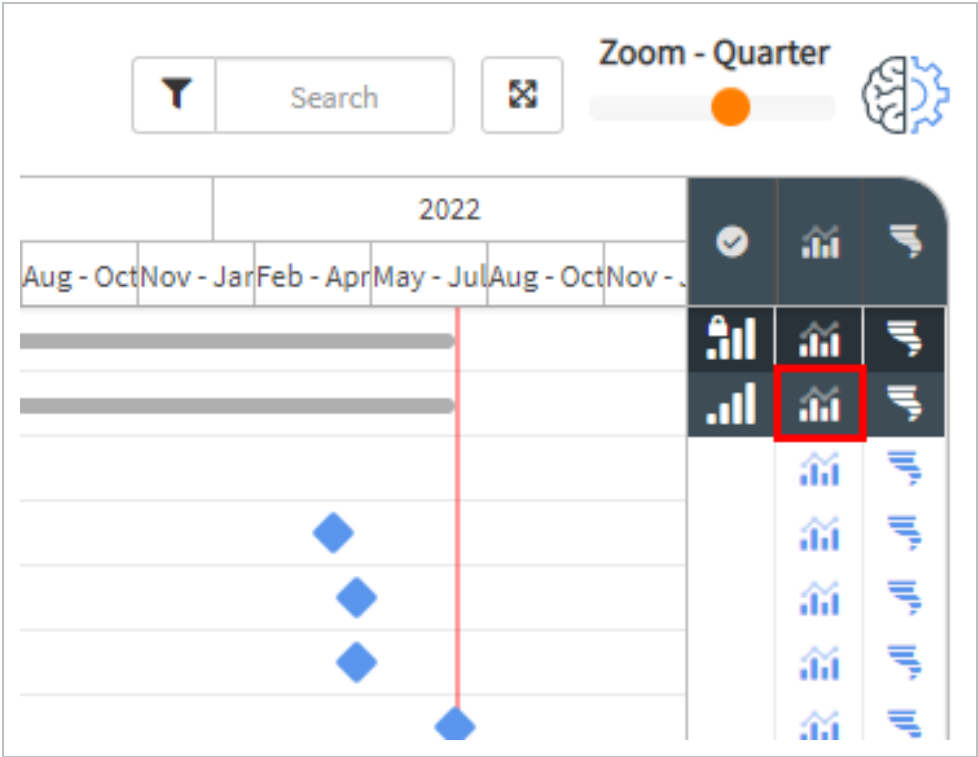


By clicking on the Risk histogram icon at the top level, you can report on the total project, as shown below.

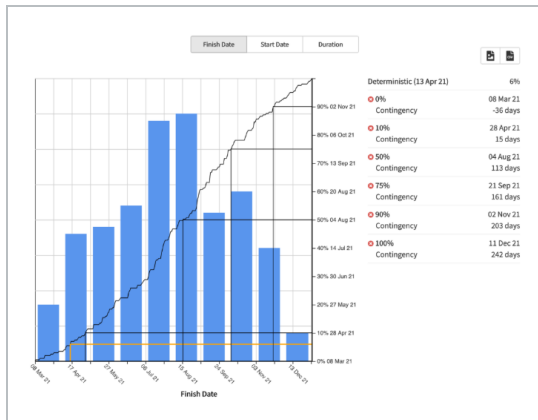

Blue bars indicate the number of iterations that land on a specific date; for this example, finish date. The information on the right provides insight into the probability of hitting the deterministic end date and indicate which dates align with various P-values. This example shows the following:

- A 6% chance of completing the project by the deterministic date of 13 Apr 21.
- P-75% shows a date of 21 Sep 21, a 161-day extension upon the deterministic date. This corresponds to the need for a contingency value of 161 days to be 75% confident in finishing the project on 21 Sep 21 or earlier.
- P-0% is best case scenario and conversely, P-100% is worst case.

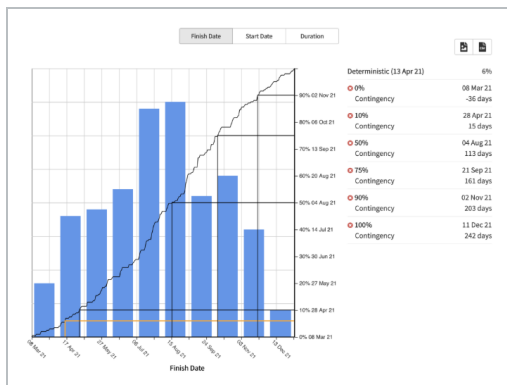


TORNADO ANALYSIS

Tornado Analysis shows key drivers that are responsible for the largest impact to a risk model. There are two main modes to choose from, Activity Mode or Risk Mode. Click on the **Tornado analysis** icon to select a mode. Similar to Risk Histogram, selecting a tornado icon at the top level will report on the total project.

COST ITEM MODE

Analyze the impact that terminal cost items have on the selected cost item.

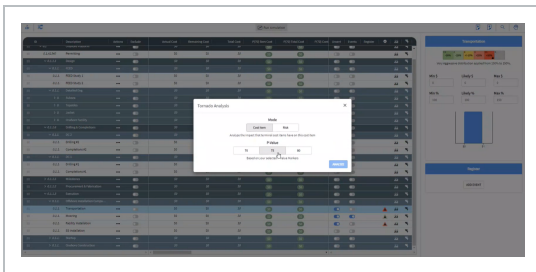


In this example, the P-Value is set to 75 based on the selected P-Values Markers. Selecting **Analyze** shows the Uncertainties and Risk Events for the Cost Item Tornado Analysis.




Interact with the following options to explore your project in Cost Item Mode:

- View
- Level
- Display Number

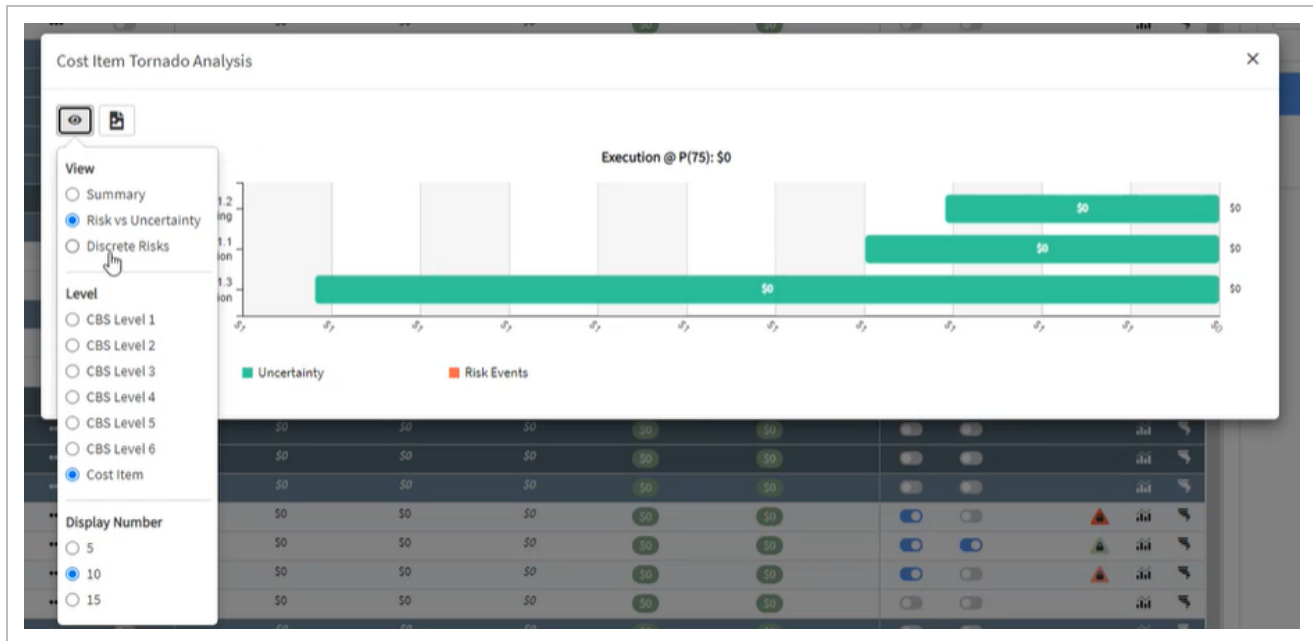

ROOT NODE IN COST RISK


Importing the Schedule Export report from Estimate to Schedule > **Cost Risk** inserts a root node into the project. The root node captures project-level data in Cost Risk for you to reference and report on. It also retains the hierarchical breakdown of the Estimate file.

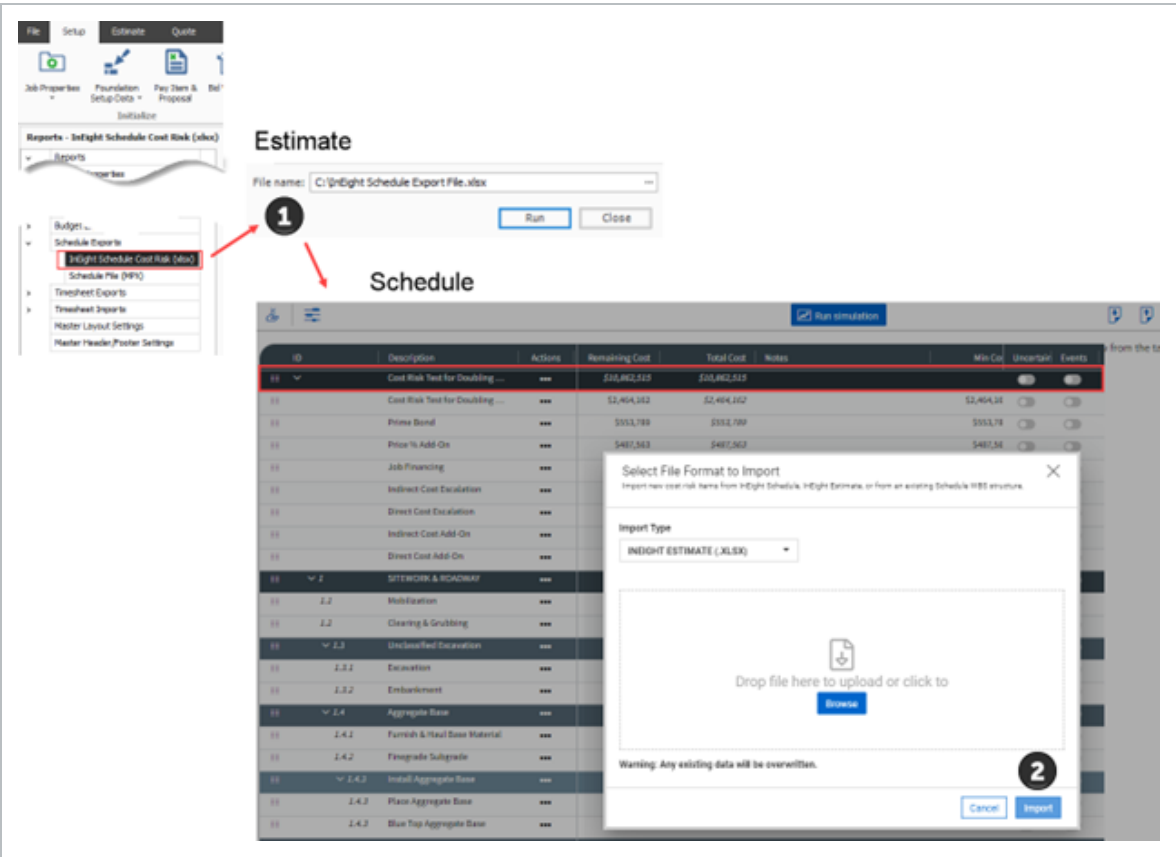

RISK MODE

Analyze the impact that risks have on the selected line item.

In the example below, you can visualize the most impactful risk events and their corresponding activities. The largest driver is Risk #3 (R3) on activity Establish Permitting Documents and accounts for 130d of risk exposure.

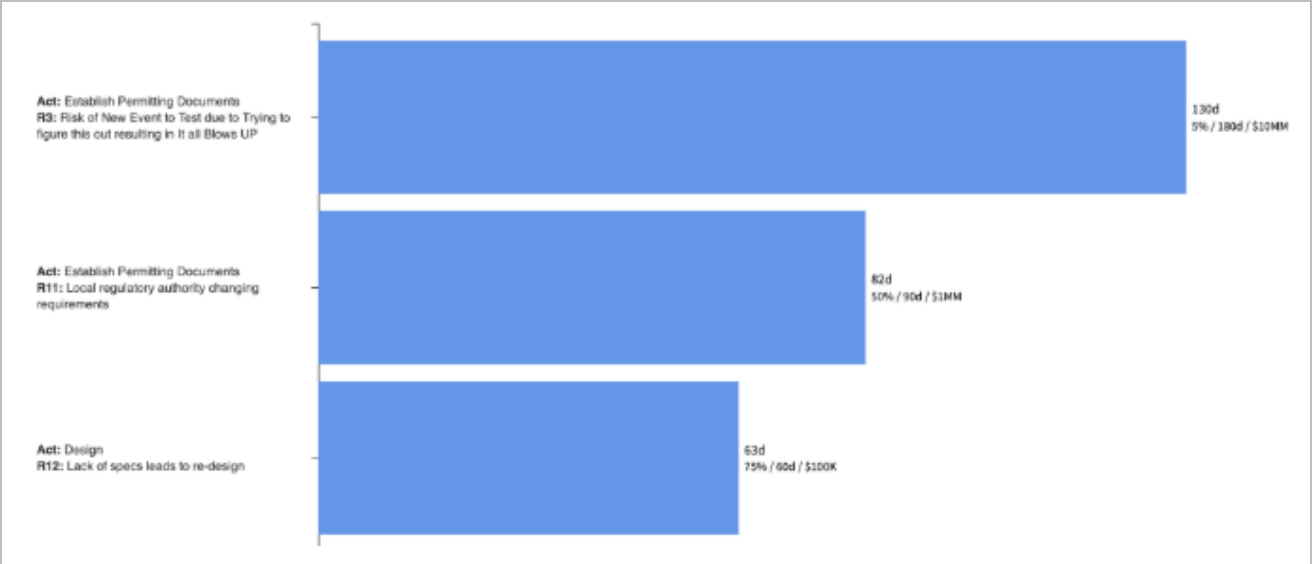


LESSON 9 – COST RISK

COST RISK OVERVIEW

Cost Risk lets you conduct risk analysis and update cost based on review.

The Actual Cost column represents the actual cost for a selected cost item prior to simulations with the option to display risk adjusted amounts based on use selection.

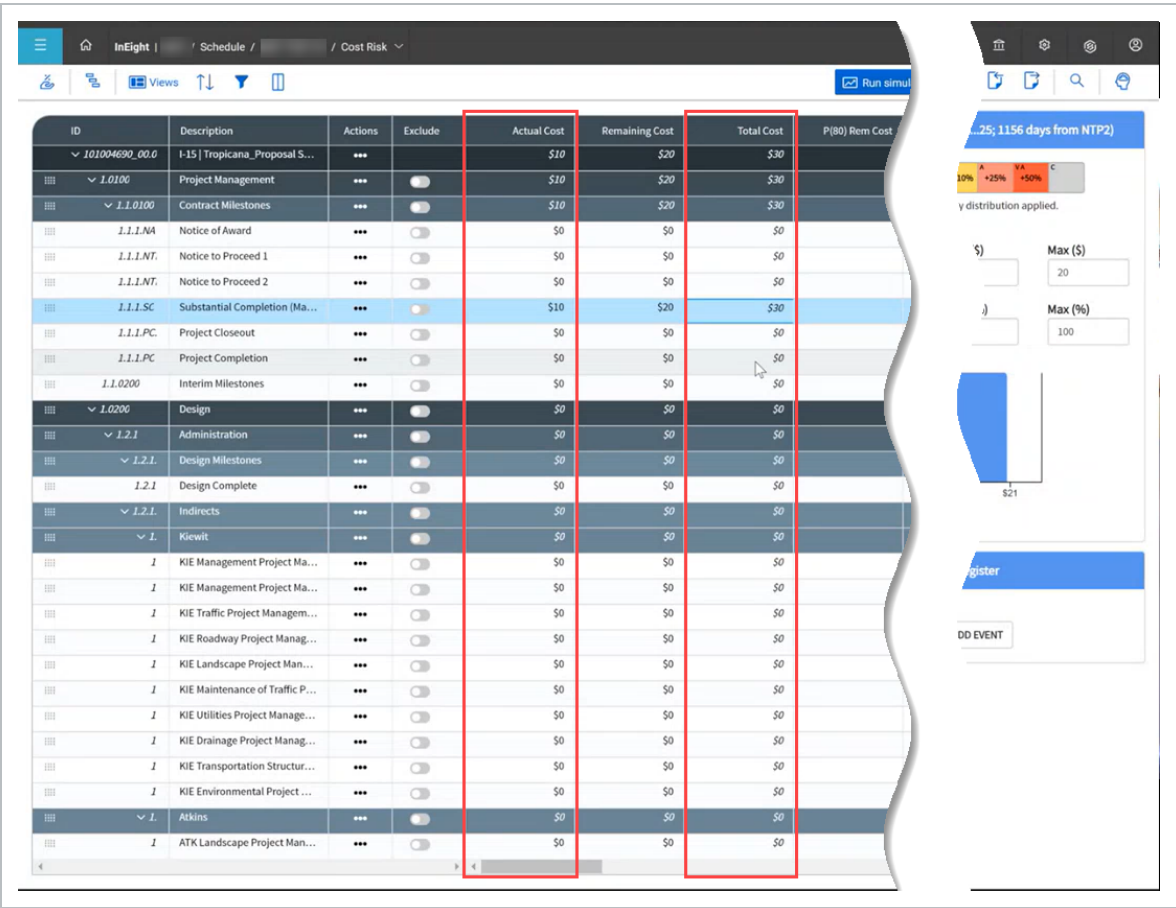

This column can also be edited directly on the page.

ID	Description	Actions	Exclude	Actual Cost
104969_01.01.00.00	I-15 Tropicana_Re...	...		\$4,323
1.0100	Project Management	...		\$4,323
1.1.0100	Contract Milestones	...		\$4,323
1.1.1.DS	Design Start	...		4323

You can also generate an InEight Schedule Cost Risk Excel file that allows you to import it into Schedule Cost Risk view and produce risk adjusted estimates. These risk adjusted estimates let you adjust contingency in an estimate to cover risk identified in a project.

FileSetupEstimateQuotePriceSystemIntegrations

Job Properties

Foundation Setup Data

Pay Item & Proposal

Bid Wizard

Initialize

Resources

Equipment

Materials

Resources

Labor

Resource Assemblies

Cost Item Assemblies

Standard Tables

Assemblies

Reports

Reports

Reports - InEight Schedule Cost Risk (xlsx)

File name: C:\Users\Paul.\Documents\InEight Schedule Export File.xlsx

Reports

Job Properties

Foundation Setup Data

Resources

Resource Register

Resource Changes

Resource Rate Details

Resource Utilization

Resource Utilization (Excel)

Resource Currency Comparison

Resource Assemblies

Cost Breakdown Structure

Quotes

Price Breakdown Structure

Pay Item & Proposal

Billing Rate Reports

Estimate Comparison Report

Audit

Job Register

InEight Schedule Cost Risk (xlsx)

Library Module

Custom Reports

Saved Views

Master Layout Settings

Master Header/Footer Settings

	A	B	C	D
1	CBS Position Code	Description	Total Cost (Forecast)	Suspend
2		Prime Bond	\$46,977.85	FALSE
3		Price % Add-On	\$294,100.61	FALSE
4		Job Financing	\$21,729.23	FALSE
5		Indirect Cost Escalation	\$2,131.11	FALSE
6		Direct Cost Escalation	\$15,048.80	FALSE
7		Indirect Cost Add-On	\$5,749.87	FALSE
8		Direct Cost Add-On	\$103,828.34	FALSE
9	1	SITEWORK & ROADWAY	\$2,464,161.56	FALSE
10	1.1	Mobilization	\$11,909.51	FALSE
11	1.2	Clearing & Grubbing	\$39,184.97	FALSE
12	1.3	Unclassified Excavation	\$233,915.81	FALSE
13	1.3.1	Excavation	\$149,922.88	FALSE
14	1.3.2	Embankment	\$83,992.94	FALSE

Run

Close

IMPORT COST RISK ITEMS

Select the import icon to import a Cost Breakdown Structure into the Cost Risk page, which helps you produce a risk adjusted estimate.

The screenshot shows the InEight software interface. The top navigation bar includes 'InEight | 23.12 Regression testing - Tatyana /' and a 'Cost Risk' dropdown. The left sidebar has a 'Views' section with icons for list, grid, and funnel views. The main content area is divided into two panes. The left pane shows a table of tasks:

ID	Description	Action
104969_01.01.00.06	I-15 Tropicana_Re...	
1.0100	Project Management	
1.1.0100	Contract Milestones	
1.1.1.DS	Design Start	...
1.1.1.Mobe	Mobilization	
1.1.1.NTP2	Notice to Proceed 2	
1.1.1.Durati	Project Duration	...
1.1.1.Start	Design and Constr...	
1.1.1.SC	Substantial Compl...	

The right pane shows the 'Design Start' task details. It includes a risk distribution chart with values: VC -50%, C -25%, R +/-10%, A +25%, VA +50%, and C. Below the chart, it states 'Conservative distribution applied from 75% to 105%'. Input fields are provided for Min (\$), Likely (\$), Max (\$), Min (%), Likely (%), and Max (%).

The cost risk file format import lets you import four different file types, which include InEight Schedule, InEight Estimate, InEight Control, and InEight Schedule.

The screenshot shows the 'Import Type' dropdown menu. The dropdown is open, displaying four options:

- INEIGHT SCHEDULE (.XLSX)
- InEight Schedule (.xlsx)
- InEight Estimate (.xlsx)
- InEight Control (.csv)
- InEight Schedule (WBS)

InEight Schedule imports the WBS from the Plan view page.

The Schedule .xlsx import lets you export an existing snapshot of the current cost risk schedule state, make any adjustments in Excel, and then import directly into the Cost Risk page.

You can import from Estimate and Control which imports values from each of these applications via .xlsx and .csv imports.


Only the InEight Schedule export type can be imported back in, and not the export.

If min/likely/max values or percentages are used, when importing from Schedule, ensure the use min, likely, max percentages toggle is turned *On*. If the .xlsx file being imported has a custom range, the uncertainty status must read Custom, then the pre-defined values configurations can be used.


The Schedule WBS import pulls the Actual Cost and Remaining Cost values, based on the assigned resources from the schedule.

STEP BY STEP – IMPORT COST RISK ITEMS


1. From the Schedule > **Cost Risk**, click the **Export** icon.

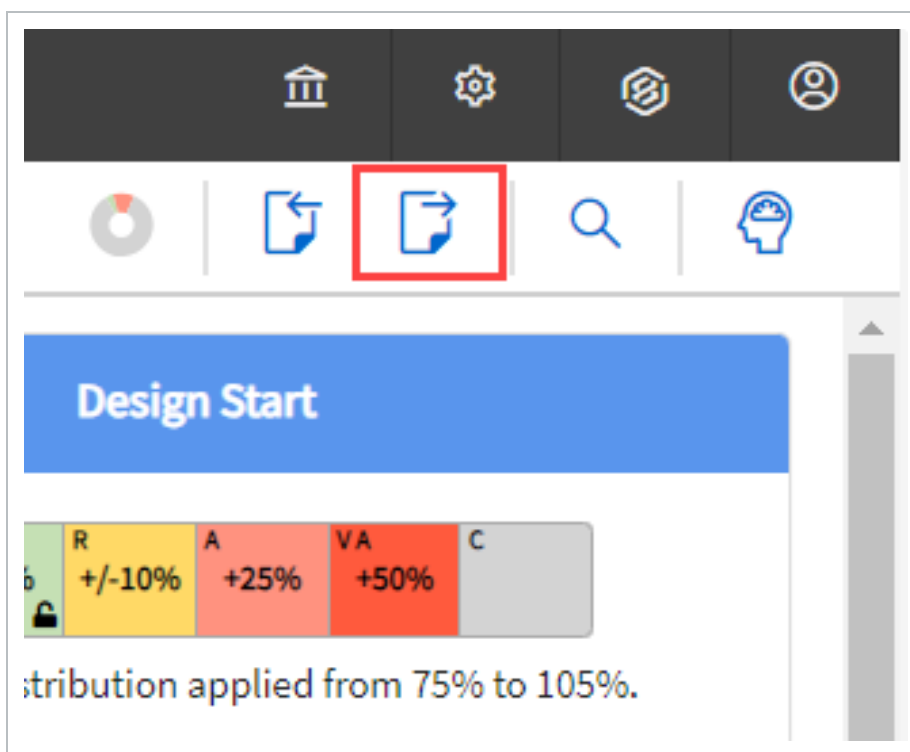


2. From the Export Type drop-down, select either **Data Import** or **InEight Schedule**. Open either file to change the contents of the file for step 4 below.
3. Click the **Import** icon.

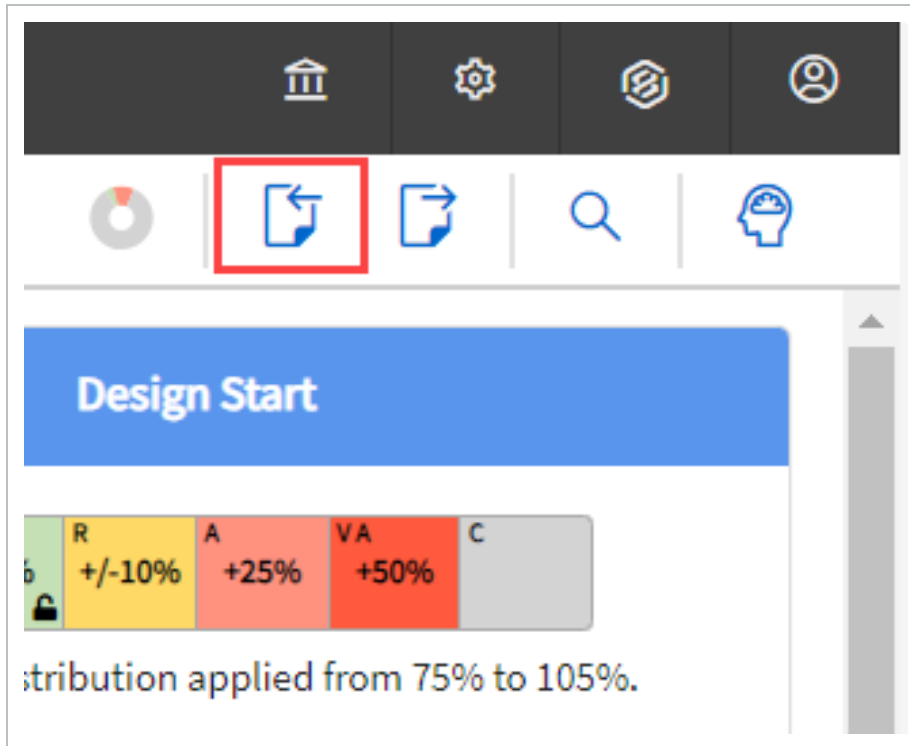

4. The Select File Format to Import pop-up window shows. The import type of InEight Schedule (.XLSX) is the default import type, and only accepts .XLSX file types. InEight Estimate also only accepts .XLSX file types. InEight Control only accepts .CSV file types, while InEight Schedule accepts only WBS file types.



- 5. You can either drag and drop a file into the upload portion of the window, or you can select the **Select Files** button to select a file.
- 6. Click **Import**.



ESTIMATE COST RISK EXPORT

You can generate a Schedule Cost Risk Excel file in Estimate, which lets you import it into the Schedule Cost Risk view and produce risk adjusted estimates. This can be accessed in Estimate > Setup > Reports > **InEight Schedule Cost Risk (.xlsx)**.

These risk adjusted estimates let you adjust contingency in an estimate to cover risk identified in a project.

The InEight Schedule Cost risk (.xlsx) fine can be generated from


File name: C:\Users\Paul.\Documents\InEight Schedule Export File.xlsx

	A	B	C	D
	CBS Position Code	Description	Total Cost (Forecast)	Suspend
2		Prime Bond	\$46,977.85	FALSE
3		Price % Add-On	\$294,100.61	FALSE
4		Job Financing	\$21,729.23	FALSE
5		Indirect Cost Escalation	\$2,131.11	FALSE
6		Direct Cost Escalation	\$15,048.80	FALSE
7		Indirect Cost Add-On	\$5,749.87	FALSE
8		Direct Cost Add-On	\$103,828.34	FALSE
9	1	SITWORK & ROADWAY	\$2,464,161.56	FALSE
10	1.1	Mobilization	\$11,909.51	FALSE
11	1.2	Clearing & Grubbing	\$39,184.97	FALSE
12	1.3	Unclassified Excavation	\$233,915.81	FALSE
13	1.3.1	Excavation	\$149,922.88	FALSE
14	1.3.2	Embankment	\$83,992.94	FALSE


Run Close

CONTROL COST RISK EXPORT

You can create a Cost Risk .CSV export specific view from Control in Control Workspaces. See the [Viewsets](#) topic to view more information on how to create viewsets. This helps you to more quickly revert to the Cost Risk Export Workspace view, when you need to export the cost risk associated data from Control.

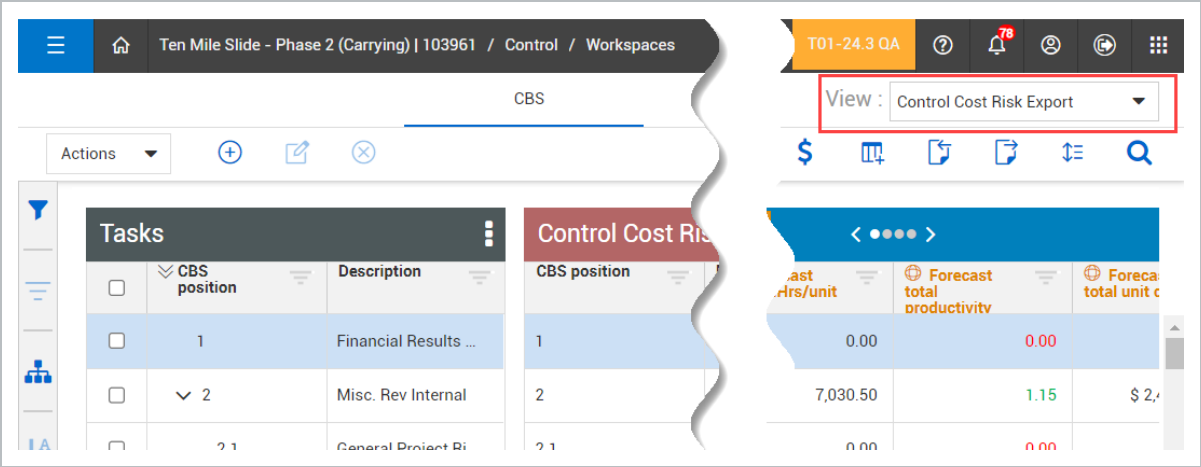

Create a new datablock to show the CBS Position Code, Description, Actual Cost (to date), and the Forecast Remaining Cost columns. View the [Datablocks](#) topic to view more information how to to create datablocks.

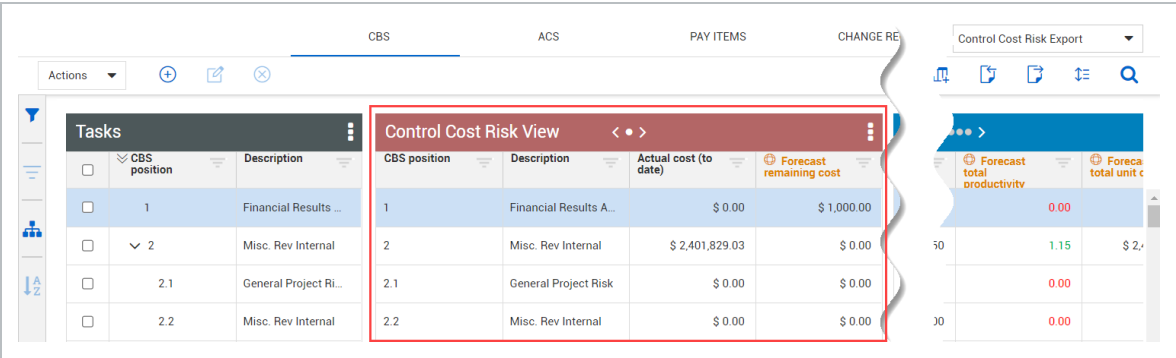

Select the Export icon to export the Control Cost Risk View data from Control.

Control / Workspaces

CBSACS

Control Cost Risk View

CBS position	Description	Actual cost (to date)	Forecast remaining cost
1	Financial Results A...	\$ 0.00	\$ 1,000.00
2	Misc. Rev Internal	\$ 2,401,829.03	\$ 0.00
2.1	General Project Risk	\$ 0.00	\$ 0.00
2.2	Misc. Rev Internal	\$ 0.00	\$ 0.00
2.3	Escalation/Conting...	\$ 0.00	\$ 0.00
2.4	Directs	\$ 705,957.35	(\$ 0.00)

T01-24.3 QA

View : Unsaved (Live forecast)

01/01/2024

Forecast unit cost	Forecast method
\$ 1,000.00	Current estimate
,401,829.03	Rollup
\$ 0.00	Manual (EAC)
\$ 0.00	Manual (EAC)
\$ 0.00	None
\$ 705,957.35	Rollup

Select Export: **CBS as CSV**.

\$

Export:

CBS as CSV


This page intentionally left blank.

LESSON 10 – SHORT INTERVAL PLANNING

SIP OVERVIEW

PROCESS OVERVIEW

Activities from the CPM Schedule show in the Short Interval Planning (SIP) view that are grouped, based on how the Plan view WBS is organized. Each activity can be planned daily by adding the specific steps, or tasks, to be completed. Red and blue bars represent the CPM planned duration. The green colored boxes represent the days that tasks for the step will be conducted.

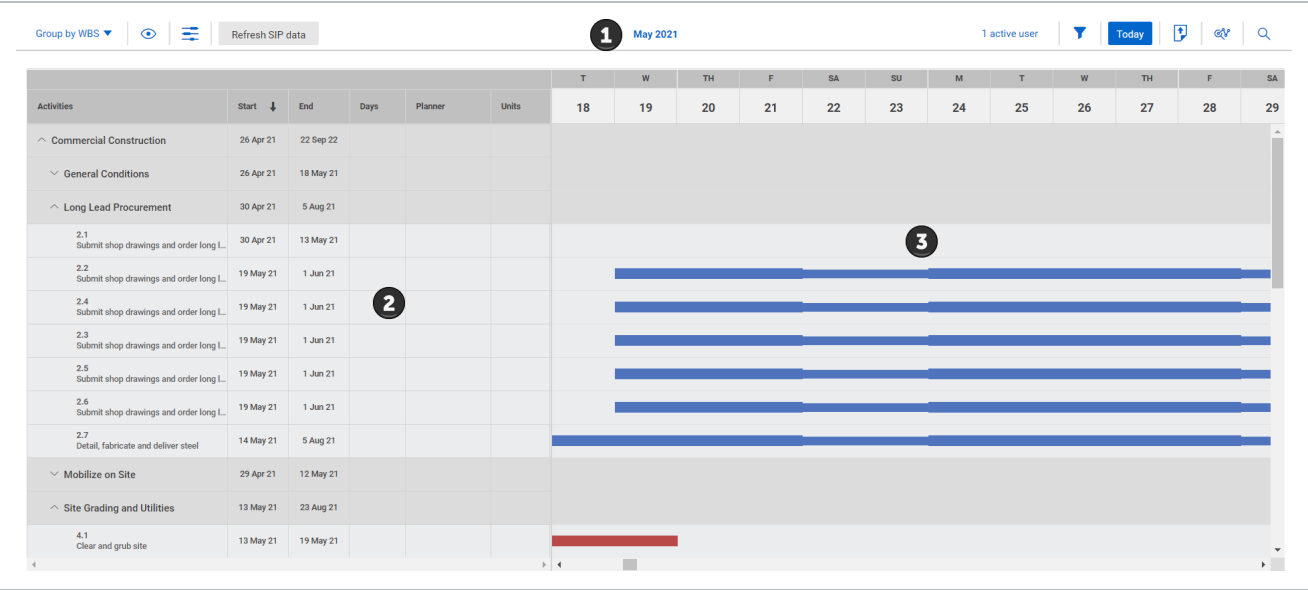

PLANNING STEPS/TASKS

Steps are created by selecting the Add icon on the row of the activity being planned out. After steps are added, you can then select the step to fill in information (description, dates, duration, and planner) for the task to be completed.

A2350 60% Design			11 Nov 21	16 Feb 22			9,000
Step 35		Add a step		11 Nov 21	17 Nov 21	5	None
Pressure Calculaitons			15 Nov 21	19 Nov 21	5	None	6,000
Slope Feed Calculations			10 Nov 21	16 Nov 21	5	Jordan Broo...	3,000

MILESTONES

Milestones are visually indicated on the SIP timeline and in the SIP activities. This provides clarity and reference to important dates when updating the short term plan on a project. When a blue milestone icon (◆) or a red critical milestone icon (◆) shows in the date timeline, you can click the icon to open a link and jump to the milestone in the step task chart.

SA	SU	M	T	W
12	13	14 ◆	15	16
<div><div>◆ 1.11</div><div>◆ 1.9</div></div>				

RESOURCES

When adding steps, you can assign predefined SIP resources to complete the steps or create and assign them in real time. If the resource does not exist in the schedule, enter a UoM and units, save the resource, and then apply it to steps while planning.

Add SIP Resource

Step 2

18 February 2019 - 22 February 2019

A3050 | Proposal Submissions

* SIP Resource name

Add and/or assign a SIP resource

UOM ⓘ

Units

0

Color assignment

Days	Units
18 February 2019	0
19 February 2019	0
20 February 2019	0
21 February 2019	0
22 February 2019	0

TOTAL: 0

0

0%

17 Feb 1918 Feb 1919 Feb 1920 Feb 1921 Feb 1922 Feb 1923 Feb 1924 Feb 19

Cancel


Save

SIP GENERAL NAVIGATION

SHORT INTERVAL PLANNING VIEW

When a schedule is ready for production, schedulers can move to the Short Interval Planning (SIP) view to begin planning out the day-to-day tasks involved with completing scheduled activities. This type of planning can be done in intervals of 17, 25, and 50 days based on a selected interval.

To open the Short Interval Planning view, in the project navigation menu click **Short Interval Planning**.

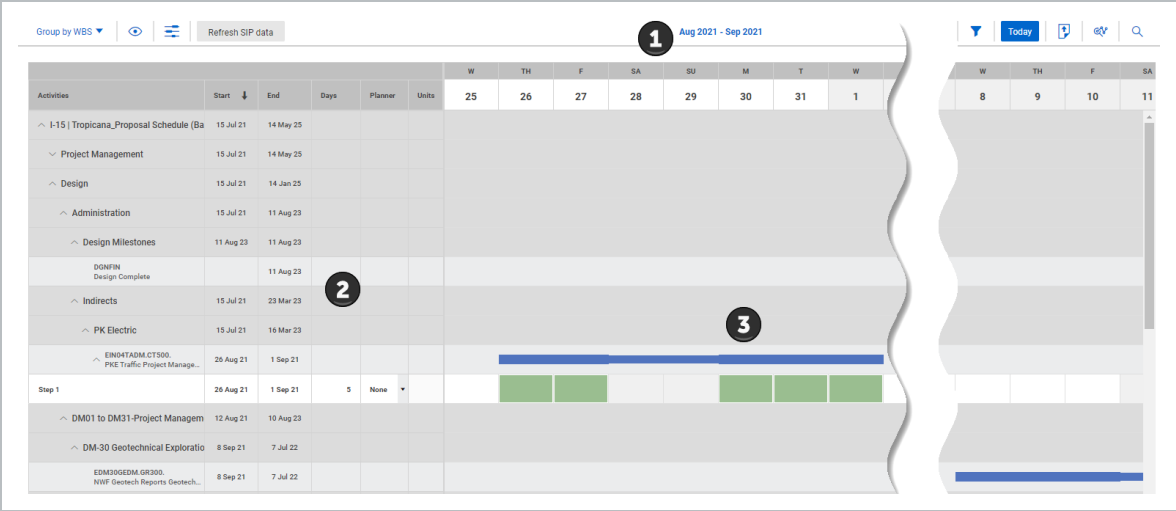


In the SIP view there are three primary sections:

1	Toolbar	Contains view adjustment settings such as, filtering, grouping, annotations, and date range.
2	Activities	Work package and activity structure are brought in from the Plan view. Tasks are further broken out in the SIP view.
3	Calendar	Shows a segment, or interval, of the schedule based on settings in the toolbar.

TOOLBAR - ICONS, FUNCTIONS, SETTINGS

GROUP BY


The Group by drop-down menu lets you see activities grouped together based on the option selected. This functionality provides flexibility to schedulers and execution planners in how they want to organize and assess tasks, resource utilization, and activity progress. You can also group activities and task by codes when knowledge tags are used on the project.



SIP FUNCTIONS

Description	Function
View options	Select metrics, view row numbers, annotations, color coding for the view, and resource histogram.
Detail level	Select the level of detail shown in the Activities section.
Filter	Opens the filter function to set parameters for the activities and tasks that show in the view.
Export	Export the current view to an Excel spreadsheet.
Zoom level	Sets the date range interval shown in the calendar.
Search	Search and find a specific task or step.

The SIP resource histogram lets you perform resource management at a short-term plan level that gives you another level of granularity when analyzing resources. The SIP resource histogram shows the assigned SIP resources for the project with functionality like the Plan view resource histogram. In the SIP view, click the **View options** icon, and then select **Resource histogram**.

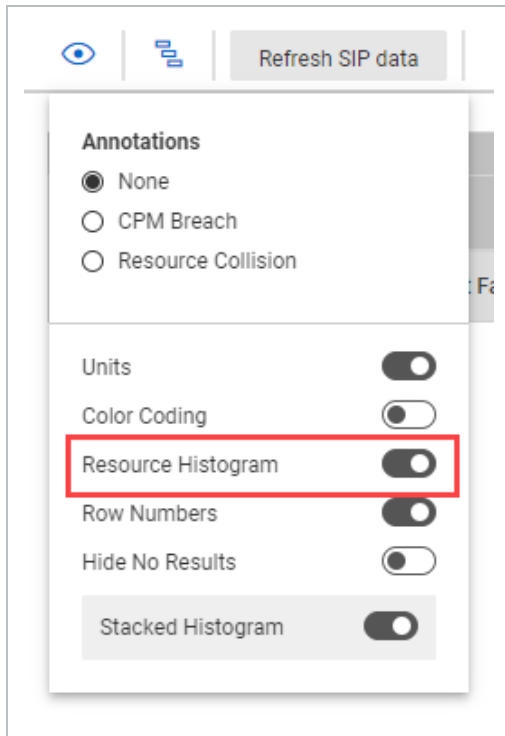

You can choose to view a single resource or select **Stacked Histogram** to show all SIP resources assigned to the specific date. You can also resize the grid and histogram areas to show more or less of the date time line.

You can add row columns to the SIP schedule by selecting the Row Numbers toggle.

Refresh SIP data

Annotations

☒ None

☐ CPM Breach

☐ Resource Collision

Units

Color Coding

Resource Histogram

Row Numbers

Hide No Results

	ID - Description	Start ↑	Finish
1	^ I-15 Tropicana_Proposal Schedule (Ba	15 Jul 2021	14 May 2025
2	^ Project Management	15 Jul 2021	14 May 2025
11	^ Design	15 Jul 2021	14 Jan 2025
2354	^ Procurement	3 Jan 2022	2 May 2023
2355	^ Permits	3 Jan 2022	5 Feb 2023
2356	CPWDENV.110 Obtain Demo Permits	3 Jan 2022	12 Jan 2022
2357	CPWDENV.220 Complete Bird Nesting Survey	3 Jan 2022	12 Jan 2022

ACTIVITIES - STEPS, ICONS, FUNCTIONS

In the Activities section, Schedule activities from the CPM are shown. Each of these activities can be broken into steps or tasks for more detail when planning field execution.

Activities	Start ↓	End	Days	Planner	Units
^ Pipeline	1 Jun 18 A	1 Nov 33			22,600
^ Design	1 Jun 18 A	10 Feb 23			17,600
^ Piping	1 Jun 18 A	7 Jun 22			17,600
^ A2340 30% Design	1 Jun 18 A	12 Jul 18 A			
Step 38	1 Jun 18	7 Jun 18	5	None	▼
Step 37	1 Jun 18	7 Jun 18	5	None	▼
Step 36	1 Jun 18	7 Jun 18	5	None	▼
Step 26	1 Jun 18	7 Jun 18	5	None	▼

Planning packages and activities are shown in a hierarchy. Planning packages group activities the same way as in the CPM schedule. Each activity line shows a planned start date, end date, activity ID, and the activity description.

When steps are defined, they show as a subordinate of the activity. An overview of the step details are noted that includes, start date, end date, duration, planner, and quantity.

To create a new step, click the **Add** icon. A step is created to input task details.



Hover over the step to show the available Action icons.




- **Zoom to start** moves the Gantt chart to one day prior to the step start date.
- **Add comment** opens a text box where you can type text and save a comment.
- **Add SIP resource** opens a SIP resource window that lets a planner assign an existing SIP resource or create a new SIP resource that can have units assigned to it.
- **Remove step** that when selected, deletes the step.


SNAP TO

In SIP view, you can select and move individual activity steps to a new date on the timeline. The Snap To feature lets you select multiple steps in an activity and move them all to new dates, maintaining the relationship relative to the initial step in the activity.

After you select the steps to move in the activity, click the **Snap To** icon to open the dialog box. Click in the **Snap to Start Date** field to open the calendar, and then select the new start date for the initial step. In the Include column, use the toggle to add or remove steps to move.

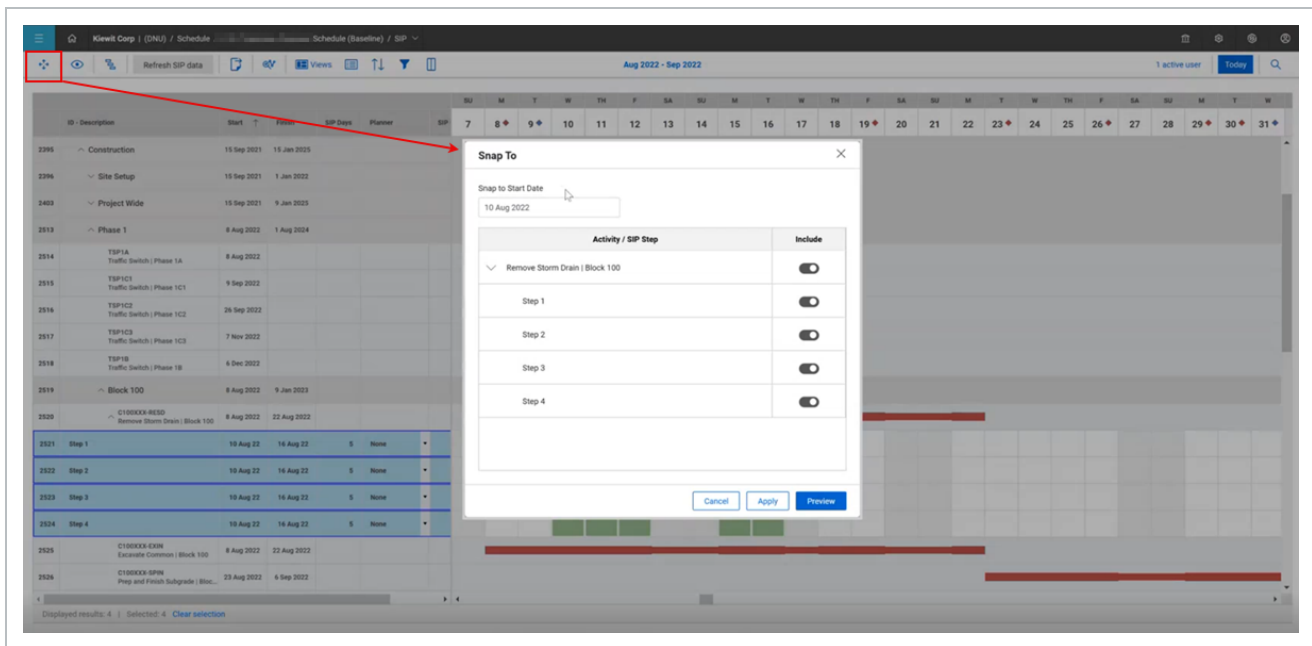

After selecting the new start date, click **Preview** to show an overlay of the steps with the new start date. You can save the changes in the preview or click **Back** to close the preview and open the dialog box again to make additional changes as needed.

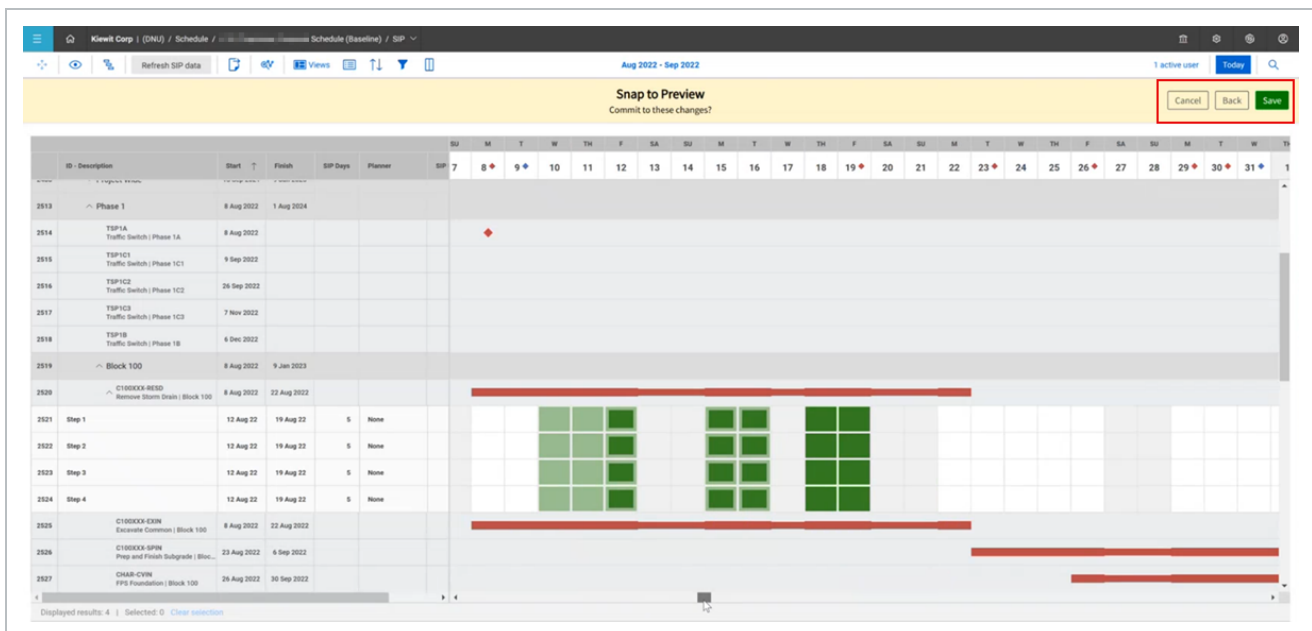

CALENDAR - VIEWS, ICONS, FUNCTIONS

The Calendar date range is adjusted in the header of the SIP view by selecting the Zoom level icon. In the calendar, there are two primary indicators, the blue and red CPM schedule activity bars, and the colored step bars.

Activities	Start ↓↑	End	Days	Planner	Units	T 31	F 1	S 2	S 3	M 4	T 5	W 6	T 7	F 8
^ A2340 30% Design	1 Jun 18 A	12 Jul 18 A												
Step 38	1 Jun 18	7 Jun 18	5	None	▼									
Step 37	1 Jun 18	7 Jun 18	5	None	▼									
Step 36	1 Jun 18	7 Jun 18	5	None	▼									
Step 26	1 Jun 18	7 Jun 18	5	None	▼									

The blue and red CPM schedule activity bars represent working days and non-working days. The thicker segments indicate working days in the activity's calendar and thinner segments are non-working days.

The colored step bars are the days that step is being worked. As a Planner you have the ability to click and drag the bars along the timeline to adjust the start date and end date of the step, and add or delete days for the step.

WEATHER SETTINGS

InEight Schedule has built in functionality to pull in weather data when a project location has been set up in Project Settings > **Project configuration**. When this function is setup, the weather shows in the date column header for the current day and a forecast for the next seven days.

F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26


You can click the weather icon to open the selected day's weather forecast. This data is powered by Open Weather.

LESSON 11 – REGISTER ITEMS

ORGANIZATIONAL REGISTER ITEMS

EVENTS REGISTER


Knowledge Library Register Items can be viewed by accessing the Knowledge Library, and clicking on the **Register** tab



From the Knowledge Library, items can quickly be edited using the following fields:

1	2	3	4	5	6	7	8	9			
Verified	Id	Type	Description	Mitigation	Probability	Schedule Impact	Cost Impact	Score	Activities	KA	Delete
	R3	Risk	▼ Risk of competing work in the fabyard	Identify overflow yards	High	High	High	16	2	KA	
	R2	Risk	▼ Risk of change in permitting authority	Schedule review with permitting office	Medium	High	Medium	12	5	KA	
	R7	Risk	▼ Risk of unknown soil conditions		Medium	High	Medium	12	2	KA	
	R4	Risk	▼ Risk of final route may not be known until 30 days before site access		Low	High	Medium	8	4	KA	
	O2	Opportunity	▼ Opportunity of identify third party engineering firm to support design		Medium	Low		6	5	KA	
	R1	Risk	▼ Risk of design rework due to first of a kind design resulting in engineering dela	Work with client to refine requirements prior to design	Low	Medium	Low	6	14	KA	
	R6	Risk	▼ Risk of weld issues causing rework		Low	Medium	Low	6	1	KA	
	R5	Risk	▼ Risk of local regulatory changing requirements		Very Low	Medium	Low	3	5	KA	
	O1	Opportunity	▼ Opportunity of use alternate pre-fab modules to accelerate delivery		Medium					KA	
	R10	Risk	▼ Risk of Hurricane due to weather resulting in destruction						1	INI	

Name	Description
Verified	Items can be either created directly in the Knowledge Library, or pushed from individual projects. Items pushed from projects shows here as unverified, and are not used as Smart Suggestion options in other projects until verified.
Type	This describes the type of register item, such as Risk, Opportunity,

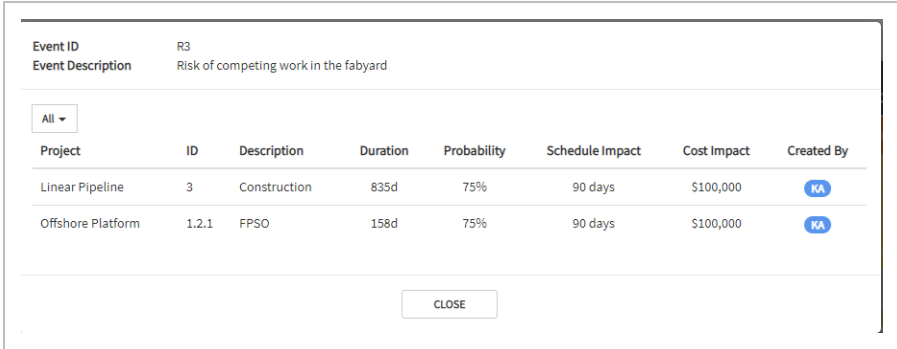Name	Description
	and Action Item.
Description	Items descriptions can be edited at any time.
Mitigation	Mitigation strategies can be captured here.
Probability/Schedule Impact/Cost Impact	Probability and impact can be reviewed and edited in a centralized view. The scoring here becomes the default score when the risk is applied to a project.
Score	Based on the probability and impact of items, a score is automatically generated.
Activities	<p>The number of times the register item appears schedules are shown here. Specific Project and WBS element appearances can be reviewed by clicking on the number. You can select the All drop-down to filter the list by project.</p> 
Created By	The name of the user that raised the register item.
Delete	Deletes the item.

REGISTER TYPES

Additional Register Types can be defined by selecting the **Register type** tab.

CPM SCHEDULES ACTIVITY PRODUCTIVITY RATES KNOWLEDGE TAGS CALENDARS REGISTER RESOURCES MACHINE LEARNING

Events Register **Register Types** Matrix Definition

Name	Prefix	Probability	Schedule Impact	Cost Impact	Positive Impact	Edit	
Opportunity	O	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		
Idea	I	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
Srini Test	SR	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		
Tatyana Test	TP	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		
Schedule Change Request	S	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
Test 9-16	TP	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>		
Type 1	TP	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
General	GEN	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
Threat	R	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>		
Issue	U	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>		

Click **Add Register Item** to create a new register item with a custom defined caption and code prefix.

CPM SCHEDULES ACTIVITY PRODUCTIVITY RATES KNOWLEDGE TAGS CALENDARS REGISTER RESOURCES

Events Register **Register Types** Matrix Definition

Name

Prefix

Probability

Schedule Impact

Cost Impact

Positive

Opportunity

O

☒

☒

☒

Idea

I

☐

☐

☐

Srini Test

SR

☒

☒

☒

Tatyana Test

TP

☒

☒

☒

Schedule Change Request

Test 9-16

Type 1

General

Threat

Issue

Add Register Type

Name

Cancel

Save

Click the **Edit** icon to define which qualifiers apply to that particular item.


Name	Prefix	Probability	Schedule Impact	Cost Impact	Positive Impact	Edit	
Opportunity	O	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		
Idea	I	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
Srini Test	SR	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		
Tatyana Test	TP	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		
Schedule Change Request	S	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
Test 9-16	TP	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>		
Type 1	TP	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
General	GEN	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
Threat	R	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>		
Issue	U	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>		

IMPORT AND EXPORT

You can import and export risks in the project register.


There are options for Oracle PRA – Pertmaster as well as Deltek Acumen. These are Excel formats that can also be generated outside of any tool and used for importing into Schedule.

The export file closely reflects what is exported from the Schedule Plan view. A color-coded key has been added in the upper left corner in the export file that shows you the required, optional, validated, and ignored records. Additional mapping tabs are also included at the bottom of the Microsoft Excel file.

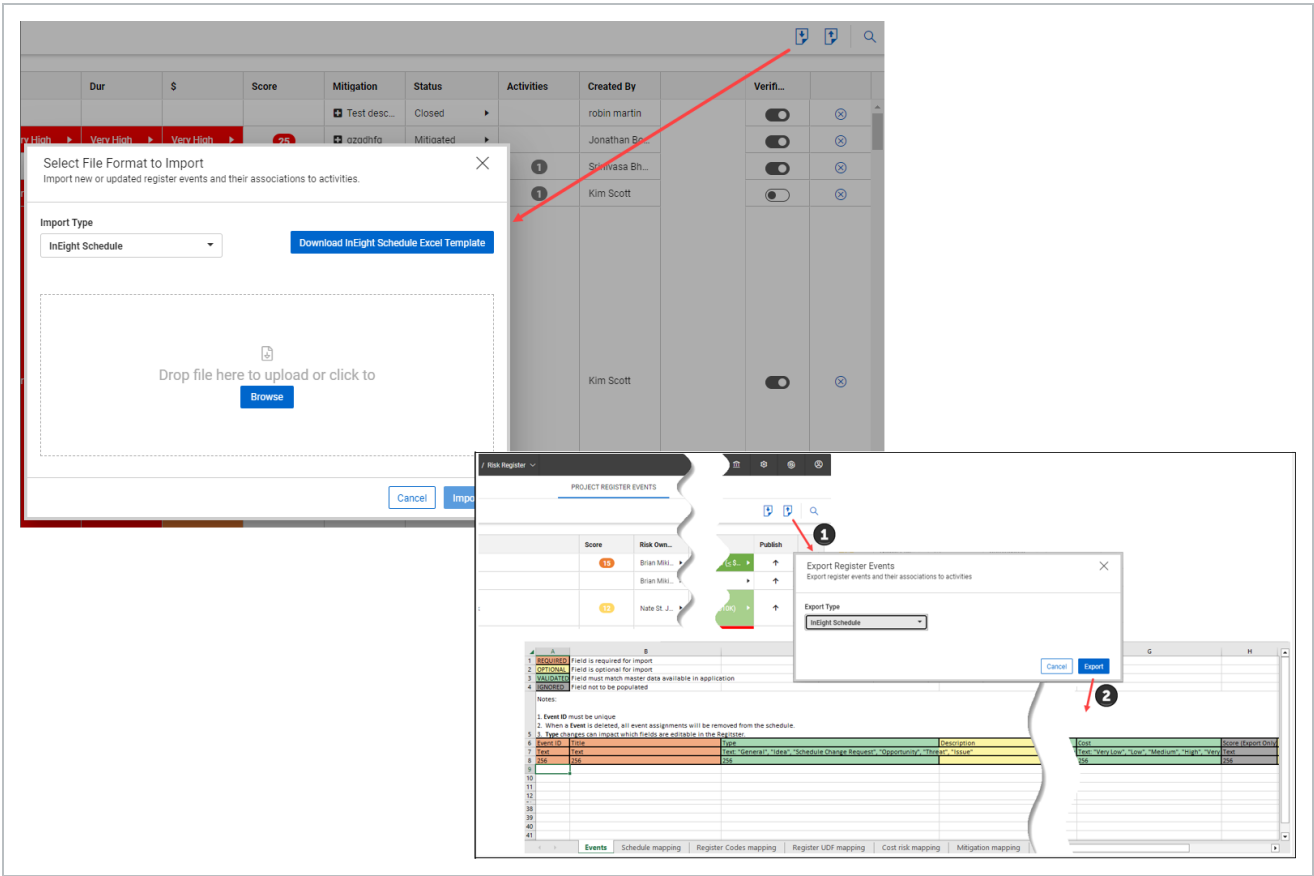

ADD REGISTER EVENT

You can manually add a register event to the project register. Select **Add Register Event** and define the event type and description.



Risk

of

Event

Cause

Effect

Risk of _____ due to _____ resulting in _____

ADD

CANCEL

FILTER

Select the **Filter** icon to enable filtering for the register view.

IMPORT/EXPORTADD REGISTER EVENT

Active	Id	Type	Description	Mitigation	Probability	Schedule Impact	Cost Impact	Score	Markup	Basis		Publish	Delete
<input type="checkbox"/>													

MATRIX DEFINITION

Qualifiers applied to register items can have the Probability percentage, schedule impact, and cost impact updated to reflect your organization’s preferred values. This becomes the default matrix when creating a new project.

Events RegisterRegister TypesMatrix Definition


Description	Probability	Schedule Impact	Cost Impact	Color
Very Low	10%	≤ 11 days	≤ \$13	
Low	25%	≤ 30 days	≤ \$10,000	
Medium	50%	≤ 60 days	≤ \$100,000	
High	75%	≤ 90 days	≤ \$1,000,000	
Very High	95%	≤ 180 days	≤ \$10,000,000	

PROJECT REGISTER EVENTS

The Project Register houses all events pertaining to the project. These events are used to notify schedulers of potential project ideas, changes, opportunities, threats, and issues.

EVENT TYPES

There are several Event types available in the Project Register. Of the available events, the following three are focused on: Idea, Opportunity, and Threat.

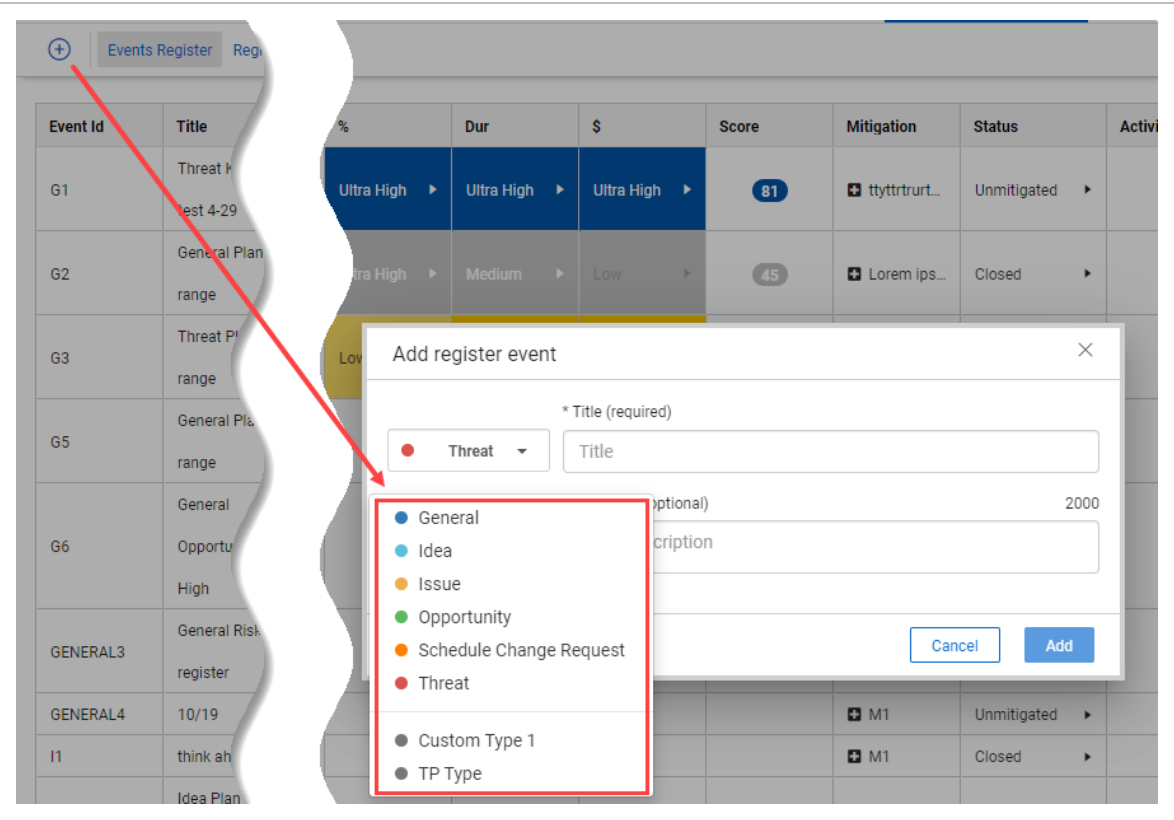

IDEA

Ideas are events that do not necessarily yield a positive or negative schedule impact. Often, ideas are schedule notes regarding an activity. They might have a favorable or unfavorable outcome in the schedule and can be replaced with a Threat or Opportunity event if circumstance dictates it.

OPPORTUNITY

Opportunities are events with the potential to yield a favorable schedule outcome such as time savings or cost reduction.

THREAT

Threats are events that may occur, posing possible schedule delays or increased cost on the project.

EVENT VALUES

When assigning an event to an activity, there are three additional fields to be populated depending on the type of event: Probability, Duration and Cost. These fields vary from event type to event type and not always need to be filled out. However, it is in the best interest of the team input as much information as possible for the Risk Analysis to be conducted.

 Lack of specs leads to re-design				SCORE
ID	Prob.	Dur.	Cost	
R5	%			

- **Probability:** Likelihood of the listed event to occur and impact the schedule.
- **Duration:** Estimated days increased or decreased due to the event
- **Cost:** Estimated cost associated with the event
- **Score:** System generated value based on the Probability, Duration, and Cost Factors involved

EVENT VALUES

EVENTS LIBRARY

In the Project Register Events Library, all events on the project and from the Knowledge Library are listed. These events can be selected and assigned to activities.

If a new event is to be created, the Project Register has an input field for new events.


CREATE AN EVENT

1. To open the Project Register Events Library from the Markup Screen, click on the **Sticky note** icon of the activity or planning package the event will be associated to.


NOTE

This icon might be red or yellow depending on the markup provided.

2. A new window opens with the Events Library.

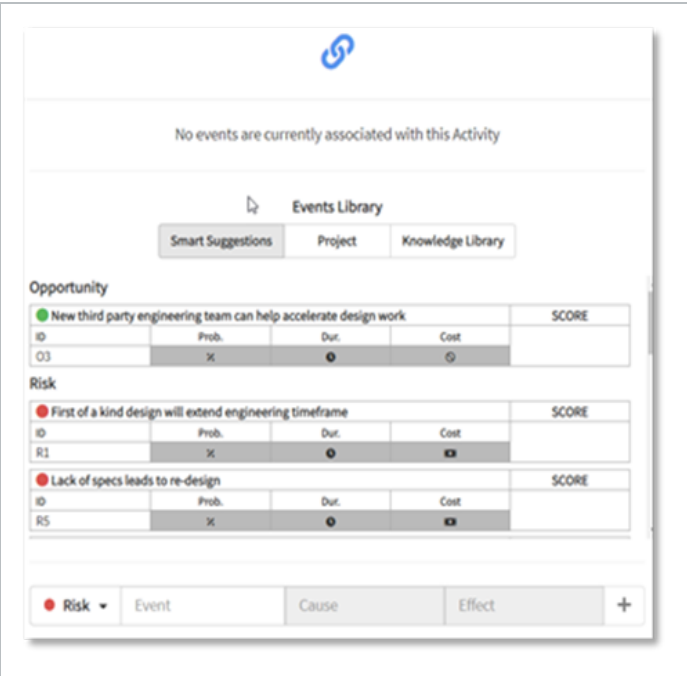

- 3. At the bottom of the Events Library is the **Event Creation** function.
- 4. Click the **Event Type** drop-down menu to select from Risk, Opportunity, Issue, Idea and Schedule Change Request.

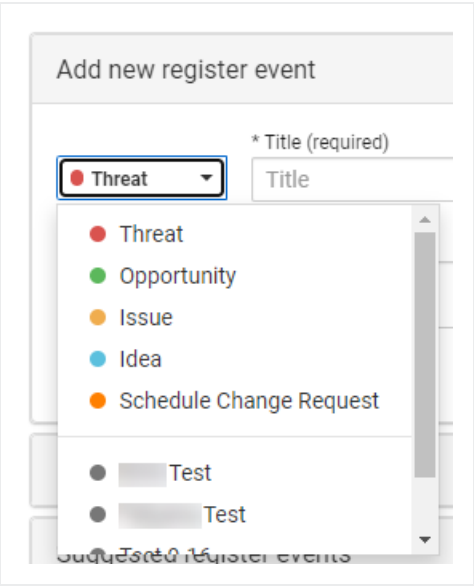

- 5. Fill out the Event, Cause, and Effect fields. As these fields are populated, a summary of the event is shown below.

Risk

Additional Cure days

Cold Temperatures

Schedule Delay

+

Risk of Additional Cure days due to Cold Temperatures resulting in Schedule Delay

- Click the **Add** icon.
- Your selection now appears at the top of the window. Fill out the remaining fields (i.e. Risk - Probability, Duration, and Cost).

Risk

✖ Risk of Additional Cure days due to Cold Temperatures resulting in Schedule Delay

SCORE

ID	Prob.	Dur.	Cost
R2	%	!	\$

Risk

✖ Risk of Additional Cure days due to Cold Temperatures resulting in Schedule Delay

SCORE

ID	Prob.	Dur. ①	Cost	
R2	50%	30d	\$10K	6

- Close when finished.

RISK RANGE SCORING

The score calculation for risk range scoring is: Probability "%" times the greater of (Duration "Dur" range OR Cost "\$").

5 point = Very Low to Very High

7 Point = Extremely Low to Extremely High

9 Point = Ultra Low to Ultra High

Range	Score
Ultra Low	1


Range	Score
Extremely Low	2
Very Low	3
Low	4
Medium	5
High	6
Very High	7
Extremely High	8
Ultra High	9

ASSIGN REGISTER ITEMS

Register items consist of risks, opportunities, change orders, and any other qualifiers that your organization has defined.

ASSIGN A REGISTER ITEM

1. Go to the Plan view from the first level drop-down menu in a project, and then select a WBS element.

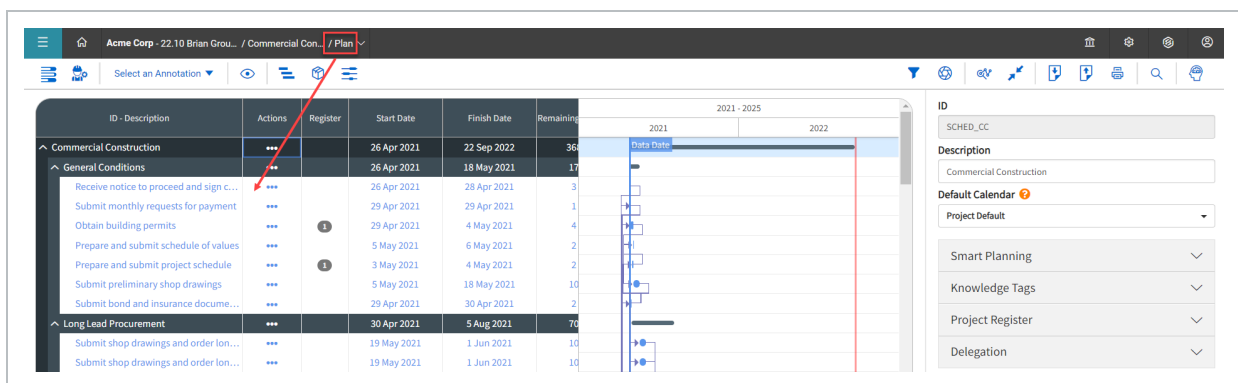

2. In the rightmost panel, expand project register, and click **Add event**. This causes a dialog box to open, showing any currently existing register items. New items can be added by selecting the

item type, and typing in the event, cause, and effect.

Submit shop drawings and order long lead items - electric
2.5

Add new register event

Threat

* Title (required)
Title

Description (optional)
Enter description


Clear Add

Existing register events

Suggested register events

Add Event

3. Click the icon to add the register item to the WBS element. Enter a probability, schedule impact, and cost impact to quantify the event. The available quantifiers are set up by your administrator based on the register item type.



Risk

✖ Site access delays

ID

Prob.

Dur.

Cost

SCORE

R2

50%

30d

\$100K

9

Events Library

Smart Suggestions

Project

Knowledge Library

Risk

● Site access delays

ID

Prob.

Dur.

Cost

SCORE

R1

%

⌚

📄

● Risk

Event

Cause

Effect

+

CLOSE

- An item has now been added to this WBS element.

NOTE

When the Register column is in the gantt view there is an indicator on the line, telling other users that the WBS element has register items associated with it.

Interior	25 Mar 21 26 Aug 21	155	111	0%		...	03 Dec 21	
Floor 1	25 Mar 21 26 Aug 21	155	111	0%		...	03 Dec 21	
Floor 2	25 Mar 21 31 May 21	68	48	0%		...	07 Sep 21	
Floor 3	14 May 21 20 Jul 21	68	48	0%		...	27 Oct 21	
Electrical Rough-in	14 May 21 27 May 21	10	10	0%	0	...	03 Sep 21	2
Finishes - Drywall	11 Jun 21 03 Jul 21	16	16	0%	0	...	09 Oct 21	1
Finishes - Final Paint	13 Jul 21 20 Jul 21	6	6	0%	0	...	27 Oct 21	
Finishes - Lighting Inst.	05 Jul 21 12 Jul 21	6	6	0%	0	...	19 Oct 21	
Plumbing Rough-in	28 May 21 10 Jun 21	10	10	0%	0	...	17 Sep 21	
Structure	15 Dec 20 28 Jun 21	196	140	0%		...	05 Oct 21	


11.1 INEIGHT SCHEDULE WORKFLOWS

INEIGHT SCHEDULE - FOCUSED WORKFLOW


InEight Inc. | Release 25.1

Page 279 of 291

This workflow shows the modules (or views) that make up the InEight Schedule application. It lists the key functions of each view and the relationships the views have to each other.

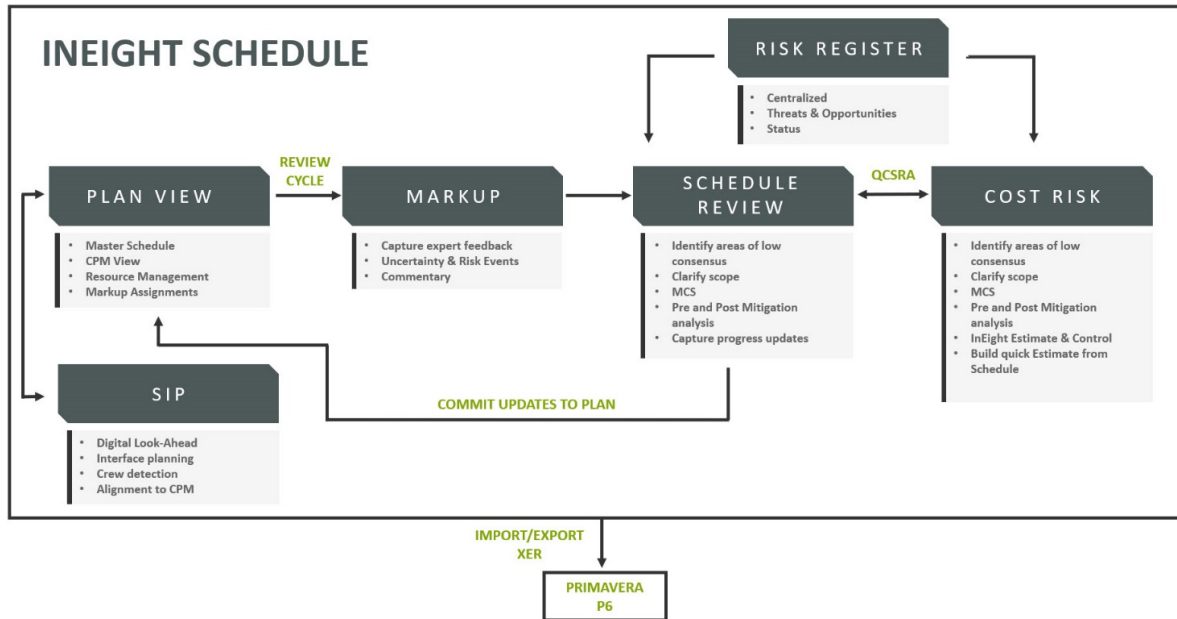


INEIGHT CONTROL GENERAL WORKFLOW

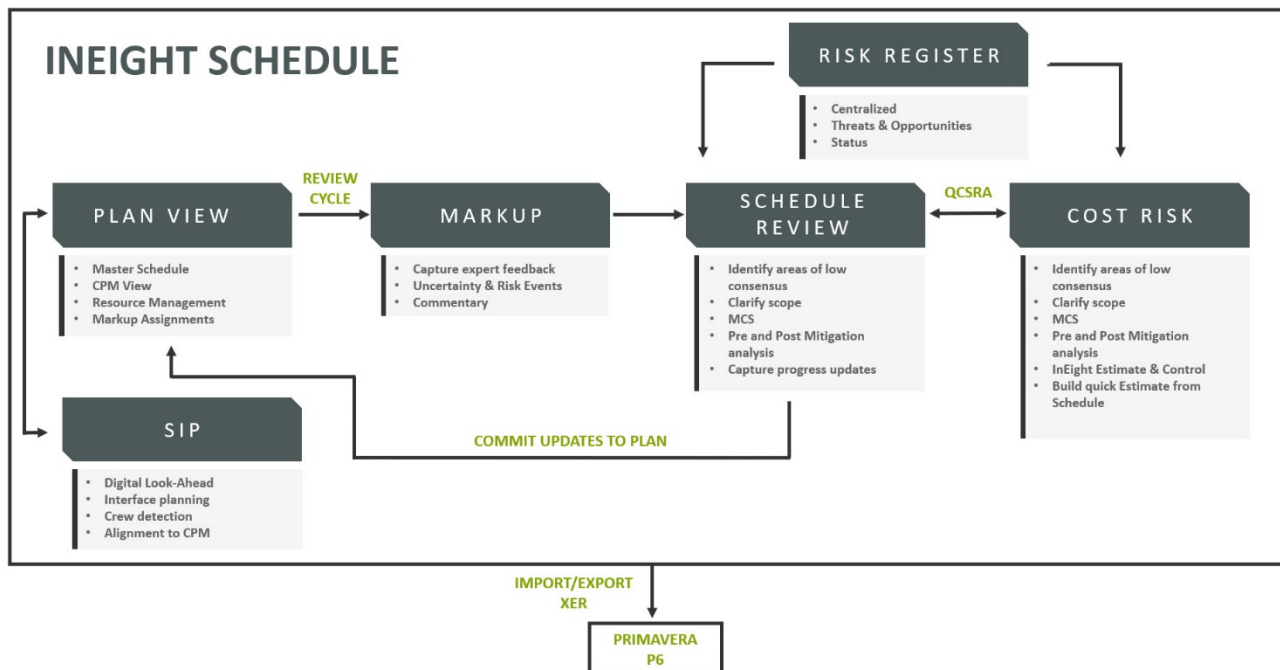

SCHEDULING & SHORT INTERVAL PLANNING WORKFLOW


This interactive workflow looks at the key functions of InEight Schedule through the lens of a typical scheduling business process. As you click on each business process step, the workflow highlights the key functions involved, along with the InEight Schedule view you would use for that step.

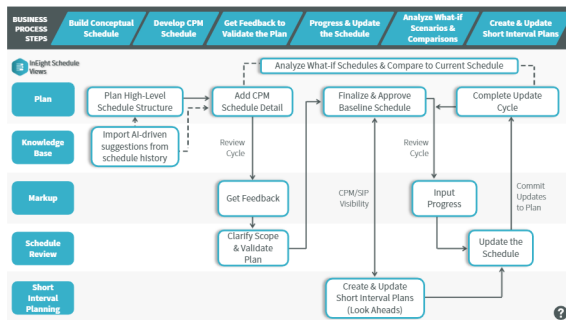

SCHEDULING & SHORT INTERVAL PLANNING BUSINESS PROCESS

SCHEDULING BUSINESS PROCESS WORKFLOW

Similar to the previous workflow, this workflow also diagrams out the typical steps involved in a scheduling business process, but includes additional detail, including touchpoints between InEight Schedule and other InEight applications.

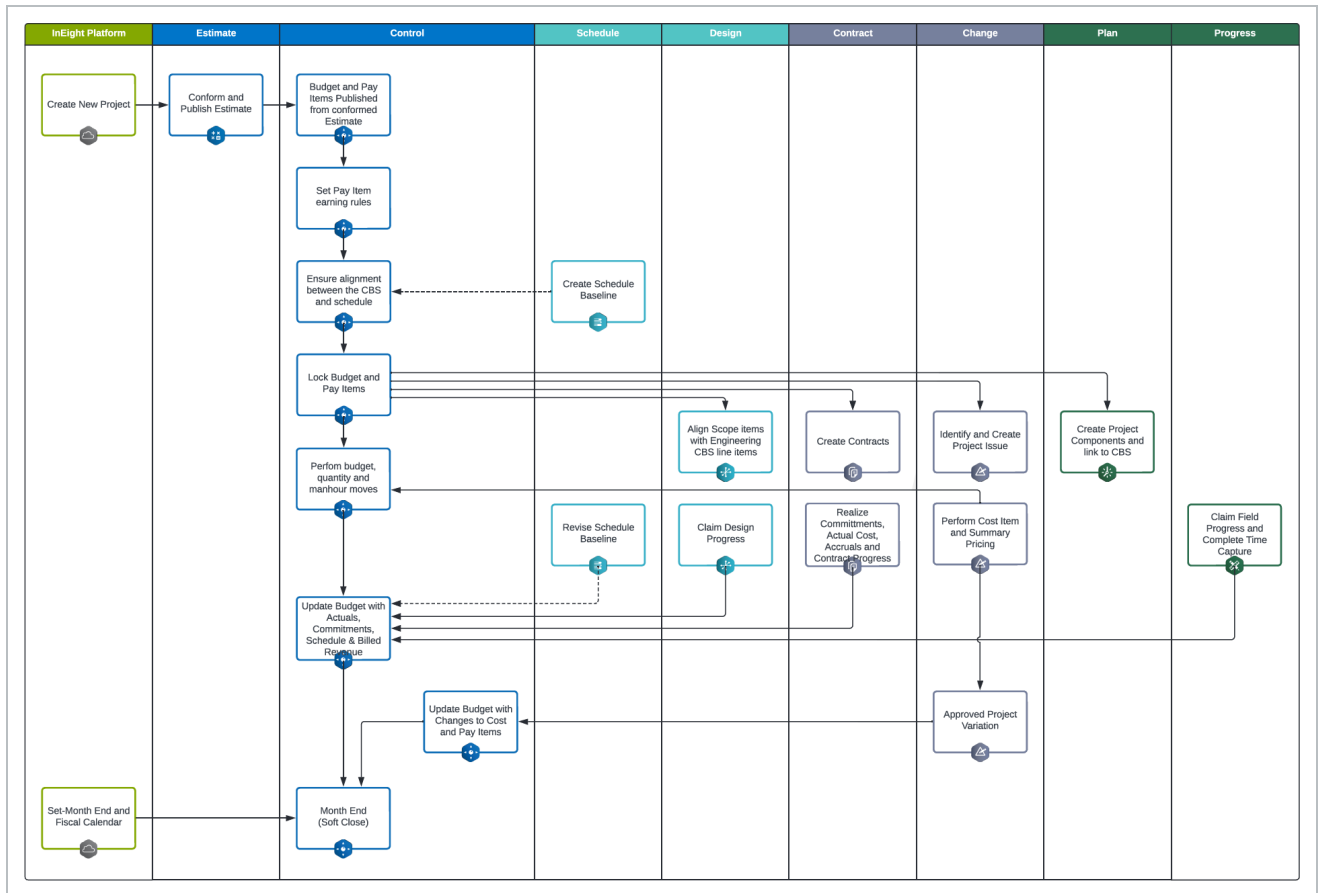

11.2 SCHEDULE FREQUENTLY ASKED QUESTIONS

How can I get schedule changes in and out of InEight Schedule?

As you manage a detailed schedule within the Plan view of InEight Schedule, you will need to make adjustments and changes. You may need to import change information from other sources, or export schedule changes to use in other applications.

You can import and export schedule data using the Import and Export options in the right toolbar within the Plan view.

For import, you have the options to import WBS items, activities, logic, codes, user-defined fields and resource assignments, using an Excel import file.

#	A	B	C	D	E	F
4	IGNORED	Field not to be populated				
Notes:						
1. To update a logic link Type , you must delete the existing logic link and create a separate row for the new logic link type						
2. Lags can be both positive and negative						
6	Predecessor Activity ID	Predecessor Activity Description	Successor Activity ID	Successor Activity Description	Lag	Type
7	Text	Text	Text	Text	Numeric	Text: "FS", "FF", "SF", "SS"
8	256	256	256	256	2	FS
9	A1430	Install Spool 3	A1540	Complete Line A	0	FS
10	A1530	Start Line A	A1410	Install Spool 1	0	SS
11	A1510	Spool 5	A1520	Spool 6	0	FS
12	A1500	Spool 4	A1510	Spool 5	0	FS
13	A1490	Spool 3	A1500	Spool 4	0	FS
14	A1290	Mechanical O	A1270	Mechanical B	0	FS
15	A1200	Electrical "L"	A1190	Electrical "B"	0	FS
16	A1280	Mechanical L	A1290	Mechanical O	0	FS
17	A1260	Mechanical S	A1230	Electrical "K"	0	FS
18	A1200	Electrical "L"	A1210	Electrical "O"	0	FS
19	A1230	Electrical "K"	A1240	Electrical "S"	0	FS
20	A1310	Mechanical K	A1260	Mechanical S	0	FS
21	A1270	Mechanical B	A1190	Electrical "B"	40	FF
22	A1290	Mechanical O	A1210	Electrical "O"	40	FF
23	A1280	Mechanical L	A1200	Electrical "L"	40	FF
24	A1260	Mechanical S	A1240	Electrical "S"	40	FF
25	A1310	Mechanical K	A1230	Electrical "K"	40	FF


WBS	Activity	Logic	Codes	WBS UDFs	Activity UDFs	Resource Assignments	+	-	x
-----	----------	-------	-------	----------	---------------	----------------------	---	---	---

For export, you have several options, including:


- Primavera P6 XER
- Excel Export
- MS Project MPP

How can I manage my resources in the Schedule Plan view?

From the Plan view of InEight Schedule, you can assign resources to an activity by selecting the **Actions** ellipses and selecting **Assign resource assignments**. This opens a window where you can select from available resources or add new ones to the activity, along with productivity and cost information.

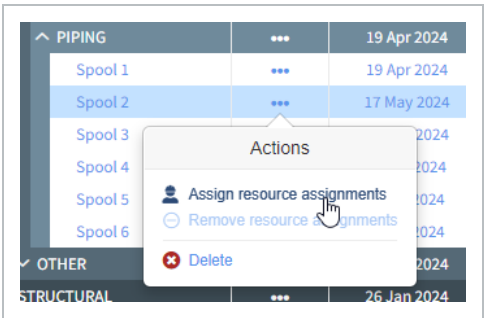

Once added, you can review your resources' planned and actual productivity by turning on the Resources Histogram from the **View Options** menu.

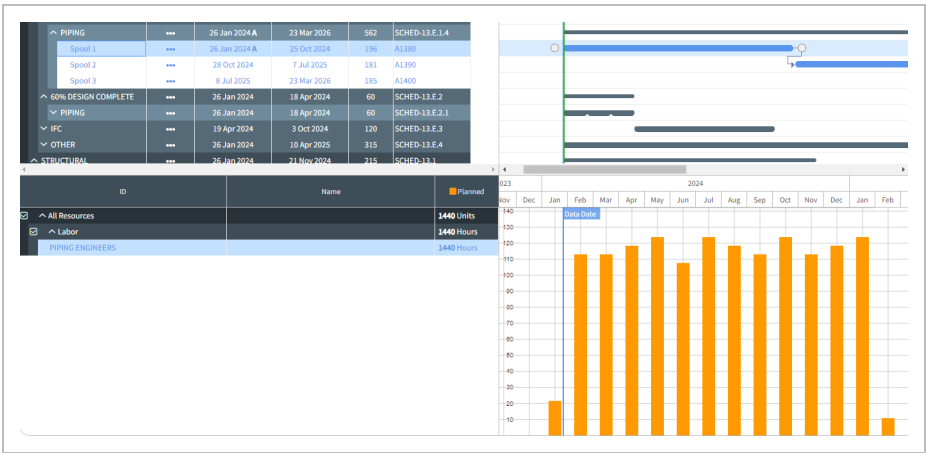








I’ve set up groupings, filters, and column sets in my Plan view. How can I save them?

If you’ve customized your Plan view by applying groupings, filters or columns sets, you can save the view by selecting **Views** from the left toolbar and selecting **Save current view**.


How can I compare multiple schedules?

To compare multiple schedules, you can take snapshots and designate which ones to compare on the Baseline/Snapshot Management slide-out panel in the Plan view. You access this slide-out panel from the right toolbar.

1 active user




Baseline/Snapshot Management


Active Baseline 


Baseline based on Industrial Plant - Baseline: Laura Koonce - 4 Apr 2024

Revert to default


Snapshot 1 

Snapshot based on Snapshot 05APR24: Laura Koonce - 10 Apr 2024

Unassign schedule 

Snapshot 2 

Snapshot based on Industrial Plant - What-If Sch... Laura Koonce - 10 Apr 2024

Unassign schedule 


Set or overwrite snapshot above, or [Create copy of current schedule](#)

	Current Schedule	Active Baseline	Snapshot 1	Snapshot 2
Data Date	26 Jan 2024	26 Jan 2024	15 Feb 2024	9 Feb 2024
Number of Activities	75	66	75	74
Start Date	26 Jan 2024	26 Jan 2024	26 Jan 2024	26 Jan 2024
Finish Date	14 Aug 2026	14 Aug 2026	3 Sep 2026	28 Aug 2026
Remaining Duration	666 days	666 days	666 days	666 days
Average Float	184 days	104 days	184 days	182 days


Once designated, you can select which snapshots to include in your view by selecting them in the View Options menu.

Baseline/Snapshots


Active Baseline



Snapshot based on Snapshot...




Snapshot based on Industrial...



You can then compare the activities of each schedule next to each other in the Gantt chart.

PIPING	...	26 Jan 2024 A	23 Mar 2026	562	SCHED-13.E.1.4
Spool 1	...	26 Jan 2024 A	25 Oct 2024	196	A1380
Spool 2	...	28 Oct 2024	7 Jul 2025	181	A1390



See Also:

[Baseline/Snapshot](#)


How can I store past schedules to be used as templates?

You can save your entire schedule, or portions of it, to the Knowledge Base for future use. To save the entire schedule, click the Actions ellipses on the highest level (first row) of the schedule and select **Publish to the knowledge base**.


Nate Co. / Schedule						
CPM SCHEDULES ACTIVITY PRODUCTIVITY RATES KNOWLEDGE TAGS CALENDARS REGISTER RESOURCES MACHINE LEARNING						
Schedules ↓						
	Schedule ID		Start	Finish	Data Date	Verified
30% Design Complete - MST	SCHED		26 Jan 2024	23 May 2024	26 Jan 2024	●
60% Design Complete - MST	SCHED-8		26 Jan 2024	8 May 2024	26 Jan 2024	●
AIAL_DP001_BL00_REVC_23 Feb 24 - Cos...	DP.001.93343.4.501-3		31 Oct 2022	15 Feb 2029	23 Feb 2024	●
Chassis - Body Builder	SCHED-1		26 May 2021	8 Sep 2021	26 May 2021	●
Chassis Builds	SCHED-2		26 May 2021	26 May 2021	26 May 2021	●
Combined Cycle Estimate Schedule	CC Power Plant Bid		2 Oct 2023	20 Oct 2026	2 Oct 2023	●
Commercial Building	SCHED-3		12 Jun 2018	17 Feb 2021	12 Jun 2018	●
IFC - MST	SCHED-9		19 Apr 2024	19 Aug 2024	26 Jan 2024	●
Industrial Plant Project	SCHED-10		26 Jan 2024	28 Aug 2026	9 Feb 2024	●
KIE Haisla Bridge Replacement - LIVE	KIEHBR		20 Apr 2021	23 Jul 2024	21 May 2021	●
Linear Pipeline	SCHED-4		12 Jun 2018	25 Apr 2023	12 Jun 2018	●

You can perform this same function at any WBS level.

Published schedules (or portions of a schedule) are stored on the CPM Schedules tab in the Knowledge Base. An Administrator must review the schedule and mark it as Verified prior to it being used.



In existing schedules, at the WBS level, you can add portions of a schedule from the Knowledge Base. This is done from the Iris panel, under the Smart Planning section.

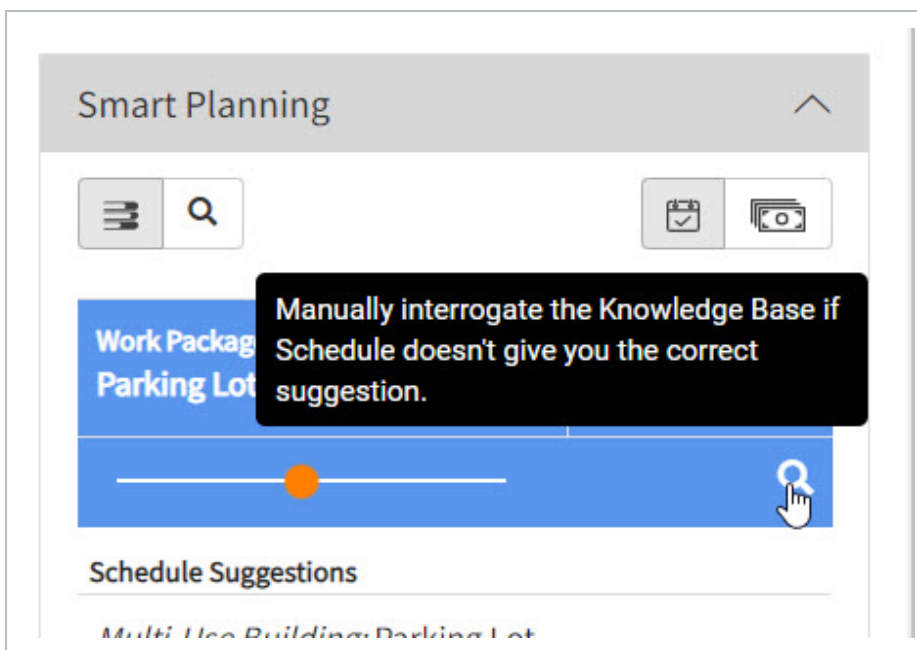

See Also:

[Knowledge Base](#)

Can InEight Schedule integrate with other InEight applications?

InEight Schedule currently includes import/export functionality to share schedule data between applications via Microsoft Excel and .XER files. Development is underway to more tightly integrate InEight Schedule with other applications including InEight Estimate and InEight Plan.

What is the difference between Short Interval Planning (SIP) resources and resources?

Resources used for scheduling in the Plan view are for considering durations, productivity and costs for the entire CPM schedule for the project and are assigned at the higher activity level.

SIP resources represent the labor, equipment and materials tracked on look-ahead schedules managed by the field team. These look-ahead or short interval plans break schedule activities down into the day-to-day steps to execute the work in the field and track the SIP resources at the step or task level.

Is there a standardized fill-down option in InEight Schedule?

Yes, there is a fill-down feature for calendars, codes and resources, where you can specify a value at a summary level and have it apply to the child elements below it. You access the Fill down feature by clicking on the Actions ellipses of your summary level item.

See Also:

[Project Resources](#)

How do we manage multiple schedules with external relationships?

InEight Schedule does not support a program level of schedule management, where distinct schedules for different projects are managed under a single program and have external relationships between them. You can still manage multiple schedules with relationships between them, however, by importing the individual schedules into one “master” schedule and then establishing logic links between them as needed.

Use Case 1: InEight Schedule only

Publish each schedule to the Knowledge Base, then add WBS items representing each schedule and import the corresponding schedule from the Knowledge Base for each WBS item using the Smart Planning feature.


Use Case 2: InEight Schedule and Primavera

Select multiple schedules in Primavera and export them as a single structure in an XER file. Then import the .XER file into InEight Schedule, where it becomes a single “master” schedule structure containing the individual schedules exported from Primavera.

Can we copy/paste data from the InEight Schedule Plan view to Excel?

You can send data from the InEight Schedule Plan view to Excel using the **Column Set Builder** and the Export feature. From the Column Set Builder Menu, select the Column Set Builder to specify

what columns you would like to include for exporting to Excel.

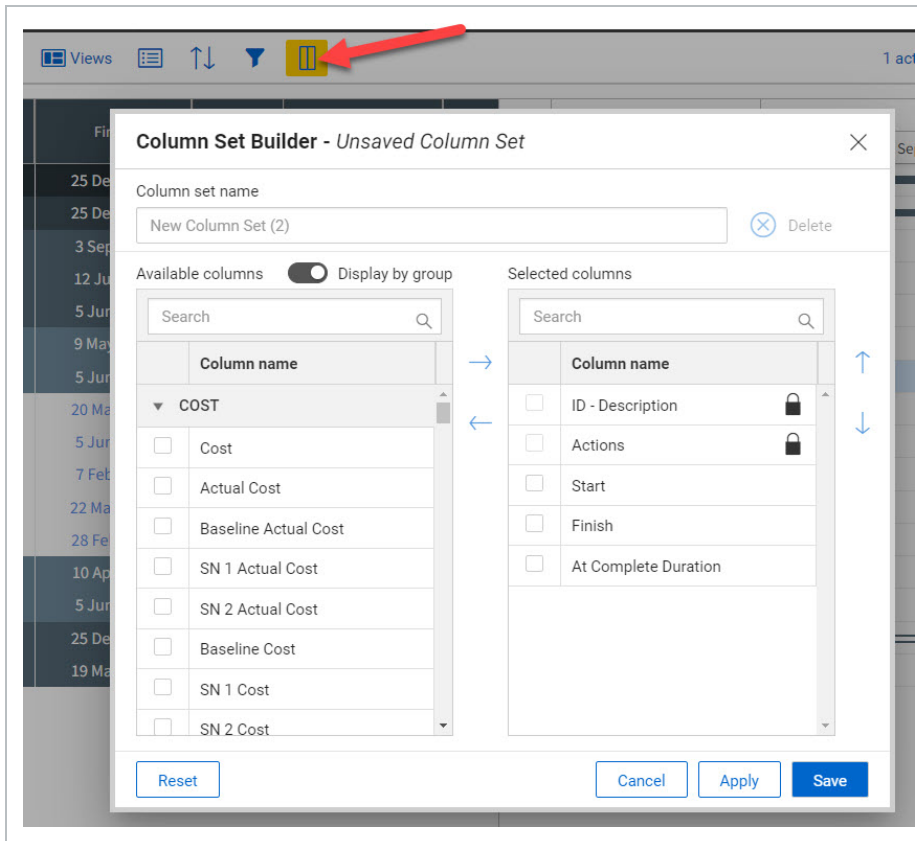

Then, you can export that set of columns and their related data to Excel, by selecting **Export** on the right toolbar.

How do I capture progress from field personnel?

InEight Schedule includes a review cycle feature that can be used to obtain progress updates from the field.

See Also:

[Input Progress](#)


Are my resources the same resources as are in InEight Control/Cloud Platform?

The resources used in InEight Schedule (both at the Knowledge Base and Project levels) are distinct from the resources used in other InEight applications. Any coordination of resources used by the different apps would therefore need to be managed via internal processes within your organization. For example, your organization could define a standard set of resources used by the company and share that list out to the various project teams to import or manually input within


each application.

How do I update my InEight Schedule from an .XER file?

You can import schedule data via an .XER file using the Import schedules function on the left toolbar of the Project List page.

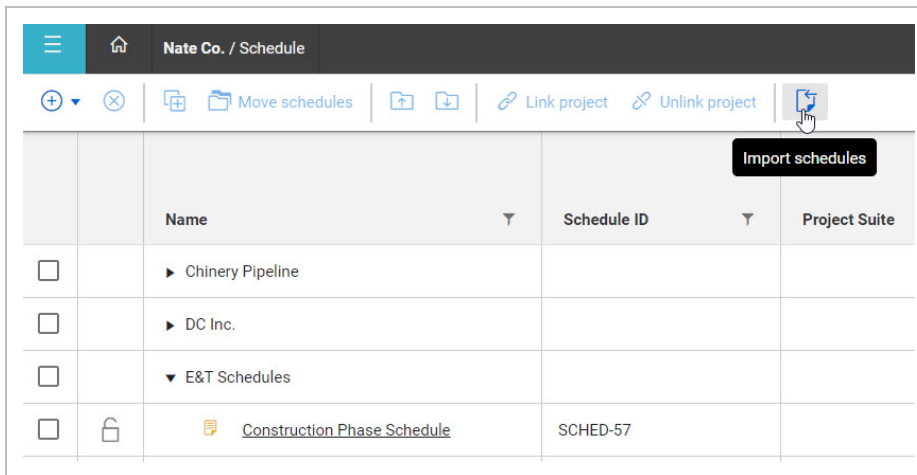

Note that when importing you can import historical data from another schedule to bring in additional information including planners, assignments, and short interval plans.

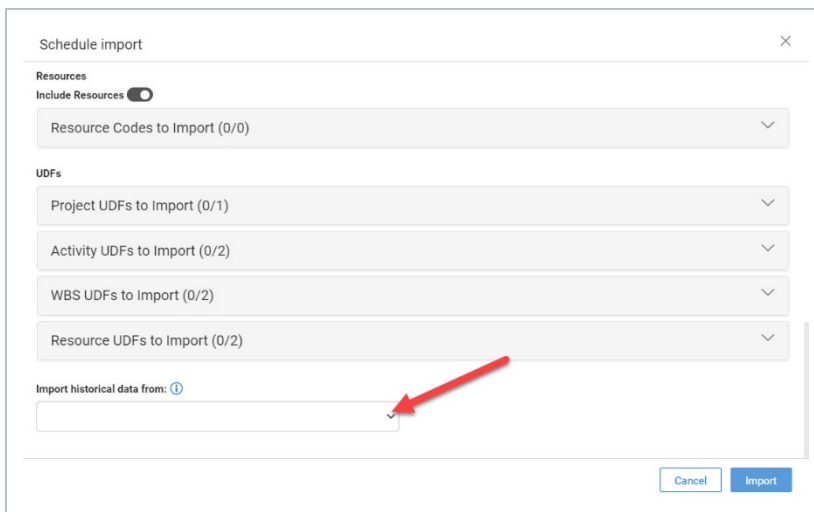


How do I get access to a schedule from within the InEight Cloud Platform?

You can access InEight Schedule from the InEight Cloud Platform, either from an organization or project level. If you select Schedule from the Organization home page, it takes you to the Project List page within InEight Schedule, where you can then select your schedule as needed. If you

select Schedule from a Project home page, it will take you to InEight Schedule, and will be filtered down to that specific project’s workspace on the Project List page, making it easier to get to the schedules related to the project.

How do I link my schedule workspace to a project in InEight Platform? In the future, will schedule workspaces be created automatically when an InEight Platform project is created?

From the Project List page of InEight Schedule, you can link a schedule workspace to a project in InEight Platform by selecting Link project on the left toolbar.



In the future, the schedule workspace will be created automatically when an InEight Platform project is created.

See Also:

[Advanced Work Packaging](#)
